Nandini Ghosh, IAS
Senior Special Secretary

URBAN DEVELOPMENT &
MUNICIPAL AFFAIRS DEPARTMENT
GOVERNMENT OF WEST BENGAL
"Nagarayan", DF - 8, Sector- I,
Salt Lake, Kolkata, 700 064
Phone: (033) 2321 1121
Email: nandinighosh.jsudma@gmail.com

Memo No. 634-Sr. Spcl. Secy (NG) **Date: 22.12.2025**

To,
The Executive Director (Technical),
National Mission for Clean Ganga, Ministry of Jal Shakti, GOI,
(Department of Water Resources, River Development & Ganga Rejuvenation)
1st Floor, Major Dhyan Chand National Stadium, India Gate, New Delhi-110002.

Subject: Submission of Quarterly Progress Report for the period from **July 2025 to September 2025** in compliance with the order of Hon'ble NGT under OA – 200/2014.

Sir,

With reference to the above subject, I am directed to attach herewith an Updated Report on OA 200 from West Bengal for the period from **July 2025 to September 2025**. The Table of Contents of the Report is as under

Sl. No.	Content	Annexure No.
1.	Main Report	Nil
2.	Good work and Efforts	I
3.	Sewage Generation Report	II
4.	STP Progress Report up to Sep 2025	III
5.	Details of Drains	IV
6.	Water Quality Report of WBPCB	A
7.	Compulsory Site Inspection Report, KMDA for Sep 2025	B
8.	Report from SUDA	C
9.	Report from P&RD	D
10.	Report from Forest Department	E
11.	Capacity Utilization, Sept, 2025	F

It may kindly be noted that Annexure-I is an elaborate Report on Monitoring and Review of the ongoing works indicating the all-out efforts taken by the State to curb and arrest pollution in the River Ganga. It is to be most humbly stated that due to sustained efforts in Solid and Liquid Waste Management in the Ganga basin, the Water Quality of Ganga has improved substantially and the River Ganga is now placed in the lesser Priority Category. Initiatives have been taken to empty Faecal Sludge in the functional STPs for co-treatment. Till September -2025 we have Co-Treated **18953.15 KL** Septage in different STPs through Cesspool.
This is for your kind perusal.

Yours faithfully,

22/12/25

Senior Special Secretary,
Department of UD&MA
&
Program Director, WBSPMG

Memo No.:634/1(20)-Sr. Spcl. Secy (NG) **Date:22.12.2025**

Copy forwarded for kind information to:

1. Additional Chief Secretary, Department of Environment
2. Director General, National Mission for Clean Ganga
3. Executive Director (Projects), National Mission for Clean Ganga.
4. Principal Secretary, Department of UD&MA & Executive Chairperson, WBSPMG
5. Member Secretary, WBPCB
6. Municipal Commissioner, Kolkata Municipal Corporation
7. Director (Projects), NMCG
8. Chief Executive Officer, Kolkata Metropolitan Development Authority
9. Director (Technical), National Mission for Clean Ganga
10. Additional Director & Divisional Head, WQM-II, CPCB
11. Special Law Officer, UD&MA Department-with a request to kindly forward a copy of the Report Ld. AOR for her kind noting.
12. Engineer In Chief in charge of Secretary, MED.
13. Director General, GAP Sector, KMDA.
14. Director General, P&D, KMC
15. Chief Engineer, GAP Sector, KMDA
16. Chief Engineer, MED (South)
17. Chief Engineer, PHE Department
18. IT Department, UD&MA Department-for uploading the Report in the NGT portal of our website.
19. OSD to Municipal Commissioner, Kolkata Municipal Corporation.
20. Senior PS to Principal Secretary, UD&MA Department.

22/12/25

Senior Special Secretary,
Department of UD&MA
&
Program Director, WBSPMG

NANDINI GHOSH, IAS
Senior Special Secretary
Department of Urban Development &
Municipal Affairs
Govt. of West Bengal

Main Report

Quarterly progress (July 2025- September 2025) report						
Sl. No.	**Concerned Department**	**Topic of Action point**	**Targets to be achieved as per orders dated 10.12.2015, 13.07.2017 and 22.08.2019 the timelines**	**Targets achieved and the reasons for delay in compliance**	**Targets not achieved and the revised timelines proposed***	**Action taken or suggested for violation of timelines or non-achieving of targets**
[1]	[2]	[3]	[4]	[5]	[6]	[7]
1	KMDA,KMC,MED,PHED	Action points for STPs are seperately considered in Annexure III	As per order of Hon'ble NGT vide OA No 593/2017 & OA No 148/2016 dated 21.5.20 revised time line for all action points are under review and active consideration. For details, pls refer to Annexure -III.	Annexure III	Annexure III	Annexure III
2	KMDA,KMC	Presently in-situ treatment work is completed at Jangipur drain and in future it will be tapped in the ongoing Baharampore - Jangipur Interception & Diversion with STP Project.	As per order of Hon'ble NGT vide OA No 593/2017 & OA No 148/2016 dated 21.5.20 revised time line for all action points are under review and active consideration. For details, pls refer to Annexure - III.	pls refer to Annexure-III	NA	pls refer to Annexure-III
3		Detailsof drain & Drain connected to STP (IV)	As per order of Hon'ble NGT vide OA No 593/2017 & OA No 148/2016 dated 21.5.20 revised time line for all action points are under review and active consideration. For details, pls refer to Annexure - IV	Annexure - IV	Annexure - IV	Annexure - IV
4		**Demarchation of Flood Plain Zone**		A Report has been received from the Environment Department in this regard on 28.06.2021. The Report has been prepared by Department of Geogrpahy, Univeristy of Calcutta. Both the Environment Department and UD & MA Department are going through the Report, post which appropriate actions will be taken.	NA	NA
		Protection and management of flood plain zones (FPZ)				
5		**North 24 Parganas -** Protection to the severely damaged left bank of river Hooghly in between Chaiotanya Ghat and Kanch Mandir Ghat by providing cement concrete block pitching for a length of 170 mm and boulder sausage protection work for a length of 50 m within Ward no. 30 & 31 of Baranagar municipality in P.S. Baranagar, District North 24 Parganas.	31.03.2021	Completed	NA	NA

Sl. No.	Concerned Department	Topic of Action point	Targets to be achieved as per orders dated 10.12.2015, 13.07.2017 and 22.08.2019 the timelines	Targets achieved and the reasons for delay in compliance	Targets not achieved and the revised timelines proposed*	Action taken or suggested for violation of timelines or non-achieving of targets
[1]	[2]	[3]	[4]	[5]	[6]	[7]
6	Irrigation &Waterways Department	**North 24 Parganas -** Protection to the severely damaged left bank of river Hooghly in between Alambazar Government Quarter campus toRamlochan Babu Ghat by providing cement concrete block pitching for a length of 215 m and reconstruction of 50 m guard wall in front of Bhabkunja Ashram undre Ward no. 4 of Baranagar municipality in P.S. Baranagar, District North 24 Parganas.	31.03.2021	Completed	NA	NA
7		**North 24 Parganas -** Protection to the left bank of river Hooghly from Mangal Pandey Ghat to Malanch Tourist Lodge near Vivekananda State Police Academy for a length of 135 m including renovation of sluice under Barrackpore Municipality in P.S. - Barrackpore, Dist. - North 24 Pgs.	31.03.2020	Completed	NA	NA
8		**South 24 Parganas -** Protection work to the left bank of Hooghly embankment at Sulapani Ghat near Harna Sluice for a length of 200m in Block - Diamond Harbour-I, P.S. Diamond harbour, Dist-South 24 Parganas.	31.03.2021	60 % progress achieved.	Mar-23	All out effort has been laid to complete in revised target.
9		**South 24 Parganas -** Protection on left embankment of the Hooghly River for a length of 150 m by dumping Geo-Bag below L.W.L with slope protection by HDPE bags at pujali in P.S – Budge Budge , Dist- South 24 Parganas.	31.03.2022	Completed	NA	NA
10		**South 24 Parganas-** Protection of Hooghly left embankment with Brick Block Pitching for a length of 250 M at Kanchantala Shasan Ghat kali Mandir within Ward No 140 of KMC in P.S – Nadial , Dist- South 24 Parganas	31.03.2022	90 % progress achieved.	Jul-22	All out effort has been laid to complete in revised target.
11		**Howrah -** Protection to right embankment of Hooghly River at the confluence of Chapa Khal for a length of 210 m at Kalinagar in Block Uluberia -I, P.S. Uluberia, District Howrah.	31.12.2020	Completed	NA	NA
12		**Howrah -** Protection to right embankment of Hooghly River at Tetikhola for a length of 150 m in Block Shyampur-I, P.S Shyampur, District Howrah.	31.12.2020	Completed	NA	NA
13		**Howrah -** Protection to right embankment of Hooghly River at the confluence of Gouriganga Khal at Chalkashi for a length of 240 m in Block Uluberia-I, PS Uluberia, District Howrah.	31.12.2020	Completed	NA	NA
14		**Howrah -** Protection of Hooghly right embankment for a length of 300 m at Sirishtala, Gadiara, in Block Shyampur-I, P.S Shyampur, District Howrah.	31.12.2020	Completed	NA	NA
15		Maintaining minimum environmental flow of river.	The river is a perennial river. The environmental flow is maintained through the release from the Farakka Barrage throughout the year.			

<table>
<tr><th>Sl. No.</th><th>Concerned Department</th><th>Topic of Action point</th><th>Targets to be achieved as per orders dated 10.12.2015, 13.07.2017 and 22.08.2019 the timelines</th><th>Targets achieved and the reasons for delay in compliance</th><th>Targets not achieved and the revised timelines proposed*</th><th>Action taken or suggested for violation of timelines or non-achieving of targets</th></tr>
<tr><td>[1]</td><td>[2]</td><td>[3]</td><td>[4]</td><td>[5]</td><td>[6]</td><td>[7]</td></tr>
<tr><td>16</td><td rowspan="2">West Bengal State Pollution Control Board (WBPCB)</td><td>Preventing discharge of Industrial effluents in Ganga and its tributaries/ drains by ensuring installation of proper functioning of ETPs/CETPs</td><td rowspan="2">There are 41 Grossly Polluting Industries along Ganga (total 54 in the State) in the state of West Bengal. Total water consumption is 110 KLD (approx.) and total waste water generation is 88.40MLD (approx.) for 41 GPIs. All the 41 GPIs have Effluent Treatment Plant (ETP) in place and are under regular surveillance of the State Board including monitored through Online Continuous effluent Monitoring System (OCEMS).</td><td></td><td></td><td></td></tr>
<tr><td>17</td><td>Taking action against polluters by way of recovering compensation for restoration of the damage to the environment</td><td></td><td></td><td></td></tr>
<tr><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr>
<tr><td></td><td></td><td>Steps for conservation of groundwater particularly with reference to critical, semi critical or over exploited areas</td><td>Ground water conservation through rainwater harvesting and Artificial Recharge to GW
<table>
<tr><th>District</th><th>Block Adjacent to polluted stretch of River Ganga</th><th>Nos.</th><th>Status</th></tr>
<tr><td>North 24 Parganas</td><td>Barrackpore I (safe)</td><td>1</td><td>Completed (2020)</td></tr>
</table></td><td>Targets achived for 19 completed schemes.</td><td></td><td></td></tr>
</table>

<table>
<tr><th>Sl. No.</th><th>Concerned Department</th><th>Topic of Action point</th><th colspan="4">Targets to be achieved as per orders dated 10.12.2015, 13.07.2017 and 22.08.2019 the timelines</th><th>Targets achieved and the reasons for delay in compliance</th><th>Targets not achieved and the revised timelines proposed*</th><th>Action taken or suggested for violation of timelines or non-achieving of targets</th></tr>
<tr><td>[1]</td><td>[2]</td><td>[3]</td><td colspan="4">[4]</td><td>[5]</td><td>[6]</td><td>[7]</td></tr>
<tr><td rowspan="10">18</td><td rowspan="10">WRIDD(SWID)</td><td rowspan="10"></td><td rowspan="2"></td><td>Barrackpore II (safe)</td><td>1</td><td>Completed (2020)</td><td rowspan="10"></td><td rowspan="10"></td><td rowspan="10"></td></tr>
<tr><td>Bidhannagar Municipal Corpn.</td><td>1</td><td>Completed (2021-2022)</td></tr>
<tr><td>Howrah</td><td>Bally-Jagacha (safe)</td><td>1</td><td>Completed (2016)</td></tr>
<tr><td colspan="2" rowspan="3">KMC (not categorised)</td><td>9</td><td>Completed (2016)</td></tr>
<tr><td>1</td><td>Completed (2017)</td></tr>
<tr><td>3</td><td>3 completed (2020)</td></tr>
<tr><td>South 24 Parganas</td><td>Diamond Harbour I (safe)</td><td>1</td><td>Completed (2017)</td></tr>
<tr><td></td><td>Diamond Harbour II (safe)</td><td>1</td><td>Completed (2019)</td></tr>
<tr><td colspan="4">Safe blocks adjacent to polluted river stretch of river Ganga has been considered for GW recharging as hydraulic gradient is positive towards river Ganga and thus GW is in losing condition. Apprehending critical groundwater condition in future i.e. safe blocks become semi critical/critical/ overexploited. GW conservation measures have been taken up a precautionary measure thereof.</td></tr>
<tr><td colspan="10"></td></tr>
<tr><td rowspan="6">19</td><td rowspan="6">P&RD</td><td>Activities</td><td colspan="2">District</td><td colspan="2">Work done till September2022</td><td></td><td></td><td></td></tr>
<tr><td>Vetiver Plantation</td><td colspan="2" rowspan="5">South 24 Parganas, Murshidabad, Hooghly, Malda, Howrah, Purba Bardhaman, Nadia</td><td colspan="2">73.78 Km</td><td></td><td></td><td></td></tr>
<tr><td>Other Plantation</td><td colspan="2">16.62 Ha</td><td></td><td></td><td></td></tr>
<tr><td>Rooftop Rain water harvesting</td><td colspan="2">15</td><td></td><td></td><td></td></tr>
<tr><td>Restoration of water bodies</td><td colspan="2">1464</td><td></td><td></td><td></td></tr>
<tr><td>Bio-diversity Park</td><td colspan="2">19</td><td></td><td></td><td></td></tr>
<tr><td>20</td><td></td><td>Liquid Waste Management</td><td colspan="4"></td><td></td><td></td><td></td></tr>
<tr><td colspan="10"></td></tr>
<tr><td rowspan="4">21</td><td rowspan="4">State Water Investigantion Departtment (SWID)</td><td rowspan="4">Restoration of water bodies</td><td colspan="4">Restoration of water bodies for rainwater harvesting</td><td rowspan="4">Target achieved</td><td rowspan="4"></td><td rowspan="4">In the Urban areas, 1036 water bodies have been excavated/re-excavated for the period 2017-2020.</td></tr>
<tr><td colspan="2">District</td><td colspan="2">Status</td></tr>
<tr><td colspan="2">South 24 Parganas</td><td colspan="2">Around 300 KM of old sited creeks have been re-excavated for rainwater harvesting in blocks (where groundwater is salinity infested) adjacent to lower reach of River Ganga</td></tr>
<tr><td colspan="10"></td></tr>
</table>

Sl. No.	Concerned Department	Topic of Action point	Targets to be achieved as per orders dated 10.12.2015, 13.07.2017 and 22.08.2019 the timelines	Targets achieved and the reasons for delay in compliance	Targets not achieved and the revised timelines proposed*	Action taken or suggested for violation of timelines or non-achieving of targets
[1]	[2]	[3]	[4]	[5]	[6]	[7]
22	UDMA	Utilisation of treated sewage and septage management	The Department of UD & MA has already framed a Policy on The Re-Use of Treated Water & notified it on 30th June 2020. A DPR is under preparation for using treated water of the Kalyani STP. The water will be used for Pisciculture, Gardening, road cleaning and washing purpose.	• State Government has taken up a pilot project of re-use of waste water generated from 21 MLD STP with 2 units located at Kalyani, which will be re-used. KMDA is preparing DPR in house for reusing the treated water for cleaning of Stadium, Gardening & use by Kalyani Krishi Viswa Vidyalaya.The DPRs are in progress & would be finalized soon. **Action by KMC :** • KMC has mandated re-use of waste water for buildings with more than built-up area of 20000 sqm, in their Building Rules. As per Rule no 145 of KMC Building Rules, 2009, waste water recycling system has been incorporated in 25 buildings and house complexes exceeding 20000 sq.metre as per Environmental Impact Assessment Guideline issued by the State Govt./Govt. of India. It has been decided by the highest authority of Department of UD & MA to construct atleast one FSTP in each districts of WB. Accordingly it has constituted a high level Committee for the purpose of drafting a Policy for construction of customised FSTP in each districts. The Committee will submit its Report with in 15 working days. It is pertinent to mention herer, the State is already running 30KLD FSTP at South Dum DUm under supervision of KMDA. The construction of two more FSTPs one at North Dumdum and Baranagar Municipality and another at Burdwan are under pipeline.		
23	UDMA	Preventing dumping of solid and other waste in and around Ganga	Ensuring collection & transportation of segregated solid wastes from individual household and its scientific disposal as per Solid Waste Management Rule 2016 for all the Urban local bodies (ULBs) within a limited timeframe. Removal of all the dump sites and GVPs from bank of river Ganga. Ensuring screening across all the out falls / channels / big drains that lead to river Ganga. Report from SUDA annexed in Annexure-IV.			
24	UDMA	Clearing old legacy Waste dumpsites	1. Bio-mining at Mollar Bheri in Bidhannagar Municipal Corporation (BMC) 2. Removal of the dumpsites from Dhapa within Kolkata Municipal Corporation (KMC) 3. Removal of other legacy waste from dumpsites from other municipalities / corporations	Out of 37 dumpsites at 31 ULBs, action has been taken at all dumpsites. Implementation at different stages is annexed. Till date 21.99 lakh household bins (green and blue colour) provided to these Ganga Towns. (Annexure V)		

Sl. No.	Concerned Department	Topic of Action point	Targets to be achieved as per orders dated 10.12.2015, 13.07.2017 and 22.08.2019 the timelines	Targets achieved and the reasons for delay in compliance	Targets not achieved and the revised timelines proposed*	Action taken or suggested for violation of timelines or non-achieving of targets
[1]	[2]	[3]	[4]	[5]	[6]	[7]
25	UDMA	Public awareness and involvement for prevention and control of pollution of Ganga	Intensive IEC activities for all the ULBs situated beside the river Ganga involving all the people to generate public awarness regarding solid waste management rule 2016, sanitary landfill facility, procedure of scientific disposal of solid waste, necessity of sewage treatment, arresting the un-treated sewage to river Ganga, promoting eco-friendly products, banning of all palstic waste within a time frame.	1) Centre for Environment and Education, an expert agency, a Centre of Excellence under Ministry of Environment & Forest, Government of India has been engaged as State Level IEC Agency for Development of communication plan, training plan and training module on waste disposal. Communication plan for awareness generation on solid waste management has been prepared. 2) State level logo and slogan competition has been organized on scientific waste disposal in the month of September, 2019 and December, 2020. 3) SHG based publicity campaign in all ULBs was organized in September, 2019. Similar campaigns were there in December, 2020 also. 4) Eco friendly products and products from waste materials are being promoted as alternative to plastics through fairs. 5) Handbook has been prepared on SWM and leaflets have been circulated to all ULBs. 6) Booklet on Solid Waste Management "Barjo Babosthaponar Sahoj Path" in Bengali, Hindi ("Kachra Prabandha ka Sahaj Path") and English("SOLID WASTE MANAGEMENT : A PRIMER") versions published and circulated widely. i) Capacity building training of the rag pickers have commenced and to be completed shortly.		
26	UDMA	Regulating activities on an around river Ganga including Ghats and other establishments	9 Ghats have been completed at Garulia and handed over to the ULB, 2 Ghats at Kalna and Katwa have been completed and handed over to the ULBS,2 Ghats one at Agradwip and another at Daihat are in progress. AA&ES for One Ghat (Prabhupada Ghat under ISCKON) has recently been issued. 3 Electric Crematoria (Garulia, Naihati and Bhatpara) have been completed and handed over to the ULBs. 9 electric Crematoria have been priotrised and now under feasiblilty study. The FSSM Policy of the State of WB for urban local bodies has been finalized and in the process of obligation. The mojor decisions under this policy are: 1. All Ganga ULBs will be having FSTPs (if not some ULBs will be clubbed together). All STPs will also be having FSTPs along with them. Under utilised STPs will temporarily be fed with the Faecal Sludge and Septage by Cess Pool vehicles. In Barrackpore STP, the low capacity utilisation is augmented to some extent by the Cess Pools carrying Faecal sludge and septage.			
27	UDMA	Plastic Waste Management	UD & MA Dept. GoWB has framed a bye-law with respect to Plastic Waste Management (Notification No: 215(Law) /C-12/NGT/Misc – 11/2020 dated 20/3/2020) Plastic carry bags are totally banned in the ecologically sensitive areas and 40 heritage / tourist sites of West Bengal 77 municipalities have banned the manufacturing, use and sale of plastic carry bags of thickness less than 50 micron and 18 municipalities banned use of single use plastic. Workshops carried out to generate awareness among different plastic waste generator and initiative taken to promote eco-friendly products as an alternative to plastic.			

Sl. No.	Concerned Department	Topic of Action point	Targets to be achieved as per orders dated 10.12.2015, 13.07.2017 and 22.08.2019 the timelines		Targets achieved and the reasons for delay in compliance	Targets not achieved and the revised timelines proposed*	Action taken or suggested for violation of timelines or non-achieving of targets
[1]	[2]	[3]	[4]		[5]	[6]	[7]
28	Department of Forest	Afforestation and setting up of biodiversity parks	**Activity** Plantation on both sides of the river	**Polluted River Stretch /Biodiversity Park** 6 ha advance work completed (100%).	Creation work in progress. Work delayed due to late receipt of fund.	NA	NA
29		Biological diversity of Ganga	After a preliminary survey undertaken from Farakka to Diamond Harbour, in which 80 Gangetic Dolphins were sighted, the Forest Department has prepared an Action Plan for Conservation of Ghariyals and Dolphins (2021-31) in West Bengal with a budgetary outlay of Rs. 95 crore.				

List of Good work and efforts of the State of West Bengal towards Liquid Waste Management in River Ganga

1. The Water Quality Data for the month of Sept, 2025 as received from WBPCB shows remarkable improvement for river Ganga. It is now placed in the least priority category i.e. Category-V (The latest Water Quality Report in report submitted by WBPCB in Annexure – A).

River	2018		2022		Sept' 2025	
	Max. BOD (mg/L)	Priority	Max. BOD (mg/L)	Priority	Max. BOD (mg/L)	Priority
Ganga	12.0	III	8.0	IV	2.95	V
With sustained & continuous efforts in LWM & SWM in the Ganga Towns, water Quality of river Ganga has been improved from Priority III to Priority V.						

The diagram showing the improvement of Water Quality with respect to BOD level over last Seven (07) years.

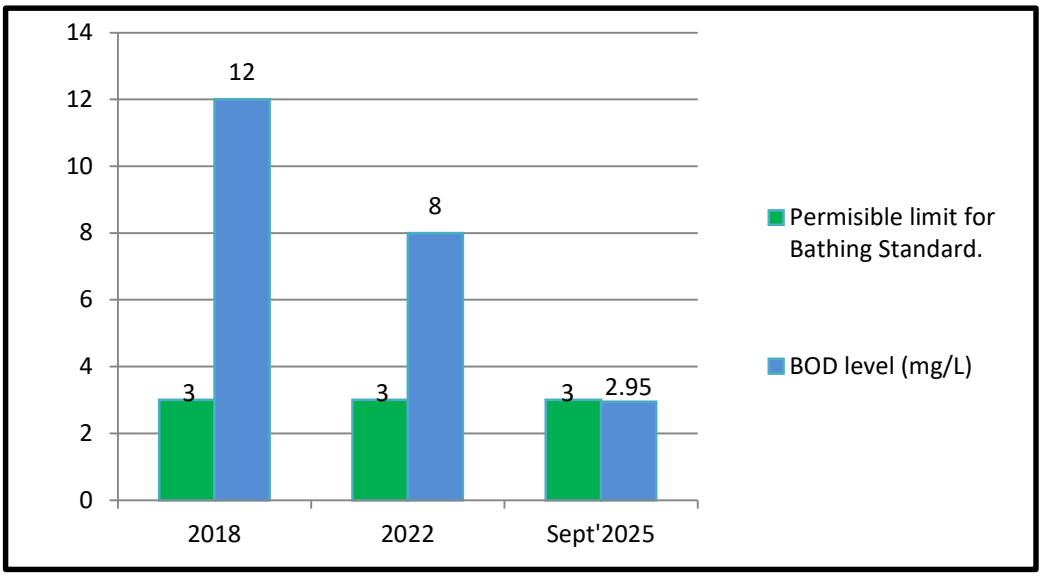

2. The Department of UD&MA is closely monitoring the work of pollution abatement in the river Ganga with due care and concern. Review Meetings are being held by the highest authorities at every month to ensure timely completion of each project. Meetings were held under Chairmanship of Hon'ble Chief Secretary, Principal Secretary, Member Secretary WBPCB, and Program Director, SMCG WB on several occasions.

Details of the Review Meeting:

Sl No	Meeting Taken by	Numbers of Meeting
1.	National Mission for Clean Ganga • Director General, NMCG-3 • Executive Director (Project), NMCG-3 • Empowered Task Force-1	7
2.	Principal Secretary, Department of UD MA & Executive Chairperson, SMCG WB	1
3.	Program Director, SMCG WB	14
Total		**22**

3. Over last Seven years, West Bengal has been successful in completing and commissioning **Twenty-Six (26) STPs** and thus increasing the treatment capacity by **472.24 MLD** and this has resulted in successful reduction of BOD in river Ganga.

Progress towards completion of Sewage Treatment Plants (STPs) over last Seven (7) years.

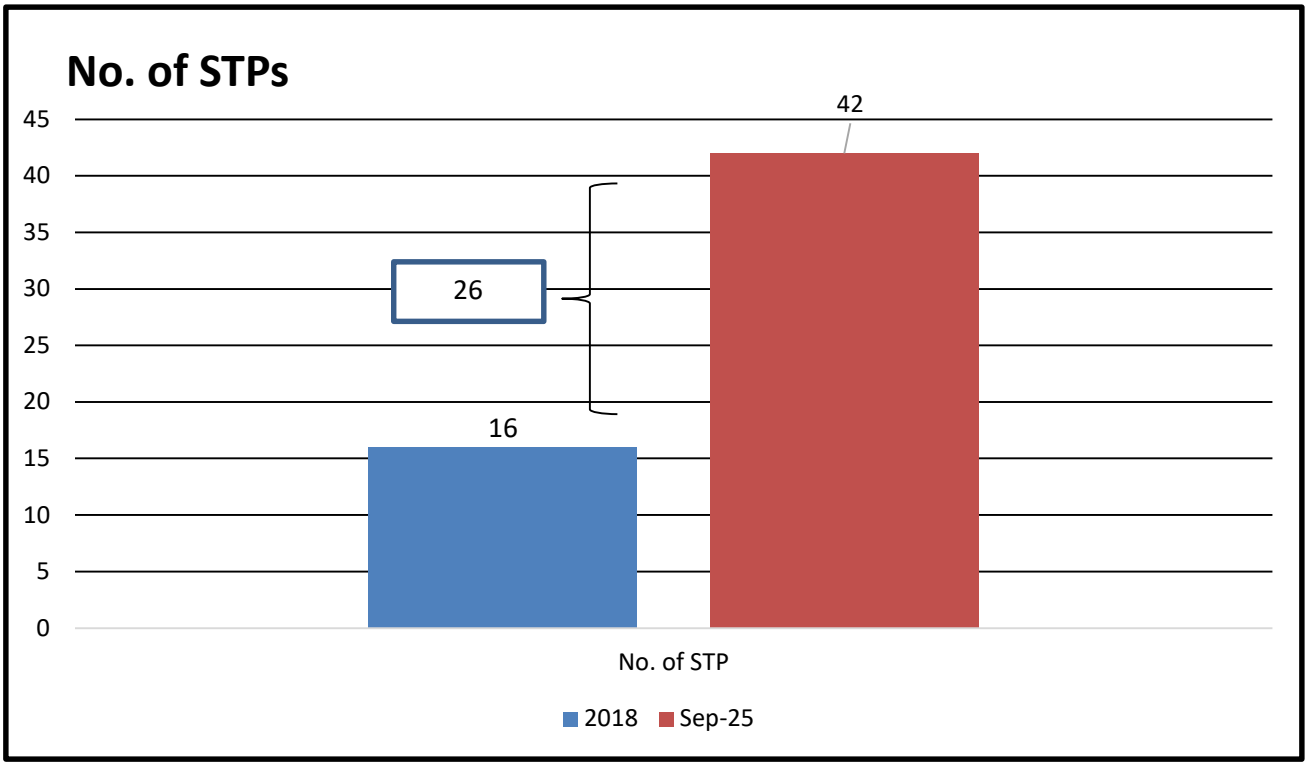

Diagram showing progress in completion of Sewage Treatment Plant as well as enhancement in the Sewage Treatment Capacity over last 7 years (2018 – Sept, 2025)

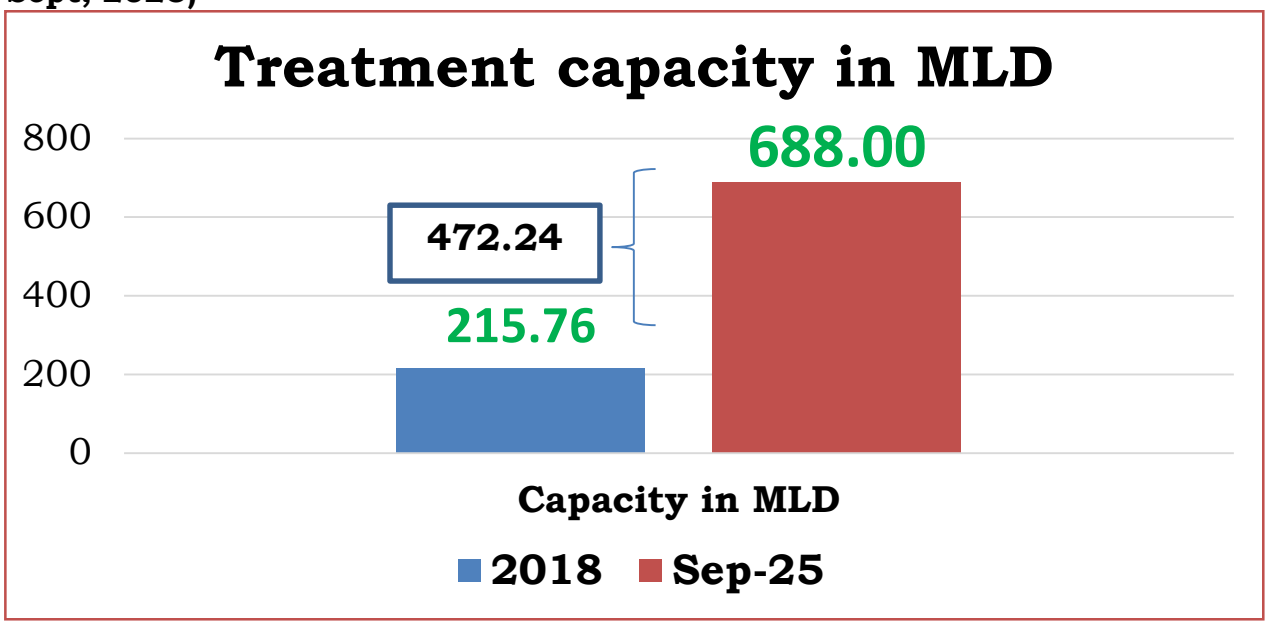

4. Projection for coming Two (2) years

Around 9 STPs with a total treatment capacity of 170.15 MLD is likely to be completed in next two years.

5. Status of Faecal Sludge & Septage Management

- ❖ For effective and comprehensive management of Sewage and Septage with an aim to reduce Faecal Coliform in River Ganga Department of UD&MA Faecal Sludge and Septage Management Policy has been framed and notified by the Department vide Memo No. 33-UDMA/24011(99)/66/2021 dated 25.05.2022.
- ❖ West Bengal is already having two (02) Fully Operational Faecal Sludge Treatment Plants (FSTP) each having a capacity of 30 KLD at Promodnagar Cluster catering the Septage from the Ganga towns of North 24 Parganas district.
- ❖ Bansberia FSTP is under construction stage, Overall Progress up to Sept. 2025 is 6.00% Completion date is July, 2026 (Including Trial Run).
- ❖ FSTPs in Uttarpara-Kotrung (22 KLD), Burdwan (50 KLD) and Pujali (8 KLD) are under Tendering Stage.
- ❖ DPRs for FSTPs at Ranaghat (15 KLD), Haldia (47 KLD) Municipalities are under examination of NMCG.
- ❖ Under Performance Based Incentive Grant (PBIG) FSTPs at Bhadreswar (10 KLD) and Garulia (15 KLD) are under examination of NMCG.
- ❖ Under Performance Based Incentive Grant (PBIG), Electric Crematoria at Chakdah, Garulia and Santipur have been sanctioned and the same are under Tendering.

6. Sludge & Septage Management in Functional Sewage Treatment Plants (STP):

Presently, Septage and Sewage is being co-treated in operational STPs of Gayeshpur, Nabadwip, Halisahar, Budge Budge, Barrackpore, Chandannagar & Chinsurah, Naihati, Kalyani, Bhatpara, Panihati, Howrah ULBs.

- ➢ Total Septage co-treated upto 30.09.2025 in the functional STPs by ULBs as below:

Sl. No	Name of ULB	Co-Treated Septage (KL)
1	Gayeshpur	110.00
2	Nabadwip	607.00
3	Halisahar	593.00
4	Budge Budge	847.60

5	Barrackpore	2211.20
6	Chandannagar & Chinsurah	5279.25
7	Naihati	2688.00
8	Kalyani	2505.00
9	Bhatpara	2083.20
10	Panihati	1992.90
11	Howrah	36.00
	Total Capacity (KL)	**18953.15**

- Total Amount of Septage emptied up to June 2025 – 16408.75 KL
- Incremental Progress over last Report (April 2025 to June 2025) is 2544.40 KL.

- ***Presently UD&MA Department has framed Faecal Sludge & Septage Management Policy wherein Faecal Sludge Treatment Plants (FSTPs) will be established at ULB level wherever possible or in cluster basis. As an integrated approach co-treatment of faecal sludge & sewage is already being done in the existing STPs which has significantly brought down the Faecal coliform load of the water discharged into river Ganga, this is getting done in accordance with the Advisory brought out by UD&MA Department vide Memo No. 1241-UDMA-11014 (49)/16/2023 dated 12.06.2025.***

7. End to End solution

Re-use of Treated Waste Water

Department of UD & MA, Govt. of West Bengal has framed a Policy on Re-use of Treated Waste Water in Urban Areas & has notified it on June 2020.

- Presently, state is utilizing Treated Waste Water in Pisciculture, Gardening Road Cleaning.

- **East Kolkata Wetlands (EKW) is internationally recognized natural STP treating 910 MLD Sewage of Kolkata which is then getting reused in Pisciculture. Presently there are around Ten (10) Fishery co-operatives here, utilizing this Waste Water and generating livelihood for local people.**

- Treated water from STPs is used in Pisciculture, Horticulture, Road cleaning and remaining is discharged which is subsequently used for WTPs for potable water.

8. The State has brought out a policy for the reuse of treated wastewater in urban areas. The UD & MA Department has constituted a committee for its upgradation and alignment with the National Policy.

- In its last meeting held on 24 November 2025, the committee discussed

in detail the following two issues:

- ❖ Mapping of functional STPs with the use patterns of treated wastewater.

- ❖ Fine-tuning the provisions available in the State Policy in line with the National Policy and norms.

- ❖ The next meeting is scheduled on the first week of January 2026, during which all reports will be placed.

9. <u>Mandatory Site Inspection Reports of the Engineers</u>

The Department of UD & MA has issued an Order no 115-UDMA-24011(99)/7/2021-JS(UDMA) dated 02.02.2021 wherein it has been instructed that all Executing Agencies must visit sites compulsorily fortnightly and to submit a Report on the progress of the work along with good quality photographs (The site inspection Report of KMDA for the month of June 2025 is Annexed as B).

10. Construction & Demolition (C&D) waste facility:

KMC has already arranged for separate collection and transportation facilities of Construction & Demolition waste and all these materials are being processed at Patharghata C&D Plant, Patharghata, Action Area-III, Newtown, Kolkata-700135. The plant is fully operational and first of its kind in Eastern India.

11. Styrofoam Waste Processing Facility:

Tender for processing of **StyrofoamWaste processing facility** at Dhapa Site, KMC is under Process.

12. Flower Waste Processing Facility:

Tender for conversion of flower waste into Incense sticks is also under pipeline.

13. Plastic Waste Processing Facility:

KMC has already set up 2 Tons per Day (TPD) Plastic Waste Processing Plant at Dhapa Site. KMC has also issued Work Order for 100 TPD Material Recovery Facility (MRF) with minimum 2 TPD Board plus minimum 8 TPD Lumber for processing and treatment of plastic waste.

14. Electric Crematorium at Barrackpore based on Eco green cremation Technology has been commissioned on 12th September 2025.

15. Ganga District Performance Monitoring System (GDPMS), a dedicated portal for uploading Minutes of the Meeting (MoM) by District Ganga Committees (DGCs) which has been developed by NMCG to capture DGC related activities across each DGC and provides an interactive dashboard to review activities of all DGCs by NMCG. 10 numbers of MoMs have been uploaded in this portal during July, 2025 to September, 2025.

16. As per mandate of the Hon'ble NGT, Online Continuous Effluent Monitoring. Systems (OCEMS) must be installed at the all functional STPs in Ganga River Basin areas. In this connection, integration of OCEMS for 19 number STPs (namely Budge Budge (9.3 MLD), Bhatpara-31 MLD, Bhatpara-10 MLD(Shyamnagar), Halishahar (16 MLD), Howrah (Arupara-65 MLD), Barrackpore-6 MLD, Barrackpore-18 MLD, Baranagar (60 MLD), Bansberia (0.3 MLD), Naihati (11.56 MLD), Gayespur (8.3 MLD), Chandan Nagar (18.16 MLD), Chandan Nagar (4.54 MLD), Bally (40 MLD), Kalyani (10 MLD), Panihati (12 MLD), Titagarh (4.54 MLD), Kalyani (11 MLD) and Bandipur (14.1 MLD)) have been made and connected to the Ganga Tarang portal of NMCG for Online Effluent Management.

17. CCTV integration in Prayag apps to monitor remotely the real time progress of under construction work at 4 STP sites (Chakdah, Maheshtala, Hooghly-Chinsurah and North Barrackpore) has been done.

18. Installation of CCTV Cameras has been done for the surveillance and monitoring functional Sewage Treatment Plant (STPs) at Bhatpara (31 MLD), Bhatpara (10 MLD), Bally (40 MLD), and Baranagar (60 MLD).

PHOTO GALLERY

Communication and Public Outreach Activities from July, 2025 to September, 2025 undertaken by the SMCGWB

Mass Awareness Exhibition (Pavilion in 28th National Exhibition, 2025)

Kolkata

Kolkata

Awareness Programme for Conservation of the endangered Gangetic Dolphin

Purba Bardhaman

Purba Bardhaman

Wall Painting at Maheshtala STP

South 24 Parganas

South 24 Parganas

Inter-School Debate Competition and Seminar regarding River Pollution Abatement

Malda

Sports Activity among local Youth

Educational Visit of Students at Halisahar STP

Educational Visit of Students at Gayeshpur STP

Educational Visit of Students at Arupara STP

Educational Visit of Students at Bhatpara STP

Swachhta Hi Sewa Campaign, 2025

Hooghly

Hooghly

Special Event of Shramdaan, 2025

Murshidabad

Hooghly

Outdoor Publicity (Display of Hoarding / Flex / Banners) during Durga Puja, 2025

Purba Bardhaman

Murshidabad

North 24 Parganas

Howrah

Installation of Permanent Hoarding of Namami Gange Program

Newly Inaugurated Barrackpore Electric Crematorium

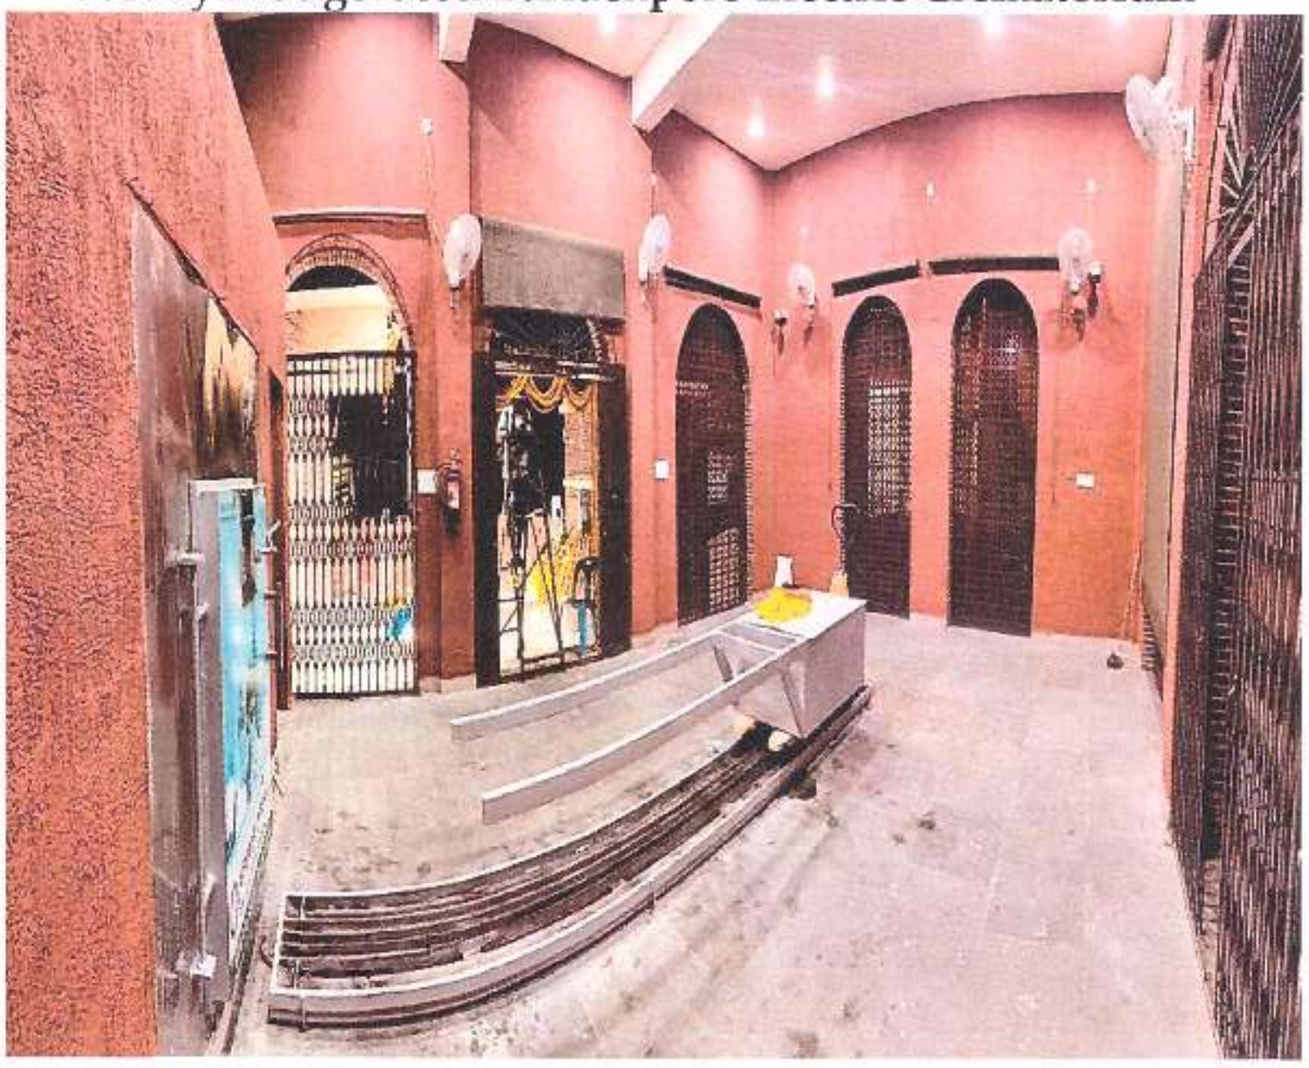

Graffiti (Wall Painting) in Ganga Ghats

NANDINI GHOSH, IAS
Program Director
State Mission for Clean Ganga West Bengal
পশ্চিমবঙ্গ গঙ্গা পরিবেশ-পরিচ্ছন্নতা রক্ষা করার প্রকল্প

(Nandini Ghosh, IAS)
Senior Special Secretary
Department of UD&MA
&
Program Director, SMCG WB

Annexure I

Overall status of Sewage Management in the Ganga Towns of West Bengal

I	**Estimated Sewage Generation** (Based on Estimated population in Urban areas as on 2022 taking 2011 census as base.)	**1401 MLD** (Kolkata - 356.1 MLD and 1044.9 MLD for DGCs)
II	**Details of Sewage Treatment Plants**	
	Existing number of operational STPs and treatment capacity	42 (688.00 MLD)
	Number of STPs under construction	12 (187.25 MLD)
	Number of STPs under renovation (It includes additional 13 MLD, by way of augmenting Garden Reach STP and Keorapukur STP;	13.00 MLD*
	Number of STPs under proposal/tendering stage. (It includes additional 9.14 MLD, by way to augmenting Katwa STP)	14 (364.64MLD) **
	Total treatment capacity	1252.89MLD
III	**Gap in treatment capacity**	**148.11 MLD.**
IV	Sewage treatment capacity in Private STP is approximately.	**78 MLD**

Note:

1. **Proposed STP on Kestopur canal with capacity 41 MLD is included under proposal stage. The canal is flowing partly through Bidhannagar Municipal area and also through North 24 Parganas and joins river Ganga through Chitpur lock gate.

2. *Both Garden Reach and Keorapukur STPs are currently treating 102 MLD Waste Water as of now.

Annexure-III, Quarterly Progress (July 2025 to Sept 2025) Report

Sl. No.	Concerned Department	Topic of Action point for STPs	No of STPs	Targets achieved and the reasons for delay in compliance	Targets not achieved and the revised timelines proposed
[1]	[2]	[3]	[4]	[5]	[6]
1	Kolkata Metropolitan Development Authority (KMDA)	Sewerage System & STP at Kalyani Municipal Town	2	Operation and Maintenance running.	Operational
2		Sewerage System & STP at Gayeshpur Municipal Town	1	Operation and Maintenance running.	Operational
3		Sewerage System & STP at Bhatpara Municipal Town	4	Operation and Maintenance running.	Operational
4		Sewerage System and STP at Halisahar Municipality	1	Operation and Maintenance running.	Operational
5		Sewerage System and STP at Budge Budge Municipality	1	Operation and Maintenance running.	Operational
6		Sewerage System and STP at Barrackpore Municipality	2	Operation and Maintenance runing	Operational
7		Pollution Abatement Work for River Ganga at Nabadwip under NGP Scheme	1	Operation and Maintenance running	Operational
8		Pollution Abatement Works for River Ganga at Howrah under HAM	1	Operational.	Commissioned on 1st October 2024.
9		Pollution Abatement Works for River Ganga at Bally under HAM	1	Operational	All the 3 STPs are functional. Presently the pending Associate Infrastructure works are going on towards completion.
10		Pollution Abatement Work for River Ganga at Kamarhati & Baranagar under HAM	1	Operational	
11		Pollution Abatement works for River Ganga at Kancharapara under DBOT	1	Operation and Maintenance running	Operational
12		Pollution Abatement Work for River Ganga at Berhampore	1	As per proposed revised BOQ Physical Progress upto 30.09.2025 : 80.00%	EoT applied till December2025 by the Agency
13		I & D network for existing drain falling in river Ganga including sewage treatment plant (STP) at Jangipur	2	Raghunathganj: Overall Physical Progress upto 30.09.2025 : 85.00% **Jangipur: Operational, Commissioned on 03.06.2025**	
15		Pollution Abatement Works for river Ganga at Hooghly Chinsurah	1	Operational	(Commmissoned on 01.04.2024)
16		Pollution Abatement Works for river Ganga at Maheshtala Municipality	1	Operational	(Commissioned on 05.06.2025)
17		Rejuvenation of existing STP along with Lifting Station & Pumping Station including Sewerage Network Operation and Maintenance at Baidyabati and Bhadreswar under Hooghly District in West Bengal.	2	Operation and Maintenance running	Operational
18		Rejuvenation of existing STP along with Lifting Station & Pumping Station including Sewerage Network and Operation and Maintenance at Chandannagar and Bansberia under Hooghly District in West Bengal.	3	Operation and Maintenance running	Operational
19		Rejuvenation of existing STP along with Lifting Station & Pumping Station including Sewerage Network and Operation and Maintenance at Serampore and Champdani under Hooghly District in West Bengal.	2	There is a acarcity of appropriate land for setting up a STP for the champdani Town. The feasibility study for setting up a FSTP for the town will be explored. For Serampore, Revised DPR after complying observations of NMCG will be submitted soon	NA

Sl. No.	Concerned Department	Topic of Action point for STPs	No of STPs	Targets achieved and the reasons for delay in compliance	Targets not achieved and the revised timelines proposed
[1]	[2]	[3]	[4]	[5]	[6]
20		Rejuvenation of existing STP along with Lifting Station & Pumping Station including Sewerage Network and Operation and Maintenance at Uttarpara – Kotrung and Konnagar under Hooghly District in West Bengal.	1	Operation and Maintenance running.	Operational
21		Rejuvenation of existing STPs alongwith Lifting Station and pumping station including network at Garulia (1 no STP), Naihati (2 nos. STP), Panihati (1 no STP), Khardah(1 no STP) and Titgrah (2 nos. STP)	7	Operation and Maintenance running.	Operational
22		Sewerage System and STPs at North Barrackpore	2	1). 30 MLD STP at Babunpur - Overall progress - 83.947% 2) 12 MLD STP could not be started for NOC of Land from Cantonment Board.	For 30 MLD STP- 15th February 2026 (Including Trial Run)
23		Pollution abatement works for River Ganga at Katwa (Including augmentation of existing STP), Murshidabad & Santipur	2	Katwa STP is under tendering stage. LoI has been issued for Mursidabad STP on 23.09.2025. Based on the observation of NMCG, revised DPR on the alternative land is under process at Santipur	NA
24		Sewerage System and STP at Chakdah	1	Physical Progress upto 30.09.2025 - 79.60%	EOT applied till March 2026
25		STP at Krishnanagar	1	Overall Progress: 2.00%	Dec, 2026 (Including Trial Run)
26		STPs at Uluberia, Jiaganj- Azimganj, Diamond Harbour, Kestopur	4	3 STPs are in proposal Stage. (Subject to availability of land), Revise DPR for kestopur STP is under preparation stage.	NA
27		STP at Khardah (under Ring fenced fund) 8.15 MLD	1	Overall Progress: 10.00%	March, 2027 (Including Trial Run)
28		STP at Santragachi (under state fund) 1.5 MLD	1	Overall Progress: 12.00%	February, 2026 (Including Trial Run)
29		STP at Kalyani added area (Under ring fenced Head)	1	Under Tendering Stage	NA
30		Near WBSETCL, Joka - 45 MLDC33:G38E35C33:G35C33:H38C33:G35	1	Overall Physical progress- 70.04%	March, 2026
31		Bank Plot, M.G Road - 40 MLD	1	Overall Physical progress- 77.6 %	March, 2026
32		Rajpur-Sonarpur, Rania - 23 MLD	1	Operational	(Commissioned)
33		Bansdroni STP	1	LoA has been issued to L1 bidder on 23.06.2025. The Agreement has been executed on 30.07.2025. Subsequently, the survey, soil investigation and design work has commenced.	36 Months from the date of issuance of Work Order + 15 Years O&M
34		STP Near Golf Garden, Sukhapukur	1		
35		Birji Road STP near Sahid Khudiram Metro	1		
36	Kolkata Municipal Corporation (KMC)	STPs at Garden Reach	1	Existing STP is operational. Overall Progress of New STP is 51.90%	October, 2026 (Including trial run)

Sl. No.	Concerned Department	Topic of Action point for STPs	No of STPs	Targets achieved and the reasons for delay in compliance	Targets not achieved and the revised timelines proposed
[1]	[2]	[3]	[4]	[5]	[6]
37	Corporation (KMC)	STPs at Keorapukur	1	Existing STP is operational. LoA for rejuvination has been isuued on 24.09.2025.	12 months + 3 months Trail Run + 15years (From the date of issueance of work order).
38		Badartala STP	1	The Preliminary Project Report (PPR) for KMC-SHARP Phase 2 is submitted to the Government of West Bengal (GoWB) for approval. Upon receiving approval, the report will be forwarded to the Department of Economic Affairs (DEA), GoI for consideration of external financing assistance.	Time line to be finalized based on the approv-al of the pro-ject from GOI.
39		STP Near BhangaKhal, Gardenreach area (22.54118, 88.25155)	1		
40		New Baghajatin STP	1		NA
41		Strand Road STP	1	Sent to 15th Finance Commission , Tripartite MOU already signed. The land area is under KOPT. The requision for land allotment for STP has been send to KOPT(Kolkata Port Trust). Land allotment is pending.	NA
42	PHED	STPs at Diamond Harbour, Berhampore, Katwa, Murshidabad (augmentation & Renovation proposed) and Nabadwip	5	Operational. Constructed in GAP-I. Augmentation of Murshidabad STP is under tendering stage.	Operational
43	MED	Jiagunj Azimgunj Takia Oxidation Pond	2	Operational	Operational

Details of tapped/untapped drains in connection with OA 200/2014*

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	District/Town	Nature of drains/Canals / Khals	water quality analysis– heavy metals	Fecal coliform (MPN/100 ml)	If tapped or untapped	Quantity of sewage discharged from the drain (MLD)	Total quantity sewage diverted and to be diverted (%) to STP	Utilization	Balance qty	sp.quantity of FC present in sewage	STP to which the drain is proposed to be connected after tapping	Compliance of STP (Norms given by NGT/MoEF)	Status of land allotted for STP	Status of funds provided for the STP	Timeline for making the STP functional	Timeline for completing the household connectivity to that STP
1	**Talpukur**	North 24 Parganas	DRAIN	BOD-19mg/l,COD 76mg/l,FC-1600 MPN/100ml	1600	**Tapped**	0.605	100%	0.605	0	968 MPN/100 ml	Tapped under Bandipur STP (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
2	**Gariffa Drain (North)4.14**	North 24 Parganas	DRAIN	BOD-21mg/l,COD 46mg/l,FC-4.7x10^6 MPN/100 ml	4700000	**Tapped**	10.36	40%	4.1	6.2	19458000 MPN/100ml	Tapped under Naihati STP(WSP) (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
3	**Kamarhati Drain @ Jute Mill, Kamarhati**	North 24 Parganas	DRAIN	BOD-24mg/l,COD 72mg/l,FC-2.7x10^4 MPN/100 ml	27000	**Tapped**	42.48	100%	42.48	0.0	1146960 MPN/100ml	Tapped under Baranagar & Kamarhati STP (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
4	**Gandhi ghat Drain @ South gate-1, Barrackpore**	North 24 Parganas	DRAIN	BOD-29mg/l,COD 63.8mg/l,FC-3.3x10^6 MPN/100 ml	3300000	**Tapped**	4.07	100%	4	0.1	13200000 MPN/100ml	Tapped under 6 MLD STP at Barrackpore (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
5	**Chinsurah -Majir Rasta Drain**	Hooghly	DRAIN	BOD-30mg/l,COD-61mg/l,FC-4.6x10^5 MPN/100ml	460000	**Tapped**	17.12	100%	17.12	0.0	7875200 MPN/100ml	Will be tapped in Hooghly Chinsurah STP. Under construction. (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
6	**Rosbara khal, Hooghly**	Hooghly	Khal	BOD-32mg/l,COD-48mg/l,FC-1.3x10^5 MPN/100ml	130000	**Tapped**	9.11	100%	9.11	0.0	1184300b MPN/100ml	Will be tapped in Hooghly Chinsurah STP. Due to non- availability of RoW on road connection not yet done. (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
7	**Drain at Tamil para Ferry Ghat, Chinsura**	Hooghly	DRAIN	BOD-33.77mg/l,COD-92.8mg/l,FC-214516MPN/100ml	214516	**Tapped**	1.5	100%	1.5	0	1774 MPN/100	will be tapped in Hooghly Chinsurah STP. Civil Construction completed. Gate will be installed soon. (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
8	**Dakineshwar -Alambazar**	North 24 Parganas	DRAIN	BOD-34mg/l,COD 118mg/l,FC-900MPN/100ml	900	**Tapped**	44.93	100%	44.93	0.0	40437 MPN/100ml	Will be tapped under 60 MLD Baranagar STP under HAM model (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
9	**Chandannagar Drain**	Hooghly	DRAIN	BOD-38mg/l,COD 70mg/l,FC-2.6x10^4MNP/100ml	26000	**Tapped**	0.6	100%	0.6	0.0	15600 MPN/100ml	Tapped in Chandannagar STP (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
10	**Debitala pancha khal**	North 24 Parganas	DRAIN	BOD-43mg/l,COD 136mg/l,FC-9.4x10^6MNP/100ml	9400000	**Tapped**	46.36	9%	4.2	42.2	9.4x10^6MNP /100ml	Tapped under Garulia STP(WSP) (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
11	**Drain near PB Ghat @ Kamarhati**	North 24 Parganas	DRAIN	BOD-50mg/l,COD 102mg/l,FC-5.2x10^5 MPN/100 ml	520000	**Tapped**	4.76	100%	4.76	0.0	2475200 - 9.4x10^6MNP /100ml	Tapped under Panihati STP (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
12	**Titagarh Drain @ Bishalaxmi Ghat**	North 24 Parganas	DRAIN	BOD-51mg/l,COD 136mg/l,FC-2.8x10^6MPN/100ml	2800000	**Tapped**	5.79	100%	5.79	0.0	16212000 - 9.4x10^6MNP /100ml	Tapped under Bandipur STP (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
13	**Thannar Khal, Naihati**	North 24 Parganas	Khal	BOD-76mg/l,COD 168mg/l,FC-4.0x10^6MPN/100ml	400000	**Tapped**	10.18	100%	10.18	0	4.0x10^6MNP /100ml	Tapped under Naihati STP(ASP) (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
14	**Jangipur Drain**	Murshidabad	DRAIN	BOD-107mg/l,COD 221mg/l,FC-3.9x10^7MPN/100ml	39000000	**Tapped**	0.8	100%	0.8	0	3.9x10^7MNP /100ml	Tapped under 8.0 MLD Jangipur STP (KMDA)	MoEF	AVALABLE	NMCG	31.09.2025	Household connection does not arise.

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	District/Town	Nature of drains/Canals / Khals	water quality analysis– heavy metals	Fecal coliform (MPN/100 ml)	If tapped or untapped	Quantity of sewage discharged from the drain (MLD)	Total quantity sewage diverted and to be diverted (%) to STP	Utilization	Balance qty	sp.quantity of FC present in sewage	STP to which the drain is proposed to be connected after tapping	Compliance of STP (Norms given by NGT/MoEF)	Status of land allotted for STP	Status of funds provided for the STP	Timeline for making the STP functional	Timeline for completing the household connectivity to that STP
15	**Gariffa Drain (South)/Ramaghat Drain-Open Pucca Drain**	North 24 Parganas	DRAIN	BOD-108mg/l,COD 204mg/l,FC-2.2x10^7MPN/100ml	22000000	**Tapped**	4.85	90%	4.4	0.5	2.2x10^7MNP/100ml	Tapped under Naihati STP(WSP) (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
16	**Alliance Jute Mill Drain**	North 24 Parganas	DRAIN	BOD-122mg/l,COD 238mg/l,FC-3.3x10^5MPN/100ml	330000	**Tapped**	1.38	30%	0.41	1.0	3.3x10^5MNP/100ml	Already Tapped with Bhatpara STP (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
17	**Dakineshwar ferry ghat**	North 24 Parganas	DRAIN	BOD-160mg/l,COD 358mg/l,FC-3.5x10^6MPN/100ml	3500000	**Tapped**	Discharge measurment is under process.	0	0	0	3.5x10^6MNP/100ml	Tapped under 60 MLD STP at Baranagar (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
18	**Bagher Khal, (Fodder Khal)**	Nadia	khal	BOD-33mg/l,COD 81mg/l,FC-4x10^6MPN/100ml	4000000	**Tapped**	55.65	Discharge measurment is under process.				Proposed to be tapped with Kancharapara STP (KMDA)	MoEF	AVALABLE	NMCG/State	Nov-25	Household connection does not arise.
19	**Munikali Khal (formerly Drain @ Akhra Food ghar)new**	South 24 Parganas	Khal	BOD-34mg/l,COD 69mg/l,FC-7x10^5MPN/100ml	700000	**Tapped**	20	100%	20	0.0	7x10^5MNP/100ml	Will be tapped to the Maheshtala STP HAM project. Under construction. (KMDA)	MoEF	AVALABLE	NMCG	31.08.25	Household connection does not arise.
20	**Sakhai Para Ghat Drain, katwa**	Purba Bardhaman	DRAIN	BOD-34mg/l,COD 106mg/l,FC-1400MPN/100ML	1400	**Tapped**	3.978	100%	3.978	0.0	1400MNP/100ML	Will be tapped under 14 MLD Katwa STP. (KMDA)	Proposed STP will be MoEF norms compliant	Got NOC from competent authority	NMCG	18 months from the date of issuance of the work order which is expected to be issued by July25	Household connection does not arise.
21	**Majher Char Khal, Kalyani**	Nadia	khal	BOD-35mg/l,COD 91mg/l,FC-2.6x10^6MPN/100ml	2600000	**Tapped**	24.32	Discharge measurment is under process.				To be tapped with the Sewerage network of added area of Kalyani Municipality, PH - I. Tender is under process. (KMDA)	MoEF	Identification of land is under process	State Fund	Functional	Household connection does not arise.
22	**Raninagar - Chakdha**	Nadia	DRAIN	BOD-36mg/l,COD 63mg/l,FC-4x10^6MPN/100ml	4000000	**Tapped**	0.085	100%	0.085	0.0	4x10^6MNP/100ml	Already considered under the Chakdah STP Project work (KMDA)	MoEF	AVALABLE	NMCG	Sep-25	Household connection does not arise.
23	**Drain near Kasiganj, Katwa**	Purba Bardhaman		BOD-60mg/l,COD 185mg/l,FC-35000MPN/100ML	35000	**Tapped**	1.665	100%	1.665	0.0	35000MNP/100ML	Will be tapped under 14 MLD Katwa STP. (KMDA)	Proposed MoEF will be MoEF norms compliant	Got NOC from competent authority	NMCG	18 months from the date of issuance of the work order which is expected to be issued by July25	Household connection does not arise.
24	**Balughat, Manirampore, Pucca drain, Barrackpore**	North 24 Parganas	DRAIN	BOD-67mg/l,COD 108mg/l,FC-1.3x10^6MPN/100ml	1300000	**Tapped**	3.17	100%	3.17	0.0	1.3x10^6MNP/100ml	To be tapped in the proposed STP of Monirampur (KMDA)	DO	DO	NMCG	DO	Household connection does not arise.
25	**Imambara Khal**	Hooghly	Khal	BOD-72mg/l,COD-126mg/l,FC-3.7x10^4MPN/100ml	37000	**Tapped**	5.24	100%	5.24	0.0	3.7x10^4MNP/100ml	Will be tapped in Hooghly Chinsurah STP.Variation proposal not yet approved by NMCG. (KMDA)	Proposed STP will be MoEF norms compliant	AVALABLE	NMCG	Functional	Household connection does not arise.
26	**Ichapur Khal**	North 24 Parganas	Khal	BOD-92mg/l,COD 343mg/l,FC->1600MNP/100ml	1600	**Tapped**	76.032	60%	45.6	30.4	1600MPN/100ml	2nd Order polluted drains of Icchapur Khal will be tapped to the on going STP at Babanpur under North Barrackpore HAM Project. (KMDA)	MoEF	AVALABLE	NMCG	Mar-26	Household connection does not arise.

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	**District/Town**	**Nature of drains/Canals / Khals**	**water quality analysis– heavy metals**	**Fecal coliform (MPN/100 ml)**	**If tapped or untapped**	**Quantity of sewage discharged from the drain (MLD)**	**Total quantity sewage diverted and to be diverted (%) to STP**	**Utilization**	**Balance qty**	**sp.quantity of FC present in sewage**	**STP to which the drain is proposed to be connected after tapping**	**Compliance of STP (Norms given by NGT/MoEF)**	**Status of land allotted for STP**	**Status of funds provided for the STP**	**Timeline for making the STP functional**	**Timeline for completing the household connectivity to that STP**
27	**Rattala- Gorabazar Beherampore**	Murshidabad	DRAIN	BOD-95mg/l,COD 290mg/l,FC-2.7x10^5MPN/100ml	270000	**Tapped**	0.4	100%	0.4	0.0	2.7x10^5MNP/100ml	To be tapped under 3.5 MLD Berhampore STP (KMDA)	MoEF	AVALABLE	NMCG	30.11.2025	Household connection does not arise.
28	**130, Foreshore Road Drain, Howrah**	Howrah	DRAIN	BOD-96mg/l,COD-197mg/l,FC-1.1x10^6MPN/100ml	1100000	**Tapped**	0.0069	100%	0.0069	0.0	1.1x10^6MNP/100ml	To be tapped in the proposed 65 MLD STP of Arupara, Howrah (KMDA)	MoEF	Identification of land is under process	NMCG	Functional	Household connection does not arise.
29	**Shibpur Burning Ghat, Howrah -Shibpur**	Howrah	DRAIN	BOD-96mg/l,COD 212mg/l,FC-2.7x10^5MPN/100ml	270000	**Tapped**	22.79	100%	22.79	0.0	2.7x10^5MNP/100ml	To be tapped in the proposed 65 MLD STP of Arupara, Howrah (KMDA)	MoEF	Identification of land is under process	NMCG	Functional	Household connection does not arise.
30	**Jagannath Drain**	Howrah	DRAIN	BOD-104mg/l,COD 185mg/l,FC-3.3x10^5MPN/100ml	330000	**Tapped**	4.29	100%	4.29	0.0	3.3x10^5MNP/100ml	To be tapped under 62 MLD STP at Kona STP (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.
31	**Nashipur Ghosh Para.Ward No-14**	Murshidabad	DRAIN	BOD-116mg/l,COD 480mg/l,FC-2.4x10^5MPN/100ml	240000	**Tapped**	0.857	100%	0.857	0.0	2.4x10^5MNP/100ml	To be tapped under 5 MLD STP at Murshidabad (KMDA)	MoEF	AVALABLE	NMCG	DO	Household connection does not arise.
32	**Sukanta Palli High Drain, Katwa**	Purba Bardhaman	DRAIN	BOD-122mg/l,COD 392mg/l,FC-350000MPN/100ml	350000	**Tapped**	1.115	100%	1.115	0.0	350000MNP/100ML	Will be tapped under 14 MLD Katwa STP. (KMDA)	MoEF	Got NOC from competent authority	NMCG	18 months from the date of issuance of the work order which is expected to be issued by July25	Household connection does not arise.
33	**Monirampore - Barrackpore**	North 24 Parganas	DRAIN	BOD-24mg/l,COD 98mg/l,FC-280MPN/100ml	280	**Tapped**	8.04	100%	8.04	0.0	280MPN/100 ml	To be tapped in the proposed STP of Monirampur (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG	Mar-26	Household connection does not arise.
34	**Dhobi Ghat Drain, Barrackpore**	North 24 Parganas	DRAIN	BOD-25mg/l,COD 51mg/l,FC-7x10^4MPN/100ml	70000	**Tapped**	0.47	100%	0.47	0.0	7x10^4MNP/100ml	To be tapped in the proposed STP of Monirampur. (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG	Mar-26	Household connection does not arise.
35	**Barrackpore (adjacent to Ramakrishana Mission)**	North 24 Parganas	DRAIN	Water quality Report awaited from WBPCB		**Tapped**	6.16	55%	3.4	2.8	Water quality Report awaited from WBPCB	To be tapped in the proposed STP of Monirampur (KMDA)	MoEF	Identification of land is under process	NMCG	2 years from the date of issuance of the work order.	Household connection does not arise.
36	**Muni Khali Khal (Akhra ferry Ghat)old**	South 24 Parganas	Khal	BOD-27mg/l,COD 41mg/l,FC-9.4x10^4MPN/100ml	94000	**Tapped**	11.72	100%	11.72	0.0	9.4x10^4MNP/100ml	Tapped to the Maheshtala STP HAM project. Under construction. (KMDA)	MoEF	AVALABLE	NMCG	31.08.25	Household connection does not arise.
37	**Chandni Ghat Drain, Chinsurah**	Hooghly	DRAIN	BOD-27mg/l,COD-49mg/l,FC-1.4x10^5MPN/100ml	140000	**Tapped**	25.75	100%	25.75	0.0	1.4x10^5MNP/100ml	To be tapped in Hooghly Chinsurah STP. Under construction. (KMDA)	MoEF	AVALABLE	NMCG	Functional	Household connection does not arise.

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	**District/Town**	**Nature of drains/Canals / Khals**	**water quality analysis– heavy metals**	**Fecal coliform (MPN/100 ml)**	**If tapped or untapped**	**Quantity of sewage discharged from the drain (MLD)**	**Total quantity sewage diverted and to be diverted (%) to STP**	**Utilization**	**Balance qty**	**sp.quantity of FC present in sewage**	**STP to which the drain is proposed to be connected after tapping**	**Compliance of STP (Norms given by NGT/MoEF)**	**Status of land allotted for STP**	**Status of funds provided for the STP**	**Timeline for making the STP functional**	**Timeline for completing the household connectivity to that STP**
38	**Jhikhurkhali drain**	Purba Medinipur	Drain	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Since BOD level of the waste water of outfall discharging is low and there is tidal effect, the DPR on FSTP is under preparation. (KMDA)	MoEF	Identification of land is under process	NMCG/State	1 year from the date of issuance of the work order.	Since it is FSTP, question of tapping of the household connectivity does not arise
39	**Drain at Begunberia, Harakhali**	Purba Medinipur	Drain	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Since BOD level of the waste water of outfall discharging is low and there is tidal effect, the DPR on FSTP is under preparation. (KMDA)	MoEF	Identification of land is under process	NMCG/State	1 year from the date of issuance of the work order.	Since it is FSTP, question of tapping of the household connectivity does not arise
40	**Green belt canal**	Purba Medinipur	Drain	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Since BOD level of the waste water of outfall discharging is low and there is tidal effect, the DPR on FSTP is under preparation. (KMDA)	MoEF	Identification of land is under process	NMCG/State	1 year from the date of issuance of the work order.	Since it is FSTP, question of tapping of the household connectivity does not arise
41	**Budge Budge -Pujali**	South 24 Parganas	Drain	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Since BOD level is low and there is tidal effect, a DPR on FSTP is prepared and submitted to the NMCG which is under examination. (KMDA)	MoEF	AVALABLE	NMCG	1 year from the date of issuance of the work order.	Since it is FSTP, question of tapping of the household connectivity does not arise
42	**Serampore/ Bhagirathi Drain**	Hooghly	DRAIN	BOD-34mg/l,COD 77mg/l,FC-2.6x10^7MNP/100ml		Untapped	25	0	0	25	2.6x10^7MNP/100ml	DPR was submitted to NMCG. Few observation of NMCG regarding the DPR will be complied by 15th Jan,2026	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Household connection does not arise.
43	**Chatra Khal, Serampore**	Hooghly	Khal	BOD-38mg/l,COD 86mg/l,FC-2x10^7MNP/100ml		Untapped	52	0%	0%	52	2x10^7MNP/100ml	DPR was submitted to NMCG. Few observation of NMCG regarding the DPR will be complied by 15th Jan,2026	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Household connection does not arise.
44	**Telkal Ghat drain, Howrah**	Howrah	DRAIN	BOD-127mg/l,COD 262mg/l,FC-2.6x10^5MNP/100ml		Untapped	10.55	0	0	10.55	2.6x10^5MNP/100ml	Engagement of consultant for preparation of DPR is under process. Due to non-availability of land, alternative tecnology is being explored.	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Household connection does not arise.
45	**Phuleswar drain @ Uluberia**	Howrah	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Bid opened and placed for the Departmental approval .	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Household connection does not arise.
46	**Madai Hat**	Howrah	DRAIN	BOD-9mg/l,COD-38mg/l,FC-900MNP/100ml		Untapped	Negligible					Alternative low cost technology is also being explored as BOD is below 30 mg/l. (KMDA)	Alternative low costt technology is also being explored as BOD is below 30 mg/l.	Alternative low costt technology is also being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low costt technology is also being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
47	**Garchumuk**	Howrah	DRAIN	BOD-11mg/l,COD 46mg/l,FC-1600MPN/100ml		Untapped	5.78	0	0	5.78	1600MPN/100ml	Alternative low cost technology is also being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is also being explored as BOD is below 30 mg/l.	Alternative low cost technology is also being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is also being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	District/Town	Nature of drains/Canals / Khals	water quality analysis– heavy metals	Fecal coliform (MPN/100 ml)	If tapped or untapped	Quantity of sewage discharged from the drain (MLD)	Total quantity sewage diverted and to be diverted (%) to STP	Utilization	Balance qty	sp.quantity of FC present in sewage	STP to which the drain is proposed to be connected after tapping	Compliance of STP (Norms given by NGT/MoEF)	Status of land allotted for STP	Status of funds provided for the STP	Timeline for making the STP functional	Timeline for completing the household connectivity to that STP
48	**Sankrail, near Manikpur ferry ghat**	Howrah	DRAIN	BOD-11mg/l,COD 41mg/l,FC-500MPN/100ml.		Untapped	30.84	0	0	30.84	500MPN/100 ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
49	**Singhi More Khal**	Howrah	Khal	BOD-13mg/l,COD 30mg/l,FC-8x10^6MNP/100ml		Untapped	14.2	0	0	14.2	8x10^6MNP/100ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
50	**Kalinga Nagar drain**	Howrah	DRAIN	BOD-13mg/l,COD 42mg/l,FC-1250MPN/100ml	1250	Untapped	20	0	0	20	Alternative low cost technology is being explored as BOD is below 30		Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
51	**Chakmadhu, Nalpur near Bauria ferry ghat**	Howrah	DRAIN	BOD-14mg/l,COD 45mg/l,FC-1250MPN/100ml	1250	Untapped	3	0	0	3	1250MPN/100ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
52	**Drain @ Bazarpara,Garighat Sharenga Khal**	Howrah	Khal	BOD-14mg/l,COD 35mg/l,FC-4.5x10^4MNP/100ml	45000	Untapped	87.2	0	0	87.2	4.5x10^4MNP/100ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
53	**Barrackpore Drain (SP Bunglow)**	North 24 Parganas	DRAIN	BOD-14 mg/l,COD 328mg/l,FC-3.2x10^5MNP/100ml	320000	Untapped	4.87	0%	0%	4.9	3.2x10^5MNP/100ml	To be tapped in the proposed STP of Monirampur (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
54	**Chakashi - Chengali**	Howrah	DRAIN	BOD-15mg/l,COD 40mg/l,FC-1250MPN/100ml	1250	Untapped	45	0%	0%	45	1250MPN/100ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
55	**Sarishapara**	Hooghly	DRAIN	BOD-16mg/l,COD 58mg/l,FC-1600MPN/100ml	1600	Untapped	41.62	0	0	41.62	1600MPN/100ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	District/Town	Nature of drains/Canals / Khals	water quality analysis– heavy metals	Fecal coliform (MPN/100 ml)	If tapped or untapped	Quantity of sewage discharged from the drain (MLD)	Total quantity sewage diverted and to be diverted (%) to STP	Utilization	Balance qty	sp.quantity of FC present in sewage	STP to which the drain is proposed to be connected after tapping	Compliance of STP (Norms given by NGT/MoEF)	Status of land allotted for STP	Status of funds provided for the STP	Timeline for making the STP functional	Timeline for completing the household connectivity to that STP
56	**Authpur (Sastrinagar)**	North 24 Parganas	DRAIN	BOD-21mg/l,COD 78mg/l,FC-1600MPN/100ml	1600	Untapped	6.03	0	0	6.03	1600MPN/100ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
57	**Rishra burning ghat**	Hooghly	DRAIN	BOD-21mg/l,COD-48mg/l,FC-78313MNP/100ml	78313	Untapped	4.95	0%	0.00	4.95	78313MNP/100ml	Alternative low cost technology is being explored as BOD is below 30 mg/l. (KMDA)	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Alternative low cost technology is being explored as BOD is below 30 mg/l.	NMCG/State	Alternative low cost technology is being explored as BOD is below 30 mg/l.	Does not arise as it will be In-situ treatment
58	**Dewangazi Drain**	Hooghly	DRAIN	BOD-31mg/l,COD-64mg/l,FC-1.1x10^7MNP/100ml	11000000	Untapped	20.67	0%	0%	20.7	1.1x10^7MNP/100ml	Proposal for In- Situ tretment on this drain is sent to NMCG on 04.07.2025 for approval.	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG	31.12.26	Does not arise as it will be In-situ treatment
59	**Halisahar Drain**	North 24 Parganas	DRAIN	BOD-33mg/l,COD 87mg/l,FC-3.3x10^6MNP/100ml	3300000	Untapped	22.94	0%	0%	23	3.3x10^6MNP/100ml	Proposal for In- Situ tretment on this drain is sent to NMCG on 04.07.2025 for approval.	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG	31.12.2026	Does not arise as it will be In-situ treatment
60	**Bally Khal, Bally**	Howrah	KHAL	BOD-22mg/l,COD-46mg/l,FC-2.2x10^4MNP/100ml	22000	Untapped	264.52	0	0	264.52	2.2x10^4MNP/100ml	DPR preparation work is under progress. Work is being delayed due to non- availability of land. Piliminary report has been submitted .	Proposed STP, if feasible, will be MoEF norms compliant	Identification of land is under process	NMCG/State	STP, if feasible, may be tentitively completed within 2 years from the date of Work Order	Does not arise as DPR is under preparation
61	**N.C.Pal Khal**	Howrah	Khal	BOD-24mg/l,COD 52mg/l,FC-3.3x10^5MNP/100ml	330000	Untapped discharging in Ganga	4.12	0%	0%	4.1	3.3x10^5MNP/100ml	Tender (3rd call) for preparation of DPR will be placed by jan 2026.	Proposed STP, if feasible, will be MoEF norms compliant	Identification of land is under process	NMCG/State	Proposed STP, if feasible, may be tentitively completed within 2 years from the date of Work Order	Does not arise as DPR is under preparation
62	**Saraswati Khal, Sankrail**	Howrah	Khal	BOD-28mg/l,COD 63mg/l,FC-1.4x10^6MNP/100ml	1400000	Untapped	3.65	0%	0%	3.7	1.4x10^6MNP/100ml	Engagement of consultant for preparation of DPR is under process. (KMDA)	Proposed STP, if feasible, will be MoEF norms compliant	Identification of land is under process	NMCG	Proposed STP, if feasible, will be completed tentitively within 2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
63	**Dhopa Ghat Drain, Hooghly**	Hooghly	DRAIN	BOD-28mg/l,COD-60mg/l,FC-2.6x10^5MNP/100ml	260000	Untapped	7.31	0%	0%	7.3	2.6x10^5MNP/100ml	Proposal for engagement of consultant for preparation of DPR is under considaration. (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	Proposed STP, if feasible, will be completed tentitively within 2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	**District/Town**	**Nature of drains/Canals / Khals**	**water quality analysis– heavy metals**	**Fecal coliform (MPN/100 ml)**	**If tapped or untapped**	**Quantity of sewage discharged from the drain (MLD)**	**Total quantity sewage diverted and to be diverted (%) to STP**	**Utilization**	**Balance qty**	**sp.quantity of FC present in sewage**	**STP to which the drain is proposed to be connected after tapping**	**Compliance of STP (Norms given by NGT/MoEF)**	**Status of land allotted for STP**	**Status of funds provided for the STP**	**Timeline for making the STP functional**	**Timeline for completing the household connectivity to that STP**
64	**Nazerganj Khal**	Howrah	Khal	BOD-29mg/l,COD 62mg/l,FC-4x10^6MNP/100ml	4000000	Untapped	336.71	0%	0	336.71	4x10^6MNP/100ml	Proposal for engagement of consultant for preparation of DPR is under considaration. (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	Proposed STP, if feasible, will be completed tentitively within 2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
65	**Gondal Para**	Hooghly	DRAIN	BOD-34mg/l,COD 136mg/l,FC-1600MPN/100ml	1600	Untapped	61.34	0	0	61.34	1600MPN/100ml	Proposal for engagement of consultant for preparation of DPR is under considaration. (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	Proposed STP, if feasible, will be completed tentitively within 2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
66	**Baidyabati Drain**	Hooghly	DRAIN	BOD-36mg/l,COD 68mg/l,FC-3.2x10^5MNP/100ml	320000	Untapped	128.77	0%	0%	128.77	3.2x10^5MNP/100ml	DPR preparation work is under progress. Work is being delayed due to non- availability of land. Alernative technology is being explored.	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
67	**Bhatpara open pucca drain**	North 24 Parganas	DRAIN	BOD-37mg/l,COD 83mg/l,FC-2.6x10^5MNP/100ml	260000	Untapped	61.89	0%	0%	61.89	2.6x10^5MNP/100ml	Engagement of consultant for preparation of DPR is under process. (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
68	**Goshpara drain, Nabadwip**	Nadia	DRAIN	BOD-37mg/l,COD 86mg/l,FC-2.6x10^6MNP/100ml	2600000	Untapped	Discharge measurment is under process.					Consultant for preparation of DPR is to be engaged by MED (MED)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
69	**Khardha Khal, Khardha**	North 24 Parganas	Khal	BOD-41mg/l,COD 116mg/l,FC-4.2x10^6MNP/100ml	4200000	Untapped	105.6	0%	0%	105.6	-4.2x10^6MNP/100ml	Consultant engaged for preparation of DPR. Alernative technology is being explored.	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	**District/Town**	**Nature of drains/Canals / Khals**	**water quality analysis– heavy metals**	**Fecal coliform (MPN/100 ml)**	**If tapped or untapped**	**Quantity of sewage discharged from the drain (MLD)**	**Total quantity sewage diverted and to be diverted (%) to STP**	**Utilization**	**Balance qty**	**sp.quantity of FC present in sewage**	**STP to which the drain is proposed to be connected after tapping**	**Compliance of STP (Norms given by NGT/MoEF)**	**Status of land allotted for STP**	**Status of funds provided for the STP**	**Timeline for making the STP functional**	**Timeline for completing the household connectivity to that STP**
70	**Drain at Akhash Ganga**	Hooghly	DRAIN	BOD-42mg/l,COD-118mg/l,FC-77000MNP/100ml	77000	Untapped	2	0%	0%	2	77000MNP/100ml	Proposal for engagement of consultant for preparation of DPR is under considaration. (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
71	**Hastings Ghat Drain, Rishra**	Hooghly	DRAIN	BOD-48mg/l,COD 166mg/l,FC-2.7x10^4	27000	Untapped	45.5	0%	0%	45.50	2.7x10^4MNP/100ml	DPR preparation work is under progress. Work is being delayed due to non- availability of land.Alernative technology is being explored.	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
72	**Ramkrishna Mullick Ghat, Howrah**	Howrah	DRAIN	BOD-64mg/l,COD 140mg/l,FC-4x10^5MNP/100ml	400000	Untapped	10.2	0%	0%	10.2	4x10^5MNP/100ml	Engagement of consultant for preparation of DPR is under process. (KMDA)	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
73	**Champdany Ferry Ghat/Paolghat drain**	Hooghly	DRAIN	BOD-67mg/l,COD 97mg/l,FC-4.9x10^7mnp/100ml	49000000	Untapped	3.26	0%	0%	3.3	4.9x10^7mnp/100ml	DPR is under process but it could not be submitted due to lack of NOC for MPS land. Alernative technology is being explored.	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
74	**DVC Canal**	Hooghly	Canal	BOD-73mg/l,COD 187mg/l,FC-1.3x10^6MNP/100ml	1300000	Untapped	72.52	0%	0%	72.52	1.3x10^6MNP/100ml	DPR preparation work is under progress. Work is being delayed due to non- availability of land. Alernative technology is being explored.	Proposed STP will be MoEF norms compliant	Identification of land is under process	NMCG/State	2years from the date of Work Order	Does not arise as DPR is under preparation
75	**Drain between Pratapnagar Rajbari, Jaggatdal**	North 24 Parganas	DRAIN	BOD-86mg/l,COD 189mg/l,FC-2x10^6MNP/100ml	2000000	Untapped	1.73	0%	0%	1.73	2x10^6MNP/100ml	Engagement of consultant for preparation of DPR is under process.	MoEF	Identification of land is under process	NMCG/State	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
76	**Bagh Khal, Rishra**	Hooghly	KHAL	BOD-102mg/l,COD-217mg/l,FC-2.6x10^7MNP/100ml	26000000	Untapped	65.52	0%	0%	65.52	2.6x10^7MNP/100ml	DPR preparation work is under progress. Work is being delayed due to non- availability of land. Alernative technology is being explored.	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
77	**Azimganj**	Murshidabad	DRAIN	BOD-116mg/l,COD 384mg/l,FC-1.3x10^3MNP/100ml	1300	Untapped	1.14	0%	0%	1.14	1.3x10^3MNP/100ml	Preparation of DPR is under process. (KMDA)	MoEF	AVALABLE	NMCG/State	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
78	**Bhatpara Drain**	North 24 Parganas	DRAIN	BOD-133mg/l,COD 293mg/l,FC-2.4x10^6MNP/100ml	2400000	Untapped	8.7	0%	0%	8.7	2.4x10^6MNP/100ml	Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
79	**Baranagar/ Kuthighata Khal**	North 24 Parganas	Khal	BOD-157mg/l,COD 347mg/l,FC-3x10^6MNP/100ml	3000000	Untapped	Discharge measurment is under process.					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
80	**Kumar Khali**	Howrah	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
81	**New Bagher khal**	North 24 Parganas	Khal	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					DPR preparation is under progress and will be submitted shortly. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2years from the issuing work order.	Does not arise as DPR is under preparation
82	**101, Foreshore Road Drain, Mowrah**	Howrah	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
83	**Drain at Halisahar Municipality**	North 24 Parganas	DRAIN	Water quality Report awaited from WBPCB		Untapped	DO					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation

SL. No.	I	II	III	IV	V	VI	VII	VIII	IX	X	XI	XII	XIII	XV	XVI	XVII	XVIII
	Name of Drain/Canals/Khals	**District/Town**	**Nature of drains/Canals / Khals**	**water quality analysis– heavy metals**	**Fecal coliform (MPN/100 ml)**	**If tapped or untapped**	**Quantity of sewage discharged from the drain (MLD)**	**Total quantity sewage diverted and to be diverted (%) to STP**	**Utilization**	**Balance qty**	**sp.quantity of FC present in sewage**	**STP to which the drain is proposed to be connected after tapping**	**Compliance of STP (Norms given by NGT/MoEF)**	**Status of land allotted for STP**	**Status of funds provided for the STP**	**Timeline for making the STP functional**	**Timeline for completing the household connectivity to that STP**
84	**Drain at Dadu Ram ghat, Naihati**	North 24 Parganas	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
85	**Drain at Ramghat Naihati**	North 24 Parganas	DRAIN	Water quality Report awaited from WBPCB		Untapped	DO					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG	2 years from the date of issuance of the work order.	Does not arise as DPR is under preparation
86	**Botanical Garden -I, Kolkata**	Howrah	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
87	**Botanical Garden -II, Kolkata**	Howrah	DRAIN	Water quality Report awaited from WBPCB		Untapped	DO					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
88	**Telini para drain**	Hooghly	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Proposal for engagement of consultant for preparation of DPR is under considaration. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
89	**Rangamati More**	Howrah	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Engagement of consultant for preparation of DPR is under process. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
90	**Drain at Panchu Dutta ghat**	Hooghly	DRAIN	Water quality Report awaited from WBPCB		Untapped	Discharge measurment is under process.					Proposal for engagement of consultant for preparation of DPR is under considaration. (KMDA)	MoEF	Identification of land is under process	NMCG/State	2 years from the date of Work Order	Does not arise as DPR is under preparation
91	**Dhanketikhal, Garden Reach**	**Kolkata**	Khal	BOD-124mg/l,l,FC-14000000MPN/100ml	Present	Bar Screen attached for arresting floating material	60	Full Quantlty to be diverted into the newly under construction	None	NA	14000000 MPN/100ml	Now under construction Garden Reach STP	Will be Complied	Available KMC own land	NMCG	24 months since 21/10/2024	Within the project period
92	**Tolly Nullah (Adi Ganga)**	**Kolkata**	Canal	Considered under Adi-Ganga Rejuvination STP projects, where presently site mobilisation work is under progress													
93	**Drain near Howrah bridge (Jagannath Ghat)**	**Kolkata**	Storm outfall	BOD-48mg/l,l,FC-1100000MPN/100ml	Present	**Tapped**	123	100%	None	NIL	1100000 MPN/100ml	East Kolkata Wetland	Complied as per WBPCB	No	No	Functional	Connected
94	**Cossipore Khal (Ratan Babu Ghat)**	**Kolkata**	Storm outfall	BOD-90 mg/l,l,FC-11000000 MPN/100ml	Present	**Tapped**	127	100%	None	NIL	11000000 MPN/100ml	Existing Bangur STP	Complied (As per design standard CPHEEO established in 1993	No	No	Functional	Connected
95	**Nimtala Burnning Ghat**	**Kolkata**	Storm outfall	Analysis is under process	Present	**Tapped**	No	100%	None	NIL	Analysis is under process	East Kolkata Wetland	Complied as per WBPCB	No	No	Functional	Connected
96	**Kanchantala -I**	**Kolkata**	Outfall	BOD-5 mg/l,l,FC-700000 MPN/100ml	Present	Untapped	73.1	0%	None	NIL	700000 MPN/100ml	DPR is under preparation stage for tapping & further treatment					
97	**Kanchantala -II**	**Kolkata**	Outfall	BOD-35 mg/l,l,FC-1400000 MPN/100ml	Present	Untapped	15.28	0%	None	NIL	1400000 MPN/100ml						
98	**Kanchantala -III**	**Kolkata**	Outfall	BOD-10 mg/l,l,FC-220000 MPN/100ml	Present	Untapped	74.06	0%	None	NIL	220000 MPN/100ml						
99	**Chitpur Ghat khal**	**Kolkata**	Planned to be considered for tapping & further treatment as BOD is low but FC is present.														

*** Kindly note that this report has been compiled as per information and data received officialy from Executing Agencies (KMDA/KMC).**

Engagement of consultant for untapped drains falling in River Ganga in KMA & non-KMA area is under process from KMDA, MED and Municipalities.

WEST BENGAL POLLUTION CONTROL BOARD

Water Quality of Polluted River stretches of 17 rivers in West Bengal during September, 2025

Priority	River	Stations	pH (Unit)	(DO) (mg/l)	BOD (mg/l)	Total Coliform (MPN/100ml)	Fecal Coliform (MPN/ 100ml)	Fecal Streptococci (MPN/100ml)
I	Mahananda	Sliguri (Upstream)	7.4	6.7	1.3	14000	7900	33
	Mahananda	Ramghat(Downstream)	6.9	6.8	2.1	170000	94000	3400
II	Vidyadhari	Haroa bridge (upstream)	7.51	0.5	12.25	350000	130000	5400
	Vidyadhari	Malancha (downstream)	7.29	1.1	8.33	13000	4500	490
II	Churni	Downstream of Ranaghat town	7.33	2.6	3.5	17000	4900	390
	Churni	Majhdia	7.3	2.4	4.7	7900	2400	330
III	Matha bhanga	Gobindapur	7.21	2	4.85	24000	7900	700
IV	Ganga	Farakka	7.11	7.2	2.4	2400	790	130
	Ganga	Farakka	7.09	7.5	2.7	3500	1300	170
	Ganga	Khagra	7.01	7.5	2	5400	2400	130
	Ganga	Khagra	7.17	7.3	2.9	3500	1100	230
	Ganga	Baharampore	6.91	7.4	2.05	22000	7000	490
	Ganga	Baharampore	7.06	7.3	2.85	13000	7900	330
	Ganga	Gorabazar	6.99	7.6	1.9	24000	7900	460
	Ganga	Gorabazar	7.21	7.4	2.8	17000	7000	220
	Ganga	Nabadip	7.09	6.9	2.9	4900	1100	230
	Ganga	Nabadip	7.17	6.2	2.8	3300	1400	170
	Ganga	Tribeni	7.21	6.8	2.7	7000	2300	330
	Ganga	Tribeni	7.17	6.8	2.8	4900	2300	330
	Ganga	Palta Shitalatala	7.04	5.3	2.7	13000	5400	490
	Ganga	Palta Shitalatala	7.09	7.4	2.85	17000	7900	460
	Ganga	Palta,	6.97	5.3	2.8	17000	9200	700
	Ganga	Palta	6.99	7.4	2.8	17000	7000	330
	Ganga	Serampore	7.21	5.4	2.85	79000	22000	1300
	Ganga	Serampore	7.29	7.3	2.95	70000	13000	1700
	Ganga	Dakshmineswar	7.1	5.1	2.65	240000	46000	3500
	Ganga	Dakshmineswar	7.35	5.2	2.8	140000	70000	1700
	Ganga	Garden reach	7.21	5.2	2.8	79000	17000	5400
	Ganga	Garden reach	7.12	6.1	2.9	94000	58000	3500
	Ganga	Howrah-shivpur	7.13	5.2	2.75	70000	13000	1700
	Ganga	Howrah-shivpur	7.11	5.7	2.8	84000	40000	3500
	Ganga	Uluberia,	7.24	5.3	2.8	63000	49000	2400
	Ganga	Uluberia,	7	5.1	2.85	54000	7000	3500
	Ganga	Durgachak near Pathikhali,	7.61	5.7	2.5	17000	7900	330
	Ganga	Durgachak near Pathikhali,	7.86	5.9	1.7	22000	11000	460
	Ganga	Diamond harbour,	7.15	5.1	2.7	2200	1100	270
	Ganga	Diamond harbour,	7.31	5.1	2.8	1700	930	140

Water Quality of Polluted River stretches of 17 rivers in West Bengal during September, 2025

Priority	River	Stations	pH (Unit)	(DO) (mg/l)	BOD (mg/l)	Total Coliform (MPN/100ml)	Fecal Coliform (MPN/ 100ml)	Fecal Streptococci (MPN/100ml)
IV	KANSI	Downstream at Midnapore	7.48	7.2	1.2	9400	4900	200
IV	JALANGI,	Downstream of Krishnanagar	7.04	5.3	2.2	4900	1700	130
V	Damodar	Dishergarh	7.83	8.8	2.8	4000	2200	32
	Damodar	IISCO near Dhenna Village	7.77	8.2	2.85	3400	1700	24
	Damodar	Narainpur	7.75	7.5	2.6	2700	1700	27
	Damodar	Near Mujher Mana Village	7.65	7.6	3.05	2600	1400	17
	Damodar	Andal D/s	7.68	7.3	1.6	3300	2600	21
	Damodar	Andal U/s	7.69	7.7	2.75	4600	2100	26
	Damodar	Asansol U/s	7.65	8.2	2.1	3400	2700	17
	Damodar	Durgapur U/s	7.6	7.1	2.7	4000	3200	26
	Damodar	Raniganj D/s	7.6	7.4	2	7900	2700	33
	Damodar	Water intake point for Burdwan Town	7.74	7.7	1.6	4900	2200	22
V	Dwarka	Upstream of Tarapith at Sadhak Bamdeb ghat	7.76	7.5	2.95	11000	3400	33
	Dwarka,	Downstream of Tarapith Satighat	7.5	7.3	3.1	13000	4000	26
V	Barakar	Asansol	7.72	8	2.4	3200	2100	14
V	Rupnarayan	Geonkhali	7.26	5.2	2	14000	7000	210
	Rupnarayan	Kolaghat (Down Stream)	7.28	5.9	2.65	7900	4900	170
V	Dwarakeshwar	Bankura town	7.81	8.5	2.2	3900	3200	33
V	Teesta	At Jalpesh	7.5	6.2	2.3	3400	1700	13
	Teesta	At Sevoke	7.2	8.1	1.7	4700	1700	27

WEST BENGAL POLLUTION CONTROL BOARD

The following four rivers have been removed from this list of polluted River stretches based on improvement in water quality in 2022 compared to 2018.

Priority	River	Stations	pH (Unit)	(DO) (mg/l)	BOD (mg/l)	Total Coliform (MPN/ 100ml)	Fecal Coliform (MPN/100ml)	Fecal streptococci (MPN/100ml)
Delisted	Silabati	Ghatal (Downstream)	*8.37*	*8*	*1.55*	*6300*	*3300*	*110*
	Mayurakshi	Suri Town	*7.93*	*9.1*	*1.55*	*2600*	*1700*	*14*
	Kaljani	Downstream of Alipurduar	*7.48*	*7.5*	*1.5*	*17000*	*8000*	*94*
	Karola	Downstream of Jalpaiguri	*7.13*	*8.2*	*2*	*17000*	*8000*	*94*
Primary Water quality Criteria for bathing water			6.5-8.5	≥5	≤3		<2500	500

Note: Implementation of Polluted River Stretches Action Plan, presently the above four Rivers i.e., Silabati, Mayurakshi, Kaljani, Karola have been improved and is removed from the list. Therefore, Polluted River Stretches in West Bengal stands with 13 rivers.

Site Inspection Report.

Month- SEPTEMBER 2025

NAME OF THE EXECUTING AGENCY- GAP WING/W&S SECTOR, KMDA

1. Physical progress of the operational STPs.

Sl. No.	Location	ULB Jurisdiction	Capacity in MLD	Actual utilization at present	Reasons for underutilization if any	Status of installation of OCEMs	Status of House Connection (if any)	Incremental progress over the last visit
1	Bhatpara	Bhatpara	60.50	23.1	1. Due to pending work of house connection 2. The STPs are designed as per the year of 2044 projected population.	Not install till now	Total House connection 91000 MLD. Connection completed as on date 34910. DPR for balance house connection under progress.	NIL
2	Kalyani	Kalyani	21.00	10.15 & 9.22	NA	Not install till now	Present length of network = 260 km (Approx) L&T= about 48km, existing about 212km, network remaining = about 110 km. Number of house hold = 30000, house connection	NIL

Sl. No.	Location	ULB Jurisdiction	Capacity in MLD	Actual utilization at present	Reasons for underutilization if any	Status of installation of OCEMs	Status of House Connection (if any)	Incremental progress over the last visit
							done =18000, house connection remaining= 12000	
3	Gayeshpur	Gayeshpur	8.33	3.34	Inadequate house connection	Not install till now	Due to pending work of house connection 11575 nos. of HSC has been completed out of 15000 household. Gayeshpur Municipality is executing the work by engaging agencies through tender. Work is in progress	Sewage (Influent) quality has been decreased compared to previous month viz.September,2021 is 3.63 MLD.
4	Budge Budge	Budge Budge	9.3	8.91	Only for available drain connection	Not install till now	Total Connection 13200 House pit constructed -13348 nos IP constructed - 5368 Connection made to the source : 2384	Under O&M HDPE PIPELINE = 100 Mtr. Jack Push work : 10 Mtr. Manhole : 8 nos IP : 8 nos
5	Barrackpore	Barrackpore	24.0	8.41 & 2.68	Sewerage network could not been completed as the Local Municipal authority has barred the Sewerage network	Not install till now	"Barrackpore Municipality has completed about 25200 no House	Operation & Maintenance work for STP started

Sl. No.	Location	ULB Jurisdiction	Capacity in MLD	Actual utilization at present	Reasons for underutilization if any	Status of installation of OCEMs	Status of House Connection (if any)	Incremental progress over the last visit
					at present for the ensuing assembly poll and House connection work has not been completed. Presently sewage from the existing drains are being taken by I& D structures		connections out of 35000. Achieved Chamber up to 29.02.2024 is 40500 nos.	
6	Halisahar	Halisahar	16.0	10.53	a.House connection pending which executed from local ULB and about 600 nos house hold source connected out of total 32866 Nos. b.Some of the drains intercepted to collect water.	Not install till now	Due to pending work of house connection Total House connection needed 32866. Achieved Chamber nos 25941 Full completed 17142	Operation & Maintenance work for STP started.
7	Bandipur (Khardah)	Khardah	14.00	12.32	a. Necessary permission from railway to rectify/restore the leakage of rising main pipe yet not receive from the competent authority till to date.	Not install till now	NA	Operation & Maintenance work for STP started.
8	Garulia	Garulia	4	3.76	a. Irregular/inadequate pumping due pump break down etc may cause deficit in inlet	Not install till now	NA	Operation & Maintenance work for STP started.

Sl. No.	Location	ULB Jurisdiction	Capacity in MLD	Actual utilization at present	Reasons for underutilization if any	Status of installation of OCEMs	Status of House Connection (if any)	Incremental progress over the last visit
					discharge. b. Irregular cleaning of Debitola Pacha Khal from others authority causing chokage of inlet screen causing deficit in adequate inlet discharge.			
9	Naihati	Naihati	6.50	5.01	a. Irregular/inadequate pumping may cause deficit in inlet discharge. b. During dry season level of water reduces accordingly. c. Irregular cleaning of Lalbaba ghat darin and Ramghat drain from others authority causing chokage of inlet screen causing deficit in adequate inlet discharge.	Not install till now	NA	Operation & Maintenance work for STP started.
10	Naihati	Naihati	11.56	9.36	a.Irregular/inadequate pumping may cause defficit in inlet discharge. b. During dry season level of water reduces accordingly.	Not install till now	NA	Operation & Maintenance work for STP started.
11	Panihati	Panihati	12.00	11.12	a.Necessary permission from PWD to rectify/restore the	Not install till now	NA	Operation & Maintenance work for STP started.

Sl. No.	Location	ULB Jurisdiction	Capacity in MLD	Actual utilization at present	Reasons for underutilization if any	Status of installation of OCEMs	Status of House Connection (if any)	Incremental progress over the last visit
					leakage of rising main pipe yet not receivethe from the competent authority till to date.			
12	Titagarh	Titagarh	9.00	4.45&4.45	a. Irregular pumping and operation due to existing labour /operator/ worker issues.	Not install till now	NA	Operation & Maintenance work for STP started.
13	Baidyabati	Baidyabati	6.00	4.89	-	Not install till now	NA	Operation & Maintenance work for STP started.
14	Bhadreswar	Bhadreswar	7.60	3.48	-	Not install till now	NA	Operation & Maintenance work for STP started.
15	Chandannagar	Chandannagar	22.66	5.80&1.45	During dry season level of water reduces accordingly.	Not install till now	NA	Operation & Maintenance work for STP started.
16	Bansberia	Bansberia	0.30	.28	NA	Not install till now	NA	Operation & Maintenance work for STP started.
17	Uttarpara – Kotrung and Konnagar	Kanaipur Gram Panchayet	22.00	17.09	NA	Not install till now	NA	Trial run started from 27.07.2022) cleaning, repairing & renovtion of network- is under progress.
18	Nabadwip	Nabadwip	9.50 MLD	5.24	Actual capacity will reached in the year 2051	Installed	NA	O&M started from 01/07/2022
19	Kanchrapara	Kanchrapara	18.00 MLD	8.73	-	Not install till now		Trial & Run started from 01/09/2022
20	Sreenathpur, Ranaghat	Ranaghat	4.0 MLD	2.76				

Sl. No.	Location	ULB Jurisdiction	Capacity in MLD	Actual utilization at present	Reasons for underutilization if any	Status of installation of OCEMs	Status of House Connection (if any)	Incremental progress over the last visit
21	Silver Jubliee Road, Ranaghat	Ranaghat	2.6 MLD	2.09				

SITE VISIT PHOTOGRAPH OF STP UNDER OPERATION& MAINTENANCE STAGE IN SEPTEMBER-2025

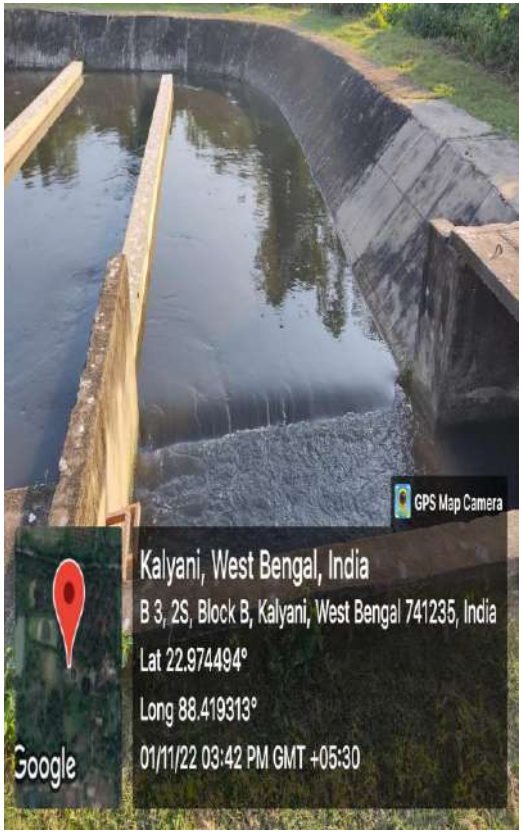

KALYANI

BARRACKPORE

Chlorination Building

GAYESHPUR

HALISAHAR

Budge budge

NAIHATI

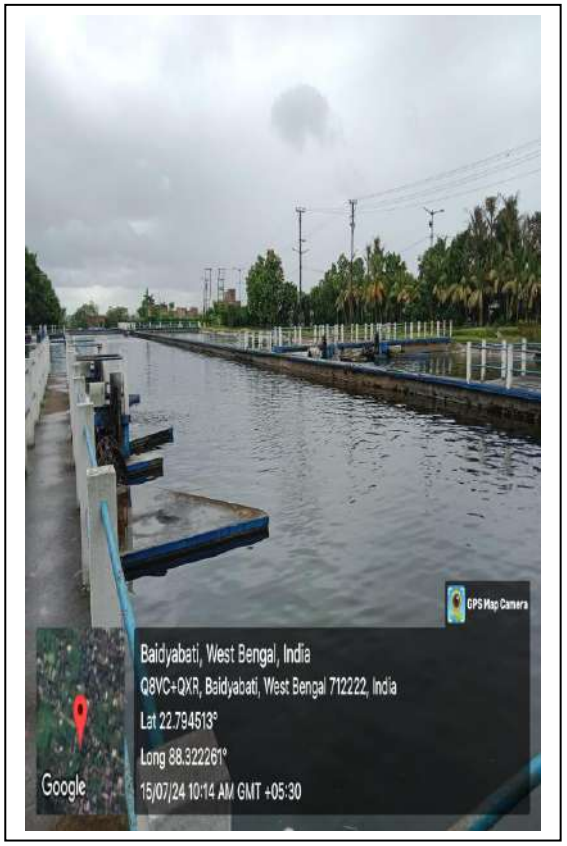

Baidyabati

Bhadreswar

Chandannagore

NABADWIP

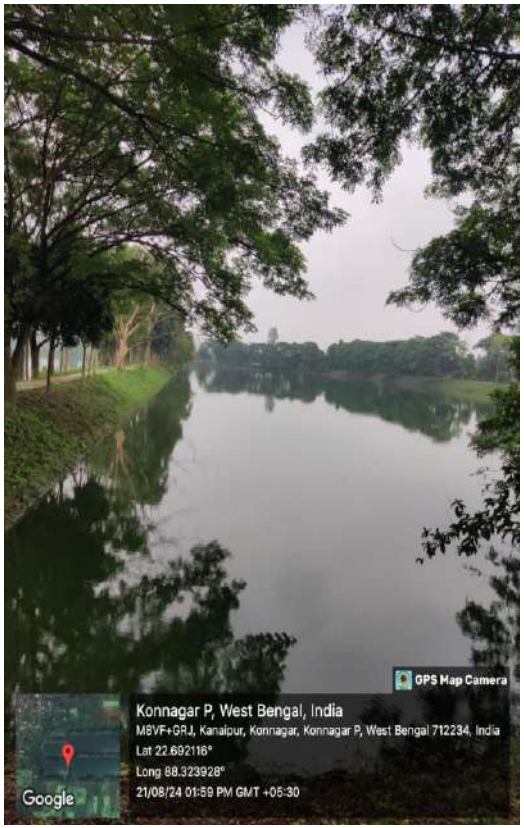

Kanaipur STP

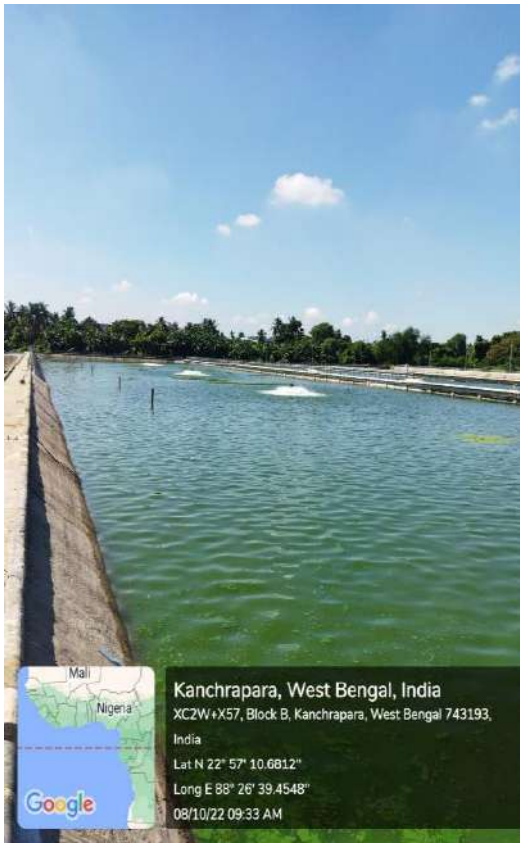

KACHRAPARA

1. Status of the non-operational STPs.

Sl. No	Location	ULB Jurisdiction	Capacity in MLD	Installed in (year) Non-functional since (year)	Current initiative towards functionalization, if any	Present Status	Incremental progress over the last visit
1.	Serampore	Serampore	18.6	Installed-1990 Non functional-2011	DPR for Augmentation and up gradation of the STP is under process	Non-functional	Nil
2.	Champdani	Champdani	1.00	Installed-2009 Non-functional-2018	DPR for Augmentation and up gradation of the STP is under process	Non-functional	Nil

2. STPs under different stages of execution.

Sl. No.	Location	ULB jurisdiction	Proposed capacity in MLD	Timeline for completion	Present Status	Incremental progress over the last visit
1	Hooghly	Hooghly	26.50	DEC 25	progress as on 30.09.2025 For Civil parts =89.80% , E&M Part= 97.00% Overall progress =92.300% (Including E&M) 1) Sewrage network design as well as structral design completed and work going on. 2) Admin building Finishing work Complited. 3) 500 dia D.I pipe laying almost ompleted &Laying of 600 mm dia D.I pipe going on& gravity line going on. 4) MPS work Completed.	
2	Jangipur	Jangipur	8.00 MLD	SEP 25	Jangipur: i .	

Sl. No.	Location	ULB jurisdiction	Proposed capacity in MLD	Timeline for completion	Present Status	Incremental progress over the last visit
					Jangipur: Construction of STP Physical progress- Civil Work 98%. Completed i) SBR Basin: SBR wall is under progress.-Civil-99.25% Completed. ii) Inlet Chamber: Civil- 98.6% Completed. iii)MCC- Blower Room: Civil Work-99% Completed. iv) Centrifuge House of STP: Civil work-99% Completed. v) Chlorination Building : Civil work-98% Completed. vi) CCT : Civil Work-98.1% Completed. vii) MPS- 1 no. 100% civil work Completed viii) Boundary Wall- Civil work-70%	

Sl. No.	Location	ULB jurisdiction	Proposed capacity in MLD	Timeline for completion	Present Status	Incremental progress over the last visit
3	Raghunathganj	Jangipur	5.00 MLD	sep 25	AAs per proposed revised BOQ Overall Physical Progress upto 30.09.2025 :85 %(Considering Construction of STP Physical progress- Civil Work 88.00 %. Completed i) SBR Basin: SBR wall is under progress.-Civil-99% Completed. ii) Inlet Chamber: Civil- 98.5% Completed. iii)MCC- Blower Room: Civil Work-96% Completed. iv) Centrifuge House of STP: Civil work-98% Completed. v) Chlorination Building : Civil work-98% Completed. vi) CCT : Civil Work-98% Completed. vii) MPS- 1 no. 90% civil work Completed viii) Boundary Wall- Civil work-70%	
4	Berhampore	Berhampore	3.50 MLD	sep 25	Physical Progress of STP upto 30.09.2025 : 80.0%(Considering actual progress as received from E&M Sector) Construction of STP Physical progress- Civil Work 75% Completed. i) SBR Basin: Civil Work-97% Completed. ii) MPS- 50% Completed iii) Centrifuse House- 90% Completed iv) Inlet Chamber- 97% Completed v) MCC Blower Room- 86% Completed. vi) Chlorination Building: 35% Completed vii) Boundary Wall- Civil work- 120 m/240m Completed LS at Kapiler Math: Civil work Progress-70% LS near DM Bungalow: Civil work Progress-60% UGLS at Battala: 90% civil work completed. . .	

Sl. No.	Location	ULB jurisdiction	Proposed capacity in MLD	Timeline for completion	Present Status	Incremental progress over the last visit
5	Bally (Kona)	Jagacha Gram Panchayet	62.00		Overall progress: 97.54% STP: 99.83% Network: Manhole Rising 98% LS MPS Repair 90% Desilting 97% Pipe Laying 97%Pipe Laying 98%	
6	Arupara	Howrah	65.00		Overall progress: 94.94% STP :99.86% Network: Manhole Rising 99% LS MPS Repair 98%	
7	Mathkal	Baranagar	60.00		Overall progress: 96.08% STP : 99.91% Network: Manhole Rising 96% LS MPS Repair 95% Desilting 98% Pipe Laying 94%	
8	Maheshtala	Maheshtala	35.00	31.08.25 (Including trial run)	Total:-100% completed till 30-09-25 consisting of :- 1. 100% of STP Civil Process unit. 2. 100% of Office Building & Staff Quarter. 3. 100% of Supply of Electromechanical Items. 4. 99.493% of Associate Infra Civil Structure & pipe Laying works. SBR Basin:-Platform & wall 100% completed. Hydrotesting of Basin-1 ,2,3,4 completed. CCT:- 100% completeed SHU:- 100% completed. PTU:- 100 % completed. Admin Building:- 100% completed Staff Quarter:- 100% Completed	

Sl. No.	Location	ULB jurisdiction	Proposed capacity in MLD	Timeline for completion	Present Status	Incremental progress over the last visit
					Pipelaying:- Pipe Laying , Hydrotesting & Road Restiration WIP. LS2- Raft 99% completed. Well Wall Completed. Brick Work & Plaster WIP. LS-2A:- 100% Civil completed. LS-3:- 100% completed. Boundary Wall WIP..	
9	North Barrackpore	North Barrackpore	38.00	OCT-2025	Total:-83.947% completed till 30-09-2025 consisting of :- SBR Basin:- Basin wall and walkway 100% completed. Other miscellaneous works has been going on. E&M work is in progress. Primary Unit: Miscellaneous Work has been going on. E&M work is in progress. SHU: Miscellaneous Work has been going on. CCT: Miscellaneous Work has been going on. STP Mechanical Procurements - 100% Completed. STP Electrical Procurements - 96% Completed. STP Mechanical Erection - 78% Completed. STP Electrical Erection - 58% Completed. BOUNDARY WALL: Excavation including Levelling & PCC work 95% completed, Sub Structure and RCC Super Structure work 80% completed, Brick Work & Plaster-60%. ADMIN BUILDING: Miscellaneous works has been going on. HT SUBSTATION : Miscellaneous works has been going on. 700mm Dia having length of 110 metres (Trenchless /Open Cut Method) - work in Progress. Construction of New 11 MLD LS at D-Drain (Civil Part) - up to Raft 100% Completed.	

SL.NO	Location	ULB Jurisdiction	Proposed capacity in MLD	Timeline for completion	Present status	Incremental progress over the last visit
10	Chakdaha	Nadia	15	SEP 25	Total:-79.60% completed till 30-09-2025 consisting of :- SBR Basin:- Basin wall and walkway 100% completed. Other miscellaneous works has been going on. E&M work is in progress. Primary Unit:- Miscellaneous Work has been going on. E&M work is in progress. SHU:- Miscellaneous Work has been going on. CCT:- Miscellaneous Work has been going on. Boundary Wall -: i) PCC Work - 60% Completed. ii)RCC Work - 50% Completed. iii) Brick Work - 50%Completed. Mechanical Procurements - 85% Completed. Electrical Procurements - 40% Completed. Mechanical Erecation - 40% Completed. Electrical Erecation -15% Completed. MPS-: Intial Open Excavation including erection and fixing of cutting shoe-100% Completed, Construction of well sinking work 100% Completed.Plugging of Well, Boulder Filling etc 100% Completed.Bottom Raft Work 100 % Completed & Screen Channel work in Progress. LS-3: Intial Open Excavation including erection and fixing of cutting shoe-100% Completed, Construction of well sinking work 100% Completed.Plugging of Well, Boulder Filling etc 100% Completed. LS-4: Intial Open Excavation including erection and fixing of cutting shoe-100% Completed, Construction of well sinking work 100% Completed..Plugging of Well, Boulder Filling etc 100% Completed.Bottom Raft	

					100% Completed.Column Work 100% Completed & top Slab work in Progress. ADMIN BUILDING-: Miscellaneous works has been going on. Gravity Sewerage-70% Completed(6715M/4580M). Rising Main 78 % Completed(4900M/3840M).	
11	**South DumDum**	**North 24PGS**	**27**	**Oct-27**	**Work Order issued**	
12	**Khardah**	**North 24PGS**	**8.15**	**12.03.27**	**10% (overall progress)**	
13	**Santragachi STP**	**Howrah**	**1.5**	**11.09.25**	**12%(overall progress)**	
14	**Bansberia**	Hooghly	**15 KLD**	**23.07.25**	**0.35%(overall progress)**	

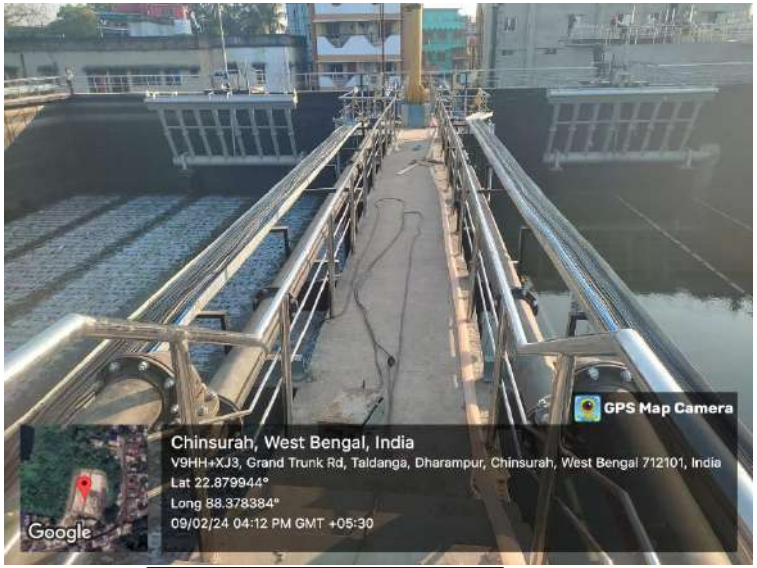

Hooghly Chinsurah

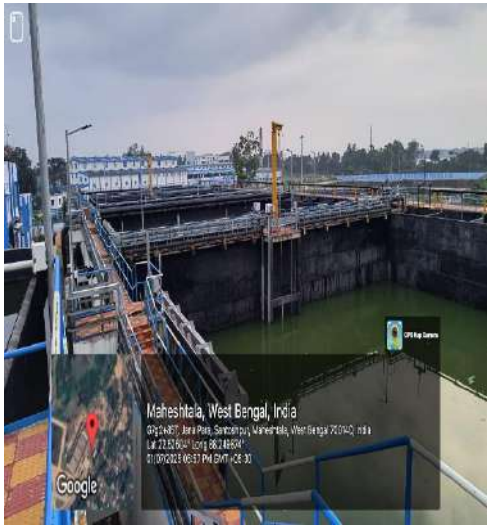

Maheshtala

CHAKDAHA

BEHARAMPORE STP SITE

RAGHUNATHGUNJ STP SITE

JANGIPUR

BALLY

ARUPARA

BARAHANAGAR

NORTH BARRACKPORE

3. Status of PollutedDrains discharging to river Ganga.

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
1.	Jangipur Drain	Jangipur	0.8 MLD	Presently in-situ treatment work is ongoing and in future it will be tapped under the ongoing Baharampore - Jangipur Interception & Diversion Project. Bar screen has already been installed.	YES	To be tapped under 8.0MLD Jangipur STP.	Dosing and Desilting work is in progress
2.	Halisahar Drain	Halisahar	22..94 MLD	To be intercepted in the Halisahar STP (16.00 MLD capacity) which is under execution.	NO	On- line treatment proposal sent.	Installation of gate completed.
3.	Garifa Drain-South / Ramaghat Open pucca drain	Garifa	4.85 MLD	Considered to be connected with the STP 1 (6.50 MLD capacity) at Naihati in rejuvenation works under North 24 Parganas district.	NO	Partially tapped under Naihati STP (WSP)	Lock Gate Installed
4.	Garifa Drain-North	Garifa	10.36 MLD	Considered to be connected with the STP 1 (6.50 MLD capacity) at Naihati in rejuvenation works under North 24 Parganas district.	NO	Partially tapped under Naihati STP (WSP)	Lock Gate Installed..
5.	Thanar Khal	Naihati	10.18 MLD	Considered to be connected with the STP 2 (11.56 MLD capacity) at Naihatiin rejuvenation works under North 24 Parganas district.	NO	Partially tapped under Naihati STP (ASP)	Lock Gate Installed completed.
6.	Imambara Khal	Hooghly-Chinsurah	5.24 MLD	Will be tapped in Hooghly Chinsurah STP, under construction.	No	Will be trapped in Hooghly Chinsurah STP,under	NIL

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
						construction.	
7.	Chinsurah-Majir Rasta Drain	Hooghly-Chinsurah	17.12 MLD	Consider in Hooghly - Chinsurah Revised DPR	No	Will be trapped in Hooghly Chinsurah STP, under construction.	NIL
8.	ChandniGhat Drain	Hooghly-Chinsurah	25.75 MLD	Consider in Hooghly - Chinsurah Revised DPR	No	Will be trapped in Hooghly Chinsurah STP,under construction	NIL
9.	DebitalaPancha Khal	Garulia	46.36 MLD	Considered to be connected with the STP (7.90 MLD capacity) at Garulia in rejuvenation works under North 24 Parganas district.	No	Partially tapped under Garulia STP (wsp)	NIL
10.	Serampore/Bhagirathi Drain	Serampore	91.88	Planned to be diverted to the existing Serampore STP which will be renovated after the finalization of Tender	No	In house DPR is ready. But it could not be submitted due to lack of NOC of railway crossing from South Eastern Rail.	Nil
11.	Chatra Khal	Serampore	76.30	Planned to be diverted to the existing Serampore STP which will be renovated after the finalization of Tender	No	DO	NA
12.	Barrackpore Khal (S. P. Banglow)	North Barrackpore	4.87 MLD	Considered to be connected with the STP 1 (6.50 MLD capacity) at North Barrackpore. DPR submitted to	No	To be tapped in the proposed 8 MLD STP of Monirampur.	NIL

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
				NMCG on 22.07.2020 for approval.			
13.	Gandhi Ghat Drain	Barrackpore	4.07 MLD	To be intercepted in the Barrackpore STP (6.00 MLD capacity) which is under execuation.	NO	Tapped under 6 MLD STP Barrackpur.	NIL
14.	Dhobi Ghat Drain	North Barrackpore	0.47 MLD	Considered to be connected with the STP 1 (6.50 MLD capacity) at North Barrackpore. DPR submitted to NMCG on 22.07.2020 for approval.	No	To be tapped in the proposed 8 MLD STP of Monirampur.	NIL
15.	Titagarh Drain (BishalaxmiGhat)	Titagarh	5.79 MLD	Considered to be connected with the STP (14.10 MLD capacity) at Khardah-Bandipur in rejuvenation works under North 24 Parganas district.	NO	Partially tapped under Bandipur STP.	NIL
16.	Hasting Ghat Drain	Rishra	45.50 MLD	Considered to be connected with the existing LS at Rishra Hooghly district.	Considered to be connect at LS at rishra	Consultant engaged for DPR.DPR shall be submitted by 14.09.24	Financial evaluation in progress
17.	DewangaziGhat Drain	Bally	20.67 MLD	Considered in Kona STP (62.00 MLD) at Bally which shall be executed by Ganga STP Project Pvt. Ltd. under HAM.	Not yet	On-line treatment proposal sent.	NIL
18.	JagatnathGhat Drain-1	Belur	4.29 MLD	Considered in Kona STP (62.00 MLD) at Bally which shall be executed by Ganga STP Project Pvt. Ltd. under HAM.	No	To be trapped under HBB HAM.	NIL

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
19.	Kamarhati Drain @ Jute Mill	Baranagar	42.48 MLD	Considered in Kamarhati-Baranagar STP (60.00 MLD) at Baranagar which shall be executed by Ganga STP Project Pvt. Ltd. under HAM	No	Partially tapped under 60MLD Baranagar STP under HAM mode.	NIL
20.	Kamarhati Drain @ PB Ghat	Panihati	4.76 MLD	Considered to be connected with the STP (12.00 MLD capacity) at Panihati in rejuvenation works under North 24 Parganas district.	No	Partially tapped under Panihati STP.	NIL
21.	Kuthighat Drain/ Baranagar Khal	Baranagar	10.84 MLD	Considered in Kamarhati-Baranagar STP (60.00 MLD) at Baranagar which shall be executed by Ganga STP Project Pvt. Ltd. under HAM.	No	Consultant to be engaged.	NIL
22.	Chitpur Ghat Khal/ Circular Canal	Chitpur	497.65 MLD	KMC area connected with Bangur STP & EKW. (KMC)	No	Under KMC	Under KMC
23.	Cossipore / Kashipur drain	Cossipore	15.09 MLD	Connected to Bangur STP. (KMC)	NO	Under KMC	Under KMC
24.	Telka Ghat Drain	Howrah	10.55 MLD	Considered in Arupara STP (65.00 MLD) at Howrah which shall be executed by Ganga STP Project Pvt. Ltd. under HAM	NO	Engagement of consultant is under process	Nil
25.	Ramkrishna Ghat Drain	Howrah	10.20 MLD	Considered in Arupara STP (65.00 MLD) at Howrah which shall be executed by Ganga STP Project Pvt. Ltd. under HAM	NO	Engagement of consultant is under process	Nil

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
26.	101,Foreshore Road Drain	Howrah	0.00 MLD	Considered in Arupara STP (65.00 MLD) at Howrah which shall be executed by Ganga STP Project Pvt. Ltd. under HAM	NO	Engagement of consultant is under process	Nil
27.	Tolly Nala	Dahighat, Hastings, Kolkata	252.49 MLD	3 new STPs are proposed (KMC)	Under KMC	Tolly'sNullah is guarded with 8 floating garbage arrester nets at different locations to arrest the floating materials for the ease of removing the same from reaching to the River.	Under KMC
28.	Nimtala Burning Ghat Drain	NimtalaGhat, Kolkata	35.93 MLD	This is combined sewer overflow line. Thereis a penstock gate arrangement to discharge diluted sewage in river. DWF is taken to EKW through a system of sewer network,pumping stations and canals. (KMC).	NO	Under KMC	NIL
29.	Dhankheti/ PB Ghat Khal	Metiabrutz, Kolkata	26.09 MLD	Draft DPR for I&D submitted to NMCG for approval on 30.03.2019. 3 New STPs are proposed.	Under KMC	Dhankheti Khal is guarded with 3bar screens at different locations to arrest the floating materials for the ease of removing the same from reaching to the	Under KMC

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
						River.	
30.	Shibpur Burning Ghat Drain	Shibpur-Howrah	22.79 MLD	Considered in Arupara STP (65.00 MLD) at Howrah which shall be executed by Ganga STP Project Pvt. Ltd. under HAM.	No	Engagement of consultant is under process	Nil
31.	Bagherkhal	Kanchrapara	55.65MLD	To be diverted to the ongoing Kancrapara STP	No	Already Tapped	Nil
32.	130 Foreshore Road Drain	Howrah	0.0069 MLD	Considered in Arupara STP (65.00 MLD) at Howrah which shall be executed by Ganga STP Project Pvt. Ltd. under HAM	No	Engagement of consultant is under process	Nil
33.	Alliance Mill Drain	Bhatpara	1.38 MLD	Diverted to 31 MLD STP at Jaggadal	No	Already tapped.	NA
34.	Rosbara Khal	Bandel	9.11 MLD	Proposed to be connected with the STP (26.50 MLD capacity) at Hooghly - Chinsurah Municipality. DPR approved by NMCG on 28.08.2020.	No	Will be tapped in Hooghly chinsurah STP, under construction.	Nil
35.	Old Muni Khali Khal	Mahestala	11.72 MLD	Considered in 35 MLD STP under Maheshtala HAM Project.	No	Construction of Interception &Diversion structure is in progress to tap the Khal with the STP.	
36.	Bhatpara Drain	Bhatpara	8.75 MLD	NO	NO		NIL

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
37.	Pratapnagar-Rajbari Drain	Bhatpara	35.3 MLD			DPR already sent to NMCG for approval	NIL
38.	Bhatpara-Open pucca drain	Bhatpara	61.89 MLD			Already been taken up by GAP sector KMDA	
39.	Bagh Khal	Rishra	65.52 MLD	NO	Tender invited for Preparation of DPR for Rishra Municipal Town in I&D with STP.	Consultant engaged for DPR.DPR shall be submitted by 14.09.24	Financial evaluation in progress
40.	Majher Char Khal	Kalyani	24.32 MLD	NO	This drain will receive 90% of its flow from Kalyani Town and therefore a disinfection unit proposed there.	DPR preparation under process.	NIL
41.	Champdani Ferry Ghat / PaolghatDrain	Chapdani	25.75 MLD	I&D work proposed after Augmentation/Up-gradation of existing STP at Serampore&Champdani Municipal town.	Tender Invited for preparation of DPR.	In house DPR is ready.But it could not be submitted due to lack of NOC for MPS land.	Financial evaluation in progress
42.	Khardah Khal	Khardah	105.60 MLD	NO	Drain with humungus capacity and flow will be treated as	Consultant engaged for DPR.DPRshall be submitted by 14.09.24.	Financial evaluation in progress

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
					separate canal/River		
43.	N.C. Pal Khal	Sankrail, Howrah	4.12 MLD	NO	Tender invited forPreparation of DPR for Howrah added zone in I&D with STP	To be tapped/DPR under tendering stage.	Financial evaluation in progress
44.	Saraswati Khal	Howrah	3.65 MLD	NO	Tender invited forPreparation of DPR for Howrah added zone in I&D with STP.	To be tapped/DPR under tendering stage.	NIL
45.	DhopaGhat Drain	Bansberia	7.31 MLD	NO	NO	Engagement of consultant is under process	NIL
46.	Chandannagar Drain	Chandannagar	0.4 MLD	Taken up into the STP at Chandannagar by I&D work	NO	Already tapped in chandannagar STP.	NIL
47.	Nazerganj Khal	Sankrail, Howrah	336.71 MLD	No	Preparation of DPR for Howrah added zone in I&D with STP	To be tapped/DPR under tendering stage.	Financial evaluation in progress
48.	ITC Triveni Drain	Hooghly	3.88 MLD	No	No	This drain carries discharge from ITC,tribeni. It is llocated under chandrahatty-2 panchyet.	Action plan of this drain has been submitted by WBPCB.

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
49.	Akhra Food Ghat drain (New Muni Khali Khal)	Mahestala	42.62 MLD	Considered in 35 MLD STP under Maheshtala HAM Project.	No	Construction of Interception &Diversion structure is in progress to tap the Khal with the STP.	Financial evaluation in progress
50.	DVC Canal	Champdani	72.52 MLD	No	No	Consultant engaged for DPR.DPR shall be submitted by 14.09.2024	
51.	Bazarpara–Garighat Drain / Sharenga drain	Sarenga-Sankrail, Howrah	87.20 MLD	No	No	To be tapped /DPR under tendering stage.	Action plan of this drain has been submitted by WBPCB.
52.	Baidyabati Drain	Baidyabati	128.77 MLD	No	Drain with humungus capacity and flow will be treated as separate canal/River	Consultant engaged for DPR.DPR shall be submitted by 14.09.2024	Financial evaluation in progress
53.	Bally Khal	Bally	264.52 MLD	NO	Drain with humongous capacity and flow will be treated as	Consultant engaged for DPR.DPR shall be submitted by 14.09.2024	Financial evaluation in progress

Sl no.	Name of drain	City/ Town of confluence point	Flow of Drain (MLD)	Any STP operation/planned in the catchment area or likely diversion/interceptionof the drain of STP	Any alternative Pollution Abetment measures taken	Present Status	Incremental progress over the last visit
					separate canal/River		
54.	Singhi More Khal	Sankrail, Howrah	14.20 MLD	NO	Tender invited forPreparation of DPR for Howrah added zone in I&D with STP	To be tapped/DPR under tendering stage.	Financial evaluation in progress
55.	BTPS Out fall Drain-I	Hooghly	49.03 MLD	No	No	This drain carries discharge from btps, tribeni. It is located under chandrahatty-2 Panchyet.	NIL
56.	Bagher Khal	Kanchrapara	55.65 MLD	To be diverted to the ongoing Kanchrapara STP	No	I&D work is under Progress	Nil

GARIFA SOUTH (RAM GHAT)

HALISAHAR DRAIN LOCKGATE

RANAGHAT

CHAKDAHA

4. DetailsofAlternateTreatmentTechnologybeingadoptedinthePollutedRiverStretches.

River name	Polluting drain	In-situ treatment details	MLD treated	Present Status	Incremental progress overthe lastvisit
GANGA	Jangipur Drain	Bio/Phyto remediation treatment process as interim measure has been taken up for Jangipur drain. Chemical dosing, desilting work etc. has been taken up periodically and as per the test result data it is expected, the desired test result for waste water may be achieved with the present treatment process.	0.2	Chemical dosing, desilting work etc. has been taken up periodically	Dosing and Desilting work is in progress

Date:10.01.2023

Name of Reporting Engineer: PRANTIK RAY

Designation: CHIEF ENGINEER

1437785/2021/O/o JS(UDMA)

Government of West Bengal

Department of Urban Development & Municipal Affairs
DF-8, Sector-I, Salt Lake,
Kolkata-700064

MemoNo. -UDMA-24011(99)/7/2021-JS(UDMA)

For smooth and efficient execution of the Projects taken under NamamiGange Schemes and with respect to the Action Plans submitted to the River Rejuvenation Committee in connection with the Polluted river stretches of the State (categorized as Priority I, II, III, IV,V Rivers), in respect of which the Department of UD & MA has to submit Reports and Returns on regular basis as mandated by Hon'ble NGT under different OAs, it is felt necessary now, that the concerned Engineers of the Executing Agencies- KMDA, KMC, MED, SJDA, SLRDC, ADDA, and others should make compulsorySiteVisitseverymonthandmonitortheprogressofdifferentProjectswhichinclude:

1. Visit to STPs under Construction, Rejuvenation, Renovation, Household Connections, laying of Sewer network including routinevisits.
2. VisittothePollutedDrainsandreviewtheprogressofdifferentPollutionAbetmentmeasuresbeingtaken.
3. Visit to the identified Polluted River stretches and review the progress of different Pollution Abetment measures being taken thereon and on theoutfalls.

Post Visit, a detailed report showing incremental Progress over the last visit along with good quality photographs to be submitted to the Department every month through proper channel in the enclosed Format. For this purpose, the controlling Head of the Executing Agency may compile all the site inspection Reports and submit the final Report accordingly. This mechanism will ensure quality monitoring and will expedite timely completion of different undergoing Projects.

This issue has an approval of the Higher Authorities.

Joint Secretary
UD&MA
Department

MemoNo. -UDMA-24011(99)/7/2021-JS(UDMA)

1. Municipal Commissioner, Kolkata Municipal Corporation,
2. CEOKMDA
3. CEOSJDA
4. CEOADDA
5. Chairman, Liquid Waste ManagementCommittee
6. Joint Secretary,KMDA
7. Secretary,MED
8. Chief Engineer, GAP Sector, KMDA
9. Chief Engineer,KMDA
10. Chief Engineer,MED
11. Additional Chief Engineer,SJDA
12. Additional Chief Engineer,ADDA
13. Special Engineer,SLRDC

14. OSD to the Municipal Commissioner,KMDA
15. PS to Hon'bleMIC
16. PS to PrincipalSecretary

Joint
SecretaryUD&MA
Department

	Status of per day Collection & Transportation of Fresh Waste of 128 ULBs of West Bengal up to September, 2025													
Sl No	**District**	**ULB**	**No. of ward**	**Population (Census 2011)**	**Per day Generation of fresh waste (TPD)**	**Door to door collection of fresh waste in no. of wards**		**Collection of segregated fresh waste in no. of wards**		**Quantity of fresh waste being collected & transported per day (TPD)**				**Tentative timeline for ensuring 100% segregation**
						Full	**Partial**	**Full**	**Partial**	**Wet Waste**	**Dry Waste**	**Mixed Waste**	**Total**	
1	Bankura	Bankura	24	1,37,386	**40**	24	0	16	8	15.95	5.45	18.60	40	Nov '25
2	Bankura	Bishnupur	19	67,783	**14**	11	8	8	11	5.00	3.00	4.00	12	Sept '25
3	Bankura	Sonamukhi	15	34,228	**9**	15	0	6	9	3.10	1.80	4.10	9	Sept '25
4	Paschim Burdwan	Asansol MC	106	11,56,387	**566**	84	22	27	79	200.00	130.00	211.00	541	Dec '25
5	Purba Burdwan	Barddhaman	35	3,14,638	**98**	35	0	23	12	44.44	42.00	11.56	98	Nov '25
6	Purba Burdwan	Dainhat	14	24,397	**7**	14	0	13	1	4.10	2.77	0.13	7	Sept '25
7	Paschim Burdwan	Durgapur MC	43	5,66,517	**244**	43	0	20	23	101.94	68.22	73.84	244	Nov '25
8	Purba Burdwan	Gushkara	16	35,374	**9**	16	0	15	1	4.00	3.50	1.50	9	Sept '25
9	Purba Burdwan	Kalna	18	56,722	**15**	18	0	18	0	7.00	5.64	2.30	15	Oct '25
10	Purba Burdwan	Katwa	20	81,615	**26**	20	0	16	4	12.33	6.77	6.90	26	Nov '25
11	Purba Burdwan	Memari	16	41,455	**11**	16	0	16	0	7.00	4.00	0.00	11	Achieved
12	Birbhum	Bolpur	22	80,210	**31**	22	0	10	12	14.00	9.00	8.00	31	Sept '25
13	Birbhum	Dubrajpur	16	38,041	**10**	16	0	16	0	5.80	3.56	0.64	10	Sept '25
14	Birbhum	Nalhati	16	41,244	**9**	14	2	14	2	3.60	1.90	2.50	8	Sept '25
15	Birbhum	Rampurhat	18	57,833	**15**	18	0	12	6	5.00	3.00	7.00	15	Sept '25
16	Birbhum	Sainthia	16	44608	**12**	16	0	10	6	6.31	3.16	2.53	12	Sept '25
17	Birbhum	Suri	21	90,314	**26**	21	0	8	13	10.50	5.00	10.50	26	Sept, 25
18	Cooch Behar	Cooch Behar	20	77935	**20**	20	0	2	18	6.50	2.00	11.50	20	Sept '25
19	Cooch Behar	Dinhata	16	36,124	**9**	16	0	16	0	6.00	2.50	0.50	9	Achieved
20	Cooch Behar	Haldibari	11	14,404	**4**	11	0	11	0	2.30	1.40	0.30	4	Oct,25
21	Cooch Behar	Mathabhanga	12	23,895	**9**	8	4	8	4	5.00	3.00	1.00	9	Sept '25
22	Cooch Behar	Mekhliganj	9	9,123	**5**	9	0	9	0	1.60	1.06	2.34	5	Sept '25
23	Cooch Behar	Tufanganj	12	20,998	**7**	12	0	12	0	4.38	1.75	0.88	7	Sept '25
24	Dakshin Dinajpur	Balurghat	25	1,51,299	**42**	25	0	25	0	23.20	13.40	5.40	42	Sept '25
25	Dakshin Dinajpur	Buniadpur	14	30183	**8**	14	0	10	4	4.00	2.00	2.00	8	Sept '25
26	Dakshin Dinajpur	Gangarampore	18	56,217	**14**	13	5	13	5	5.00	2.00	5.00	12	Sept '25
27	Darjeeling	Darjeeling	32	1,20,414	**24**	32	0	32	0	16.00	5.00	3.00	24	Dec '25
28	Kalimpong	Kalimpong	23	49,403	**13**	16	7	10	4	6.00	2.00	4.00	12	Nov'25
29	Darjeeling	Kurseong	20	42,346	**7**	20	0	10	10	2.55	1.27	3.18	7	Nov '25
30	Darjeeling	Mirik	9	11,513	**4**	6	3	6	3	2.00	1.00	1.00	4	Sept '25
31	Darjeeling	Siliguri MC	47	5,13,264	**297**	47	0	35	12	142.00	70.00	85.00	297	Dec, 25
32	Howrah	Uluberia	32	2,32,290	**86**	32	0	25	7	26.00	12.00	48.00	86	Sept, 25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
33	Hooghly	Arambagh	19	66,175	16	19	0	14	5	9.00	5.00	2.00	16	Sept, 25
34	Hooghly	Baidyabati	23	1,21,110	50	23	0	23	0	34.00	14.00	2.00	50	Sept,25
35	Hooghly	Bansberia	22	1,03,920	30	20	2	16	6	8.00	4.00	17.00	29	Sept, 25
36	Hooghly	Bhadreswar	22	1,01,477	26	22	0	22	0	16.25	9.75	0.00	26	Achieved
37	Hooghly	Champdany	22	1,11,251	19	20	2	18	4	9.00	4.00	5.00	18	Oct, 25
38	Hooghly	Chandannagore MC	33	1,66,867	52	33	0	31	2	27.00	17.00	8.00	52	Sept, 25
39	Hooghly	Dankuni	21	94,966	32	21	0	17	4	15.00	8.00	9.00	32	Nov '25
40	Hooghly	Hooghly Chinsurah	30	1,77,259	56	30	0	20	10	38.00	16.00	2.00	56	Nov, 25
41	Hooghly	Konnagar	20	76,172	26	20	0	19	1	15.29	7.65	3.06	26	Oct'25
42	Hooghly	Rishra	23	1,24,585	45	23	0	9	14	13.30	6.70	25.00	45	Sept '25
43	Hooghly	Serampore	29	1,83,339	95	29	0	16	13	30.00	21.00	44.00	95	Sept '25
44	Hooghly	Tarakeswar	15	30,947	10	15	0	15	0	5.00	3.00	2.00	10	Dec'25
45	Hooghly	Uttarpara Kotrung	24	1,62,386	72	24	0	24	0	47.00	25.00	0.00	72	Nov'25
46	Alipurduar	Alipurduar	20	65,232	21	15	5	15	5	11.50	7.50	1.00	20	Sept '25
47	Jalpaiguri	Dhupguri	16	44,719	7	1	15	1	15	2.00	1.00	1.00	4	Dec '25
48	Jalpaiguri	Jalpaiguri	25	1,07,341	38	25	0	25	0	22.80	13.24	1.96	38	Oct,25
49	Jalpaiguri	Mal	15	25,218	6	11	4	11	4	3.00	1.50	1.00	6	Sept '25
50	Malda	English Bazar	29	2,05,521	82	29	0	19	10	40.00	18.00	24.00	82	Nov '25
51	Malda	Old Malda	20	84,012	23	20	0	20	0	11.00	7.50	4.50	23	Sept '25
52	Murshidabad	Beldanga	14	29,182	7	14	0	14	0	2.60	1.60	2.80	7	Oct,25
53	Murshidabad	Berhampore	28	1,95,363	66	28	0	18	10	25.00	14.00	27.00	66	Nov '25
54	Murshidabad	Dhuliyan	21	95,706	18	21	0	0	21	6.00	4.00	13.00	23	Oct '25
55	Murshidabad	Domkal	21	1,21,927	24	21	0	6	15	9.00	5.40	9.60	24	Sept '25
56	Murshidabad	Jangipur	21	88,165	29	21	0	21	0	14.50	8.70	5.80	29	Sept, 25
57	Murshidabad	Jiaganj-Azimganj	17	51,790	15	9	8	2	15	6.00	2.00	5.00	13	Sept '25
58	Murshidabad	Kandi	18	55,632	12	15	3	15	3	7.00	2.50	1.50	11	Sept, 25
59	Murshidabad	Murshidabad	16	44,064	16	16	0	10	6	6.00	4.00	6.00	16	Nov '25
60	Nadia	Birnagar	14	30799	10	14	0	13	1	6.50	3.00	0.50	10	Sept,25
61	Nadia	Chakdah	21	95,203	19	6	15	6	3	5.00	3.00	6.00	14	Oct '25
62	Nadia	Cooper's Camp	12	18,839	5	12	0	8	4	2.50	1.00	1.50	5	Dec'25
63	Nadia	Gayeshpur	18	58,998	16	18	0	4	14	8.00	3.20	4.80	16	Sept '25
64	Nadia	Haringhata	17	45,953	12	5	12	0	0	0.00	0.00	9.00	9	Dec '25
65	Nadia	Kalyani	21	1,00,620	50	21	0	3	18	12.00	4.00	34.00	50	Sept '25
66	Nadia	Krishnanagar	25	1,53,062	90	25	0	21	4	50.00	24.00	16.00	90	Dec'25
67	Nadia	Nabadwip	24	1,25,528	36	24	0	24	0	18.60	12.00	5.40	36	Dec'25
68	Nadia	Ranaghat	20	75,365	20	20	0	12	8	10.00	6.00	4.00	20	Sept, 25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
69	Nadia	Santipur	24	1,51,777	40	24	0	16	8	18.00	8.00	14.00	40	Sept '25
70	Nadia	Taherpur	13	20,894	5	13	0	11	2	2.70	2.00	0.30	5	Oct'25
71	North 24 Parganas	Ashokenagar-Kalyangarh	23	1,21,592	35	23	0	23	0	22.00	10.00	3.00	35	Sept'25
72	North 24 Parganas	Baduria	17	52,500	6	6	11	6	11	0.50	0.20	3.00	4	Oct '25
73	North 24 Parganas	Baranagar	34	2,45,213	134	34	0	11	23	50.50	15.00	68.50	134	Nov '25
74	North 24 Parganas	Barasat	35	2,78,435	163	35	0	30	5	79.00	60.00	24.00	163	Dec '25
75	North 24 Parganas	Barrackpore	24	1,52,783	40	24	0	22	2	26.40	12.40	1.20	40	Nov, 25
76	North 24 Parganas	Basirhat	23	1,25,058	53	23	0	23	0	39.50	9.50	4.00	53	Oct'25
77	North 24 Parganas	Bhatpara	35	3,85,867	164	35	0	35	0	86.57	58.18	19.25	164	Dec, 25
78	North 24 Parganas	Bidhan Nagar MC	41	6,34,107	287	41	0	0	41	111.00	76.00	100.00	287	Nov '25
79	North 24 Parganas	Bongaon	22	1,08,864	42	18	4	16	6	20.00	9.00	12.00	41	Nov '25
80	North 24 Parganas	Dum Dum	22	1,14,786	50	22	0	8	16	22.50	7.50	20.00	50	Nov '25
81	North 24 Parganas	Garulia	21	85,336	35	21	0	8	13	12.00	5.00	18.00	35	Nov '25
82	North 24 Parganas	Gobardanga	17	45,392	12	17	0	17	0	10.00	2.00	0.00	12	Achieved
83	North 24 Parganas	Habra	24	1,47,221	44	24	0	20	4	29.00	8.00	7.00	44	Dec, 25
84	North 24 Parganas	Halisahar	23	1,24,851	38	16	7	16	7	13.00	8.00	15.00	36	Sept, 25
85	North 24 Parganas	Kamarhati	35	331163	128	35	0	28	7	60.00	41.00	27.00	128	Nov '25
86	North 24 Parganas	Kanchrapara	24	1,29,576	37	19	5	19	0	15.00	10.00	8.00	33	Oct'25
87	North 24 Parganas	Khardah	22	1,08,496	38	22	0	20	2	19.00	12.00	7.00	38	Dec'25
88	North 24 Parganas	Madhyamgram	28	1,96,127	62	28	0	28	0	36.00	21.00	5.00	62	Oct '25
89	North 24 Parganas	Naihati	31	2,18,194	72	31	0	20	11	22.00	12.00	38.00	72	Sept '25
90	North 24 Parganas	New Barrackpore	20	76,879	22	20	0	20	0	11.60	5.20	5.20	22	Oct '25
91	North 24 Parganas	North Barrackpore	23	1,32,806	46	23	0	12	11	20.00	8.00	18.00	46	Sept '25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
92	North 24 Parganas	North Dum Dum	34	2,49,142	30	34	0	34	0	20.00	10.00	0.00	30	Nov'25
93	North 24 Parganas	Panihati	35	3,77,351	127	35	0	0	0	0.00	0.00	127.00	127	Dec '25
94	North 24 Parganas	South Dum Dum	35	4,03,316	287	35	0	26	9	135.00	28.00	124.00	287	Dec, 25
95	North 24 Parganas	Taki	16	38,263	9	16	0	10	6	4.50	2.00	2.50	9	Sept, 25
96	North 24 Parganas	Titagarh	23	1,16,541	42	23	0	16	7	19.00	13.00	10.00	42	Dec'25
97	Paschim Midnapore	Chandrakona	12	23,629	8	12	0	8	4	3.50	2.00	2.50	8	Dec'25
98	Paschim Midnapore	Ghatal	17	54,591	17	13	4	4	13	5.00	4.00	7.00	16	Sept '25
99	Jhargram	Jhargram	18	61,682	15	16	2	4	14	10.50	1.50	2.00	14	Dec'25
100	Paschim Midnapore	Kharagpur	35	2,07,604	40	27	8	1	26	18.00	11.00	9.00	38	Dec '25
101	Paschim Midnapore	Kharar	10	12,220	4	10	0	8	2	1.50	0.50	2.00	4	Dec'25
102	Paschim Midnapore	Khirpai	10	16,385	5	10	0	3	7	3.00	1.00	1.00	5	Dec'25
103	Paschim Midnapore	Midnapore	25	1,69,127	62	25	0	13	12	30.00	18.00	14.00	62	Nov '25
104	Paschim Midnapore	Ramjibanpur	11	19,611	5	11	0	4	7	2.00	1.50	1.50	5	Sept '25
105	Purba Midnapore	Contai	21	92,226	40	15	6	16	5	20.00	8.00	10.00	38	Nov '25
106	Purba Midnapore	Egra	14	30,148	9	14	0	12	2	5.00	2.00	2.00	9	Sept '25
107	Purba Midnapore	Haldia	29	2,00,827	80	29	0	3	26	15.00	5.00	60.00	80	March '26
108	Purba Midnapore	Panskura	18	57,932	11	18	0	18	0	6.00	5.00	0.00	11	Achieved
109	Purba Midnapore	Tamluk	20	65,312	15	20	0	17	3	8.50	5.00	1.50	15	Oct '25
110	Jhalda	Jhalda	12	19,540	4	12	0	12	0	1.50	1.00	1.50	4	Sept, 25
111	Purulia	Purulia	23	1,21,067	16	16	7	0	23	6.00	3.00	6.00	15	Sept '25
112	Purulia	Raghunathpur	13	25,621	7	13	0	8	5	1.40	2.66	2.94	7	Sept, 25
113	South 24 parganas	Baruipur	17	53,128	22	17	0	6	11	12.00	3.00	7.00	22	Sept '25
114	South 24 parganas	Budge Budge	20	76,858	24	20	0	18	2	13.60	7.60	2.80	24	Oct '25
115	South 24 parganas	Diamond Harbour	16	43,169	12	16	0	9	7	5.00	2.50	4.50	12	Dec'25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
116	South 24 parganas	Jainagar-Mazilpur	14	25,922	**6**	14	0	14	0	3.50	1.50	1.00	6	Dec'25
117	South 24 parganas	Maheshtala	35	4,49,423	**168**	35	0	10	25	72.00	40.00	56.00	168	Dec '25
118	South 24 parganas	Pujali	16	37,040	**11**	2	14	2	2	2.00	0.50	2.00	5	Dec '25
119	South 24 parganas	Rajpur-Sonarpur	35	4,23,724	**279**	35	0	28	7	135.00	126.00	18.00	279	Nov'25
120	Uttar Dinajpur	Dalkhola	16	37,063	**11**	13	3	9	7	5.00	3.50	2.00	11	Sept '25
121	Uttar Dinajpur	Islampur	17	54,340	**14**	13	4	13	4	5.00	3.50	4.00	13	Sept '25
122	Uttar Dinajpur	Kaliaganj	17	53,530	**22**	17	0	15	2	11.00	7.00	4.00	22	Sept '25
123	Uttar Dinajpur	Raiganj	27	1,83,612	**60**	19	8	0	9	16.00	9.00	33.00	58	Sept '25
124	Howrah	Howrah MC	50	10,70,645	**568**	45	5	11	0	75.00	40.00	432.00	547	March '26
125	Howrah	Bally	35	2,91,916	**112**	35	0	0	0	0.00	0.00	112.00	112	Feb'26
126	Jalpaiguri	Maynaguri	17	36,263	**8**	2	15	0	17	3.00	1.50	1.00	6	Sept '25
127	Alipurduar	Falakata	18	54,039	**14**	2	16	0	0	0.00	0.00	5.77	6	Oct '25
128	Kolkata	Kolkata MC	144	4594718	**3668**	144	0	27	117	1840.00	360.00	1468.00	3668	Apr '26
		Total =	2997	**21532295**	**10227.00**	**2761**	**236**	**1772**	**1019**	**4488.20**	**1837.13**	**3799.57**	**10124.91**	

	Status of per day Collection & Transportation of Fresh Waste of 128 ULBs of West Bengal upto July,2025													
Sl No	**District**	**ULB**	**No. of ward**	**Population (Census 2011)**	**Per day Generation of fresh waste (TPD)**	**Door to door collection of fresh waste in no. of wards**		**Collection of segregated fresh waste in no. of wards**		**Quantity of fresh waste being collected & transported per day (TPD)**				**Tentative timeline for ensuring 100% segregation**
						Full	**Partial**	**Full**	**Partial**	**Wet Waste**	**Dry Waste**	**Mixed Waste**	**Total**	
1	Bankura	Bankura	24	1,37,386	**37**	24	0	16	8	13.95	5.46	17.59	37	Sept '25
2	Bankura	Bishnupur	19	67,783	**16**	11	8	8	11	4.92	3.08	8.00	16	Sept '25
3	Bankura	Sonamukhi	15	34,228	**8**	15	0	6	9	3.08	1.85	3.08	8	Sept '25
4	Paschim Burdwan	Asansol MC	106	11,56,387	**560**	84	22	27	79	196.80	128.00	235.20	560	Sept '25
5	Purba Burdwan	Barddhaman	35	3,14,638	**101**	35	0	23	12	43.35	45.39	12.26	101	Sept '25
6	Purba Burdwan	Dainhat	14	24,397	**7**	14	0	13	1	4.09	2.77	0.13	7	Sept '25
7	Paschim Burdwan	Durgapur MC	43	5,66,517	**244**	43	0	20	23	101.93	68.22	73.84	244	Sept '25
8	Purba Burdwan	Gushkara	16	35,374	**8**	16	0	15	1	3.67	3.00	1.33	8	Sept '25
9	Purba Burdwan	Kalna	18	56,722	**14**	18	0	18	0	6.37	5.65	1.98	14	Oct '25
10	Purba Burdwan	Katwa	20	81,615	**29**	20	0	16	4	12.32	6.77	9.91	29	Sept '25
11	Purba Burdwan	Memari	16	41,455	**10**	16	0	16	0	6.88	3.13	0.00	10	Achieved
12	Birbhum	Bolpur	22	80,210	**33**	22	0	10	12	13.20	9.00	10.79	33	Sept '25
13	Birbhum	Dubrajpur	16	38,041	**10**	16	0	16	0	5.79	3.56	0.64	10	Sept '25
14	Birbhum	Nalhati	16	41,244	**9**	14	2	14	2	3.60	1.80	3.60	9	Sept '25
15	Birbhum	Rampurhat	18	57,833	**17**	18	0	12	6	6.68	2.43	7.89	17	Sept '25
16	Birbhum	Sainthia	16	44608	**12**	16	0	10	6	6.32	3.16	2.53	12	Sept '25
17	Birbhum	Suri	21	90,314	**23**	21	0	8	13	7.46	4.97	10.57	23	Sept, 25
18	Cooch Behar	Cooch Behar	20	77935	**17**	20	0	2	18	3.04	1.21	12.75	17	Sept '25
19	Cooch Behar	Dinhata	16	36,124	**10**	16	0	16	0	6.64	3.36	0.00	10	Achieved
20	Cooch Behar	Haldibari	11	14,404	**4**	11	0	11	0	2.31	1.38	0.31	4	Oct,25
21	Cooch Behar	Mathabhanga	12	23,895	**9**	8	4	8	4	4.36	3.29	1.35	9	Sept '25
22	Cooch Behar	Mekhliganj	9	9,123	**5**	9	0	9	0	1.60	1.06	2.34	5	Sept '25
23	Cooch Behar	Tufanganj	12	20,998	**7**	12	0	12	0	4.38	1.75	0.88	7	Sept '25
24	Dakshin Dinajpur	Balurghat	25	1,51,299	**45**	25	0	25	0	25.20	14.40	5.40	45	Sept '25
25	Dakshin Dinajpur	Buniadpur	14	30183	**8**	14	0	10	4	4.00	2.00	2.00	8	Sept '25
26	Dakshin Dinajpur	Gangarampore	18	56,217	**17**	13	5	13	5	6.07	1.82	9.11	17	Sept '25
27	Darjeeling	Darjeeling	32	1,20,414	**21**	32	0	32	0	15.60	3.60	1.80	21	Sept '25
28	Kalimpong	Kalimpong	23	49,403	**12**	16	7	10	4	5.68	1.89	4.42	12	Sept '25
29	Darjeeling	Kurseong	20	42,346	**7**	20	0	10	10	2.55	1.27	3.18	7	Sept '25
30	Darjeeling	Mirik	9	11,513	**3**	6	3	6	3	1.29	1.07	0.64	3	Sept '25
31	Darjeeling	Siliguri MC	47	5,13,264	**287**	47	0	35	12	137.09	64.94	84.98	287	Sept, 25
32	Howrah	Uluberia	32	2,32,290	**96**	32	0	25	7	25.22	10.78	60.00	96	Sept, 25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
33	Hooghly	Arambagh	19	66,175	18	19	0	14	5	9.29	7.97	0.74	18	Sept, 25
34	Hooghly	Baidyabati	23	1,21,110	50	23	0	23	0	34.00	14.00	2.00	50	Sept,25
35	Hooghly	Bansberia	22	1,03,920	32	20	2	16	6	10.11	4.61	17.28	32	Sept, 25
36	Hooghly	Bhadreswar	22	1,01,477	26	22	0	22	0	16.25	9.75	0.00	26	Achieved
37	Hooghly	Champdany	22	1,11,251	19	20	2	18	4	9.00	4.00	6.00	19	Sept, 25
38	Hooghly	Chandannagore MC	33	1,66,867	58	33	0	31	2	30.45	20.13	7.42	58	Sept, 25
39	Hooghly	Dankuni	21	94,966	34	21	0	17	4	16.19	12.14	5.67	34	Sept '25
40	Hooghly	Hooghly Chinsurah	30	1,77,259	60	30	0	20	10	40.00	18.40	1.60	60	Sept, 25
41	Hooghly	Konnagar	20	76,172	26	20	0	19	1	15.29	7.65	3.06	26	Oct'25
42	Hooghly	Rishra	23	1,24,585	45	23	0	9	14	13.33	6.67	25.00	45	Sept '25
43	Hooghly	Serampore	29	1,83,339	95	29	0	16	13	30.00	21.00	44.00	95	Sept '25
44	Hooghly	Tarakeswar	15	30,947	8	15	0	15	0	4.87	3.74	0.51	9	Dec'25
45	Hooghly	Uttarpara Kotrung	24	1,62,386	72	24	0	24	0	47.00	25.00	0.00	72	Achieved
46	Alipurduar	Alipurduar	20	65,232	21	15	5	15	5	11.50	8.50	1.00	21	Sept '25
47	Jalpaiguri	Dhupguri	16	44,719	7	1	15	1	15	0.87	0.60	5.53	7	Sept '25
48	Jalpaiguri	Jalpaiguri	25	1,07,341	38	25	0	25	0	22.80	13.24	1.96	38	Oct,25
49	Jalpaiguri	Mal	15	25,218	6	11	4	11	4	3.00	2.00	1.00	6	Sept '25
50	Malda	English Bazar	29	2,05,521	93	29	0	19	10	49.20	20.40	23.40	93	Sept '25
51	Malda	Old Malda	20	84,012	23	20	0	20	0	11.19	7.46	4.35	23	Sept '25
52	Murshidabad	Beldanga	14	29,182	7	14	0	14	0	2.60	1.60	2.80	7	Oct,25
53	Murshidabad	Berhampore	28	1,95,363	60	28	0	18	10	19.44	12.96	27.60	60	Sept '25
54	Murshidabad	Dhuliyan	21	95,706	23	21	0	0	21	2.41	1.46	19.14	23	Sept '25
55	Murshidabad	Domkal	21	1,21,927	24	21	0	6	15	9.00	5.40	9.60	24	Sept '25
56	Murshidabad	Jangipur	21	88,165	29	21	0	21	0	14.50	8.70	5.80	29	Sept, 25
57	Murshidabad	Jiaganj-Azimganj	17	51,790	10	9	8	2	15	4.49	1.84	3.67	10	Sept '25
58	Murshidabad	Kandi	18	55,632	12	15	3	15	3	6.95	2.53	2.53	12	Sept, 25
59	Murshidabad	Murshidabad	16	44,064	12	16	0	10	6	3.60	2.40	6.00	12	Sept '25
60	Nadia	Birnagar	14	30799	10	14	0	13	1	6.42	2.95	0.63	10	Oct,25
61	Nadia	Chakdah	21	95,203	23	6	3	6	3	4.97	1.86	16.16	23	Oct '25
62	Nadia	Cooper's Camp	12	18,839	5	12	0	8	4	2.13	1.75	1.13	5	Dec'25
63	Nadia	Gayeshpur	18	58,998	16	18	0	4	14	8.00	3.20	4.80	16	Sept '25
64	Nadia	Haringhata	17	45,953	12	5	12	0	0	0.00	0.00	9.00	9	Oct '25
65	Nadia	Kalyani	21	1,00,620	48	21	0	3	18	11.20	1.60	35.20	48	Sept '25
66	Nadia	Krishnanagar	25	1,53,062	120	25	0	21	4	71.26	38.00	10.74	120	Dec'25
67	Nadia	Nabadwip	24	1,25,528	36	24	0	24	0	18.60	12.00	5.40	36	Dec'25
68	Nadia	Ranaghat	20	75,365	15	20	0	12	8	7.80	3.60	3.60	15	Sept, 25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
69	Nadia	Santipur	24	1,51,777	50	24	0	16	8	24.70	16.27	9.04	50	Sept '25
70	Nadia	Taherpur	13	20,894	5	13	0	11	2	2.70	2.00	0.30	5	Oct'25
71	North 24 Parganas	Ashokenagar-Kalyangarh	23	1,21,592	29	23	0	23	0	18.13	8.46	2.42	29	Oct'25
72	North 24 Parganas	Baduria	17	52,500	6	6	0	6	0	0.42	0.15	5.43	6	Oct '25
73	North 24 Parganas	Baranagar	34	2,45,213	134	34	0	11	23	49.75	14.44	69.81	134	Sept '25
74	North 24 Parganas	Barasat	35	2,78,435	163	35	0	30	5	78.69	60.22	24.09	163	Sept '25
75	North 24 Parganas	Barrackpore	24	1,52,783	40	24	0	22	2	26.40	12.40	1.20	40	Sept, 25
76	North 24 Parganas	Basirhat	23	1,25,058	53	23	0	23	0	39.75	9.46	3.79	53	Oct'25
77	North 24 Parganas	Bhatpara	35	3,85,867	164	35	0	35	0	86.57	58.18	19.25	164	Sept, 25
78	North 24 Parganas	Bidhan Nagar MC	41	6,34,107	280	41	0	0	41	105.60	104.00	70.40	280	Sept '25
79	North 24 Parganas	Bongaon	22	1,08,864	38	18	4	16	6	18.39	8.58	11.03	38	Sept '25
80	North 24 Parganas	Dum Dum	22	1,14,786	50	22	0	8	16	22.54	7.33	20.13	50	Sept '25
81	North 24 Parganas	Garulia	21	85,336	29	21	0	8	13	7.30	4.05	17.65	29	Sept '25
82	North 24 Parganas	Gobardanga	17	45,392	12	17	0	17	0	10.64	1.36	0.00	12	Achieved
83	North 24 Parganas	Habra	24	1,47,221	42	24	0	20	4	28.20	7.80	6.00	42	Sept, 25
84	North 24 Parganas	Halisahar	23	1,24,851	42	16	7	16	7	15.67	10.98	15.35	42	Sept, 25
85	North 24 Parganas	Kamarhati	35	331163	128	35	0	28	7	43.57	51.71	32.72	128	Sept '25
86	North 24 Parganas	Kanchrapara	24	1,29,576	44	19	0	19	0	18.88	12.13	12.99	44	Oct'25
87	North 24 Parganas	Khardah	22	1,08,496	38	22	0	20	2	11.65	18.45	7.91	38	Dec'25
88	North 24 Parganas	Madhyamgram	28	1,96,127	72	28	0	28	0	39.92	27.74	4.34	72	Oct '25
89	North 24 Parganas	Naihati	31	2,18,194	86	31	0	20	11	21.46	11.90	52.64	86	Sept '25
90	North 24 Parganas	New Barrackpore	20	76,879	22	20	0	20	0	11.60	5.20	5.20	22	Oct '25
91	North 24 Parganas	North Barrackpore	23	1,32,806	59	23	0	12	11	25.86	12.12	21.01	59	Sept '25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
92	North 24 Parganas	North Dum Dum	34	2,49,142	26	34	0	34	0	17.88	8.13	0.00	26	Achieved
93	North 24 Parganas	Panihati	35	3,77,351	141	35	0	0	0	0.00	0.00	141.00	141	Oct '25
94	North 24 Parganas	South Dum Dum	35	4,03,316	287	35	0	26	9	135.11	27.98	123.91	287	Sept, 25
95	North 24 Parganas	Taki	16	38,263	9	16	0	10	6	4.11	1.93	2.96	9	Sept, 25
96	North 24 Parganas	Titagarh	23	1,16,541	39	23	0	16	7	17.99	11.45	9.57	39	Sept '25
97	Paschim Midnapore	Chandrakona	12	23,629	6	12	0	8	4	2.49	1.71	1.80	6	Dec'25
98	Paschim Midnapore	Ghatal	17	54,591	17	13	4	4	13	5.04	4.13	2.29	11	Sept '25
99	Jhargram	Jhargram	18	61,682	15	16	2	4	14	10.53	1.58	2.89	15	Dec'25
100	Paschim Midnapore	Kharagpur	35	2,07,604	50	27	8	1	26	17.07	12.80	20.12	50	Sept '25
101	Paschim Midnapore	Kharar	10	12,220	4	10	0	8	2	1.41	0.56	2.04	4	Dec'25
102	Paschim Midnapore	Khirpai	10	16,385	5	10	0	3	7	3.10	0.92	0.98	5	Dec'25
103	Paschim Midnapore	Midnapore	25	1,69,127	56	25	0	13	12	27.88	17.77	10.35	56	Sept '25
104	Paschim Midnapore	Ramjibanpur	11	19,611	5	11	0	4	7	2.14	1.43	1.43	5	Sept '25
105	Purba Midnapore	Contai	21	92,226	36	15	6	16	5	9.00	3.60	2.40	15	Sept '25
106	Purba Midnapore	Egra	14	30,148	9	12	2	12	2	4.81	1.54	2.65	9	Sept '25
107	Purba Midnapore	Haldia	29	2,00,827	80	29	0	3	26	15.00	5.00	60.00	80	Sept '25
108	Purba Midnapore	Panskura	18	57,932	11	18	0	18	0	6.11	4.89	0.00	11	Achieved
109	Purba Midnapore	Tamluk	20	65,312	15	20	0	17	3	8.38	5.03	1.59	15	Oct '25
110	Jhalda	Jhalda	12	19,540	4	12	0	12	0	1.50	1.00	1.50	4	Sept, 25
111	Purulia	Purulia	23	1,21,067	12	16	7	0	23	2.00	1.50	5.00	9	Sept '25
112	Purulia	Raghunathpur	13	25,621	7	13	0	8	5	1.40	2.66	2.94	7	Sept, 25
113	South 24 parganas	Baruipur	17	53,128	20	17	0	6	11	11.02	2.86	6.12	20	Sept '25
114	South 24 parganas	Budge Budge	20	76,858	24	20	0	18	2	13.60	7.60	2.80	24	Oct '25
115	South 24 parganas	Diamond Harbour	16	43,169	12	16	0	9	7	5.00	2.50	4.50	12	Dec'25

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
116	South 24 parganas	Jainagar-Mazilpur	14	25,922	6	14	0	14	0	3.33	1.33	1.33	6	Dec'25
117	South 24 parganas	Maheshtala	35	4,49,423	168	35	0	10	25	72.00	40.00	56.00	168	Sept '25
118	South 24 parganas	Pujali	16	37,040	11	2	14	2	2	2.00	0.05	8.50	11	Oct '25
119	South 24 parganas	Rajpur-Sonarpur	35	4,23,724	279	35	0	28	7	134.89	126.50	17.61	279	Sept '25
120	Uttar Dinajpur	Dalkhola	16	37,063	11	13	3	9	7	5.15	3.31	2.54	11	Sept '25
121	Uttar Dinajpur	Islampur	17	54,340	14	13	4	13	4	4.98	3.32	5.70	14	Sept '25
122	Uttar Dinajpur	Kaliaganj	17	53,530	24	17	0	15	2	12.92	8.86	2.22	24	Sept '25
123	Uttar Dinajpur	Raiganj	27	1,83,612	57	19	8	0	9	9.60	7.20	40.20	57	Sept '25
124	Howrah	Howrah MC	50	10,70,645	112	45	5	11	0	17.35	11.04	83.61	112	Sept '25
125	Howrah	Bally	35	2,91,916	568	35	0	0	0	0.00	0.00	568.00	568	Oct '25
126	Jalpaiguri	Maynaguri	17	36,263	8	2	15	0	17	3.00	1.50	2.50	7	Sept '25
127	Alipurduar	Falakata	18	54,039	14	2	16	0	0	0.00	0.00	7.75	8	Oct '25
128	Kolkata	Kolkata MC	144	4594718	3600	144	NA	27	117	1840.00	360.00	1400.00	3600	December '25
		Total =	2997	**21532295**	**10227.00**	**2759**	**210**	**1772**	**1008**	**4389.27**	**1877.79**	**3920.31**	**10187.38**	

	Information regarding Per Day Collection, Transportation of Fresh Waste and land availilibilty of 128 ULBs of West Bengal									
Sl No	**District**	**ULB**	**No. of ward**	**Population (Census 2011)**	**Per day Generation of fresh waste (TPD)**	**Quantity of fresh waste being collected & transported per day (TPD)**				**Tentative timeline for ensuring 100% segregation**
						Wet Waste	**Dry Waste**	**Mixed Waste**	**Total**	
1	Bankura	Bankura	24	1,37,386	82	23	12	47	82	December '24
2	Bankura	Bishnupur	19	67,783	86	21	9	56	86	March '25
3	Bankura	Sonamukhi	15	34,228	13	5	3	5	13	March '25
4	Paschim Burdwan	Asansol MC	106	11,56,387	700	210	140	350	700	March '25
5	Purba Burdwan	Barddhaman	35	3,14,638	168	72.1	75.5	20.4	168	January '25
6	Purba Burdwan	Dainhat	14	24,397	10.55	6.12	4.12	0.31	10.55	November '24
7	Paschim Burdwan	Durgapur MC	43	5,66,517	304	127	85	92	304	March '25
8	Purba Burdwan	Gushkara	16	35,374	19.3	5.12	7.14	7.04	19.3	November '24
9	Purba Burdwan	Kalna	18	56,722	23	10.47	9.28	3.25	23	October '24
10	Purba Burdwan	Katwa	20	81,615	40.94	20.45	11.01	9.48	40.94	November '24
11	Purba Burdwan	Memari	16	41,455	16	8	3	5	16	November '24
12	Birbhum	Bolpur	22	80,210	54.98	20.4	13.6	20.98	54.98	March '25
13	Birbhum	Dubrajpur	16	38,041	15.54	9	5.54	1	15.54	October '24
14	Birbhum	Nalhati	16	41,244	28	19	3	6	28	November '24
15	Birbhum	Rampurhat	18	57,833	49	21	10	18	49	December '24
16	Birbhum	Sainthia	16	44608	19	5.7	3.8	9.5	19	February '25
17	Birbhum	Suri	21	90,314	60	19	11	30	60	December '24
18	Cooch Behar	Cooch Behar	20	77935	45.68	20.5	13.62	11.56	45.68	March '25
19	Cooch Behar	Dinhata	16	36,124	15.52	8.16	4.21	3.15	15.52	October '24
20	Cooch Behar	Haldibari	11	14,404	5.2	2	1.8	1.4	5.2	October '24

21	Cooch Behar	Mathabhanga	12	23,895	14.27	3.76	2.74	2.77	9.27	January '25
22	Cooch Behar	Mekhliganj	9	9,123	4.7	1.5	1	2.2	4.7	October '24
23	Cooch Behar	Tufanganj	12	20,998	14.25	6.35	7.6	0.3	14.25	October '24
24	Dakshin Dinajpur	Balurghat	25	1,51,299	75	38	23	14	75	October '24
25	Dakshin Dinajpur	Buniadpur	14	30183	12	6	3	3	12	December '24
26	Dakshin Dinajpur	Gangarampore	18	56,217	28	10	3	15	28	December '24
27	Darjeeling	Darjeeling	32	1,20,414	35	26	6	3	35	October '24
28	Kalimpong	Kalimpong	23	49,403	38.85	18.85	15.28	4.72	38.85	March '25
29	Darjeeling	Kurseong	20	42,346	11	4	2	5	11	January '25
30	Darjeeling	Mirik	9	11,513	4.2	1.8	1.5	0.9	4.2	January '25
31	Darjeeling	Siliguri MC	47	5,13,264	358	171	81	106	358	February '25
32	Howrah	Uluberia	32	2,32,290	48.7	20.52	13.48	14.5	48.5	October '24
33	Hooghly	Arambagh	19	66,175	28.76	14.84	12.73	1.19	28.76	December '24
34	Hooghly	Baidyabati	23	1,21,110	50	27	15	8	50	December '24
35	Hooghly	Bansberia	22	1,03,920	24	8.64	5.76	9.6	24	October '24
36	Hooghly	Bhadreswar	22	1,01,477	32	20	12	0	32	NA
37	Hooghly	Champdany	22	1,11,251	19	6	3	10	19	December '24
38	Hooghly	Chandannagore MC	33	1,66,867	60	36	24	0	60	NA
39	Hooghly	Dankuni	21	94,966	42	20	15	7	42	March '25
40	Hooghly	Hooghly Chinsurah	30	1,77,259	82	50	30	2	82	December '24
41	Hooghly	Konnagar	20	76,172	25.5	10	4	11.5	25.5	October '24
42	Hooghly	Rishra	23	1,24,585	35	8.21	5.47	21.32	35	March '25
43	Hooghly	Serampore	29	1,83,339	70	14	9	47	70	March '25
44	Hooghly	Tarakeswar	15	30,947	13.16	6.01	3.73	3.42	13.16	December '24

45	Hooghly	Uttarpara Kotrung	24	1,62,386	89.81	37	52.81	0	89.81	
46	Alipurduar	Alipurduar	20	65,232	21	10	8	3	21	January '25
47	Alipurduar	Dhupguri	16	44,719	10.5	1.3	0.9	8.3	10.5	March '25
48	Alipurduar	Jalpaiguri	25	1,07,341	62	37.2	21.6	3.2	62	November '24
49	Alipurduar	Mal	15	25,218	13.74	4.98	2.1	6.66	13.74	March '25
50	Malda	English Bazar	29	2,05,521	210	140	70	0	210	NA
51	Malda	Old Malda	20	84,012	37	18	12	7	37	NA
52	Murshidabad	Beldanga	14	29,182	11	4.08	2.52	4.4	11	October '24
53	Murshidabad	Berhampore	28	1,95,363	90	32.4	21.6	36	90	March '25
54	Murshidabad	Dhuliyan	21	95,706	46.42	4	2.42	40	46.42	March '25
55	Murshidabad	Domkal	21	1,21,927	40	15	9	16	40	March '25
56	Murshidabad	Jangipur	21	88,165	48	24	14.4	9.6	48	December '24
57	Murshidabad	Jiaganj-Azimganj	17	51,790	25	9	6	10	25	March '25
58	Murshidabad	Kandi	18	55,632	31.05	16.78	10.7	3.57	31.05	December '24
59	Murshidabad	Murshidabad	16	44,064	32	12	10	10	32	January '25
60	Nadia	Birnagar	14	30799	9.82	4.714	3.142	1.96	9.816	December '24
61	Nadia	Chakdah	21	95,203	58	0	0	0	0	July '25
62	Nadia	Cooper's Camp	12	18,839	8.04	3.42	2.81	1.81	8.04	December '24
63	Nadia	Gayeshpur	18	58,998	31	17	6	8	31	March '25
64	Nadia	Haringhata	17	45,953	0	0	0	0	0	July '25
65	Nadia	Kalyani	21	1,00,620	55	14	2	39	55	March '25

66	Nadia	Krishnanagar	25	1,53,062	120	70.8	36	13.2	120	December '24
67	Nadia	Nabadwip	24	1,25,528	63	31	23	9	63	December '24
68	Nadia	Ranaghat	20	75,365	45	23	15	7	45	February '25
69	Nadia	Santipur	24	1,51,777	75.84	37.85	23.75	14.24	75.84	March '25
70	Nadia	Taherpur	13	20,894	5	2.7	2	0.3	5	December '24
71	North 24 Parganas	Ashokenagar-Kalyangarh	23	1,21,592	79	42	28	9	79	December '24
72	North 24 Parganas	Baduria	17	52,500	5.97	0.42	0.15	5.4	5.97	July '25
73	North 24 Parganas	Baranagar	34	2,45,213	150	62	18	70	150	March '25
74	North 24 Parganas	Barasat	35	2,78,435	203	92	68	43	203	January '25
75	North 24 Parganas	Barrackpore	24	1,52,783	50	33	15.5	1.5	50	December '24
76	North 24 Parganas	Basirhat	23	1,25,058	56	27	2	27	56	December '24
77	North 24 Parganas	Bhatpara	35	3,85,867	205	108.21	72.73	24.06	205	February '25
78	North 24 Parganas	Bidhan Nagar MC	41	6,34,107	350	132	130	88	350	March '25
79	North 24 Parganas	Bongaon	22	1,08,864	62	28	12	22	62	January '25
80	North 24 Parganas	Dum Dum	22	1,14,786	62.1	20	7	35	62	January '25
81	North 24 Parganas	Garulia	21	85,336	21	9	5	7	21	March '25
82	North 24 Parganas	Gobardanga	17	45,392	18.64	16.52	2.12	0	18.64	NA
83	North 24 Parganas	Habra	24	1,47,221	70	47	13	10	70	December '24
84	North 24 Parganas	Halisahar	23	1,24,851	47	19.4	13.6	14	47	December '24
85	North 24 Parganas	Kamarhati	35	331163	160	48.46	64.64	46.9	160	January '25
86	North 24 Parganas	Kanchrapara	24	1,29,576	53	22.26	14.84	15.9	53	December '24
87	North 24 Parganas	Khardah	22	1,08,496	46	13.8	22.54	9.66	46	December '24
88	North 24 Parganas	Madhyamgram	28	1,96,127	90	49.9	34.67	5.43	90	November '24
89	North 24 Parganas	Naihati	31	2,18,194	110	26.7	17.8	65.5	110	January '25

90	North 24 Parganas	New Barrackpore	20	76,879	27.5	10.5	4.51	12.5	27.51	December '24
91	North 24 Parganas	North Barrackpore	23	1,32,806	73	32	15	26	73	January '25
92	North 24 Parganas	North Dum Dum	34	2,49,142	32	22	10	0	32	NA
93	North 24 Parganas	Panihati	35	3,77,351	156	0	0	136	136	July '25
94	North 24 Parganas	South Dum Dum	35	4,03,316	376	169	23	184	376	February '25
95	North 24 Parganas	Taki	16	38,263	22.75	8.4	5.6	8.75	22.75	October '24
96	North 24 Parganas	Titagarh	23	1,16,541	65	32	16	17	65	January '25
97	Paschim Midnapore	Chandrakona	12	23,629	8.42	3.5	2.4	2.52	8.42	December '24
98	Paschim Midnapore	Ghatal	17	54,591	26.7	7.92	6.48	3.6	18	
99	Paschim Midnapore	Jhargram	18	61,682	28.5	20	3	5.5	28.5	February '25
100	Paschim Midnapore	Kharagpur	35	2,07,604	82	28	21	33	82	March '25
101	Paschim Midnapore	Kharar	10	12,220	5.4	1.9	0.75	2.75	5.4	December '24
102	Paschim Midnapore	Khirpai	10	16,385	6.76	4.19	1.25	1.32	6.76	February '25
103	Paschim Midnapore	Midnapore	25	1,69,127	92	43.8	29.2	19	92	March '25
104	Paschim Midnapore	Ramjibanpur	11	19,611	23	3	2	7	12	March '25
105	Purba Midnapore	Contai	21	92,226	60	15	6	4	25	March '25
106	Purba Midnapore	Egra	14	30,148	14.6	7.8	2.5	4.3	14.6	January '25
107	Purba Midnapore	Haldia	29	2,00,827	80	15	5	60	80	January '25
108	Purba Midnapore	Panskura	18	57,932	18	10	8	0	18	NA
109	Purba Midnapore	Tamluk	20	65,312	24.6	13.75	8.25	2.6	24.6	December '24
110	Jhalda	Jhalda	12	19,540	6.48	2.1	1.54	2.84	6.48	December '24
111	Purulia	Purulia	23	1,21,067	20	3	2	7	12	March '25
112	Purulia	Raghunathpur	13	25,621	11	2.2	4.18	4.62	11	February '25
113	South 24 parganas	Baruipur	17	53,128	24.5	13.5	3.5	7.5	24.5	January '25
114	South 24 parganas	Budge Budge	20	76,858	27.13	18	9.5	0	27.5	NA
115	South 24 parganas	Diamond Harbour	16	43,169	12	5	3	4	12	December '24

116	South 24 parganas	Jainagar-Mazilpur	14	25,922	14	9	3	2	14	December '24
117	South 24 parganas	Maheshtala	35	4,49,423	249	50.4	33.56	102.6	186.56	March '25
118	South 24 parganas	Pujali	16	37,040	0.413	0.358	0.0551	0	0.4131	July '25
119	South 24 parganas	Rajpur-Sonarpur	35	4,23,724	348.52	153.5	102.33	41.31	297.14	March '25
120	Uttar Dinajpur	Dalkhola	16	37,063	17.29	8.09	5.2	4	17.29	January '25
121	Uttar Dinajpur	Islampur	17	54,340	21.73	7.728	5.152	8.85	21.73	January '25
122	Uttar Dinajpur	Kaliaganj	17	53,530	39	21	14.4	3.6	39	October '24
123	Uttar Dinajpur	Raiganj	27	1,83,612	97	16	12	69	97	March '25
124	Howrah	Howrah MC	50	10,70,645	715	110	70	535	715	March '25
125	Howrah	Bally	35	2,91,916	139.93	0	0	139.93	139.93	July '25
126	Jalpaiguri	Maynaguri	17	36,263	12.7	1.5	0.6	0.3	2.4	March '25
127	Alipurduar	Falakata	18	54,039	22	0	0	0	0	July '25
128	Kolkata	Kolkata MC	144	4594718	4500	2300	450	1750	4500	December '25
			2997		**13457.95**				**13166.21**	
									97.83	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to September, 2025

Sl. No.	Name of District	ULB	No. of ward	Population (Census 2011)	Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of Wet Waste processing Unit	Type of Dry Waste processing Unit	Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
										Organic material (Wet Waste)	Inert	RDF	Other	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Budget outlay (Rs. In Cr)	DPR Prepared for Plant Infrastructure works (Yes/ No)	Tender Published for engagement of agency for Plant Infrastructure works (Yes/ No)	Work Order Issued to agency (Yes/ No)	Infrastructure Work Started by agency (Yes/ No)	Time line for starting of 100% processing of Fresh waste	Remarks
1	Bankura	Bankura	24	1,37,386	**40**	0	40	Windraw Composting	Material Recovery Facility (MRF)	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	6.68	Yes	Yes	Yes	Yes	May, 2026	
2	Bankura	Bishnupur	19	67,783	**14**	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.85	Yes	Yes	Yes	Yes	May, 2026	
3	Bankura	Sonamukhi	15	34,228	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.42	Yes	Yes	Yes	Yes	Dec, 2025	
4	Paschim Bardhaman	Asansol MC	106	11,56,387	**566**	0	566	Windraw Composting	MRF	311.3	56.6	33.96	164.14	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	76.65	Yes	Yes	Yes	No	April, 2026	
5	Purba Bardhaman	Barddhaman	35	3,14,638	**98**	0	98	Windraw Composting	MRF	53.9	9.8	5.88	28.42	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	18.40	No	No	No	No	December,2026	
6	Purba Bardhaman	Dainhat	14	24,397	**7**	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.16	No	No	No	No	Dember,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Sept, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
7	Paschim Bardhaman	Durgapur MC	43	5,66,517	**244**	0	244	Windraw Composting	MRF	134.2	24.4	14.64	70.76	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	33.29	Yes	Yes	Yes	No	December,2026	Work order issued to an agency for setting up of fresh waste processing unit at the ULB. Due to local agitation the agency could not start infrastrcure work for setting up of fresh waste processing unit at the reclaimed land of the dumpsite. For this, a feasible land is under identification.
8	Purba Bardhaman	Guskhara	16	35,374	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.31	Yes	Yes	Yes	Yes	April , 2026	
9	Purba Bardhaman	Kalna	18	56,722	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.52	Yes	Yes	Yes	No	March, 2026	
10	Purba Bardhaman	Katwa	20	81,615	**26**	0	26	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	5.16	No	No	No	No	December,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
11	Purba Bardhaman	Memari	16	41,455	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.75	Yes	Yes	Yes	Yes	December , 2025	
12	Birbhum	Bolpur	22	80,210	**31**	0	31	Windraw Composting	MRF	17.05	3.1	1.86	8.99	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	6.02	No	No	No	No	Oct,2026	
13	Birbhum	Dubrajpur	16	38,041	**10**	0	10	Windraw Composting	MRF	5.5	1	0.6	2.9	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.70	Yes	Yes	Yes	Yes	Feb, 2026	
14	Birbhum	Nalhati	16	41,244	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.64	Yes	Yes	Yes	Yes	March, 2026	
15	Birbhum	Rampurhat	18	57,833	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.07	Yes	Yes	No	No	October, 2026	
16	Birbhum	Sainthia	16	44608	**12**	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.08	Yes	Yes	Yes	Yes	Dec, 2025	
17	Birbhum	Suri	21	90,314	**26**	0	26	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.05	Yes	Yes	No	No	June, 2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to September, 2025																													
										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
18	Cooch Behar	Coochbehar	20	77935	20	0	20	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.07	Yes	No	No	No	December, 2026	
19	Cooch Behar	Dinhata	16	36,124	9	3	6	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	1.65	0.18	0.3	0.87	1.70	Yes	Yes	Yes	Yes	Dec, 2025	
20	Cooch Behar	Haldibari	11	14,404	4	2.5	1.5	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	1.375	0.15	0.25	0.725	0.57	Yes	Yes	Yes	Yes	January , 2026	
21	Cooch Behar	Mathabhanga	12	23,895	9	5	4	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.75	0.3	0.5	1.45	1.56	Yes	Yes	Yes	No	June, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit was started but due to public agiatation it was disrupted.
22	Cooch Behar	Mekhliganj	9	9,123	5	4	1	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.2	0.24	0.4	1.16	0.51	Yes	Yes	Yes	Yes	Dec, 2025	
23	Cooch Behar	Tufanganj	12	20,998	7	6	1	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	3.3	0.36	0.6	1.74	0.88	Yes	Yes	Yes	Yes	Dec, 2025	
24	Dakshin Dinajpur	Balurghat	25	1,51,299	42	0	42	Windraw Composting	MRF	23.1	4.2	2.52	12.18	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	8.21	Yes	Yes	Yes	Yes	June, 2026	
25	Dakshin Dinajpur	Buniadpur	14	30183	8	0	8	Windraw Composting	MRF	4.4	0.8	0.48	2.32	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.31	Yes	Yes	Yes	Yes	March, 2026	
26	Dakshin Dinajpur	Gangarampur	18	56,217	14	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.07	Yes	Yes	Yes	No	May, 2026	
27	Darjeeling	Darjeeling	32	1,20,414	24	0	24	Windraw Composting	MRF	13.2	2.4	1.44	6.96	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.83	No	No	No	No	Oct,2026	
28	Kalimpong	Kalimpong	23	49,403	13	0	13	Windraw Composting	MRF	7.15	1.3	0.78	3.77	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.08	No	No	No	No	Oct,2026	
29	Darjeeling	Kurseong	20	42,346	7	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.20	No	No	No	No	Oct,2026	
30	Darjeeling	Mirik	9	11,513	4	0	4	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.46	No	No	No	No	November,2026	
31	Darjeeling	Siliguri MC	47	5,13,264	297	297	0	Windraw Composting	MRF	163.35	29.7	17.82	86.13	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	163.35	17.82	29.7	86.13	39.20	Yes	Yes	Yes	Yes	Started	
32	Howrah	**Uluberia**	32	2,32,290	86	0	86	Windraw Composting	MRF	47.3	8.6	5.16	24.94	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	13.14	Yes	Yes	Yes	No	March, 2026	
33	Hooghly	Arambagh	19	66,175	16	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.15	No	No	No	No	Oct,2026	State Government has provided a land to the ULB for setting up of fresh waste processing unit. But due to public agitation further action could not be taken. Local administration is trying to reslove the matter.Expected that the matter will be resloved within Oct, 2025. After that, tender will be folated for enagagement of agency for setting up of freh waste processing plant.
34	Hooghly	Baidyabati	23	1,21,110	50	50	0	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	27.5	3	5	14.5	5.48	Yes	Yes	Yes	Yes	Started	
35	Hooghly	Bansberia	22	1,03,920	30	0	30	Windraw Composting	MRF	16.5	3	1.8	8.7	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.38	No	No	No	No	Oct,2026	
36	Hooghly	Bhadreswar	22	1,01,477	26	12	14	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	6.6	0.72	1.2	3.48	3.50	Yes	Yes	Yes	Yes	Sept, 2026	
37	Hooghly	Champdany	22	1,11,251	19	19	0	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	10.45	1.14	1.9	5.51	2.08	Yes	Yes	Yes	Yes	Started	
38	Hooghly	Chandernagore municipal corporation	33	1,66,867	52	0	52	Bio-CNG	MRF	28.6	5.2	3.12	15.08	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	7.82	No	No	No	No	Dec,2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to September, 2025																													
										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
39	Hooghly	Dankuni	21	94,966	32	0	32	Windraw Composting	MRF	17.6	3.2	1.92	9.28	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.60	Yes	Yes	Yes	Yes	Started	
40	Hooghly	Hooghly Chinsurah	30	1,77,259	56	0	56	Bio-CNG	MRF	30.8	5.6	3.36	16.24	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	8.21	No	No	No	No	Oct,2026	
41	Hooghly	Konnagar	20	76,172	26	25.5	0.5	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	14.025	1.53	2.55	7.395	2.79	Yes	Yes	Yes	Yes	Started	
42	Hooghly	Rishra	23	1,24,585	45	45	0	Windraw Composting	MRF	24.75	4.5	2.7	13.05	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	24.75	2.7	4.5	13.05	5.91	Yes	Yes	Yes	Yes	Dec, 2025	
43	Hooghly	Serampore	29	1,83,339	95	95	0	Windraw Composting	MRF	52.25	9.5	5.7	27.55	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	52.25	5.7	9.5	27.55	10.40	Yes	Yes	Yes	Yes	Started	
44	Hooghly	Tarakeswar	15	30,947	10	0	10	Windraw Composting	MRF	5.5	1	0.6	2.9	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.44	No	No	No	No	Oct,2026	
45	Hooghly	Uttarpara Kotrung	24	1,62,386	72	72	0	Windraw Composting	MRF	39.6	7.2	4.32	20.88	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	39.6	4.32	7.2	20.88	7.88	Yes	Yes	Yes	Yes	Started	
46	Alipurduar	Alipurduar	20	65,232	21	21	0	Windraw Composting	MRF	11.55	2.1	1.26	6.09	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	11.55	1.26	2.1	6.09	2.30	Yes	Yes	Yes	Yes	Started	
47	Jalpaiguri	Dhupguri	16	44,719	7	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.15	No	No	No	No	Oct,2026	
48	Jalpaiguri	Jalpaiguri	25	1,07,341	38	3	35	Windraw Composting	MRF	20.9	3.8	2.28	11.02	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	1.65	0.18	0.3	0.87	6.79	Yes	Yes	No	No	Oct, 2026	
49	Jalpaiguri	Mal	15	25,218	6	0	6	Windraw Composting	MRF	3.3	0.6	0.36	1.74	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.99	Yes	Yes	Yes	Yes	Dec, 2025	
50	Malda	English Bazar	29	2,05,521	82	0	82	Windraw Composting	MRF	45.1	8.2	4.92	23.78	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	16.97	Yes	Yes	Yes	No	Sep, 2026	
51	Malda	Old Malda	20	84,012	23	0	23	Windraw Composting	MRF	12.65	2.3	1.38	6.67	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.05	No	No	No	No	Oct,2026	
52	Murshidabad	Beldanga	14	29,182	7	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.20	Yes	Yes	Yes	No	March, 2026	
53	Murshidabad	Berhampore	28	1,95,363	66	0	66	Windraw Composting	MRF	36.3	6.6	3.96	19.14	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	10.95	No	No	No	No	Nov,2026	
54	Murshidabad	Dhuliyan	21	95,706	18	0	18	Windraw Composting	MRF	9.9	1.8	1.08	5.22	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.19	No	No	No	No	Oct,2026	
55	Murshidabad	Domkol	21	1,21,927	24	0	24	Windraw Composting	MRF	13.2	2.4	1.44	6.96	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.38	No	No	No	No	Oct,2026	
56	Murshidabad	Jangipur	21	88,165	29	0	29	Windraw Composting	MRF	15.95	2.9	1.74	8.41	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	5.26	No	No	No	No	Oct,2026	
57	Murshidabad	Jiaganj-Azimganj	17	51,790	15	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.79	No	No	No	No	Oct,2026	
58	Murshidabad	Kandi	18	55,632	12	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.08	No	No	No	No	Dec,2026	
59	Murshidabad	Murshidabad	16	44,064	16	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.19	Yes	Yes	Yes	Yes	June, 2026	
60	Nadia	Birnagar	14	30799	10	8	2	Windraw Composting	MRF	5.5	1	0.6	2.9	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	4.4	0.48	0.8	2.32	1.08	Yes	Yes	Yes	Yes	Dec, 2025	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to September, 2025																													
										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
61	Nadia	Chakdaha	21	95,203	19	0	19	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.05	Yes	Yes	Yes	Yes	May, 2026	
62	Nadia	Cooper's Camp	12	18,839	5	0	5	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.88	Yes	Yes	Yes	Yes	Dec, 2025	
63	Nadia	Gayeshpur	18	58,998	16	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.19	Yes	Yes	Yes	Yes	Dec, 2025	
64	Nadia	Haringhata	17	45,953	12	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.19	No	No	No	No	Nov,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
65	Nadia	Kalyani	21	1,00,620	50	0	50	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	6.57	Yes	No	No	No	Oct, 2026	
66	Nadia	Krishnanagar	25	1,53,062	90	120	-30	Windraw Composting	MRF	49.5	9	5.4	26.1	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	66	7.2	12	34.8	13.14	No	No	No	No	Oct,2026	
67	Nadia	Nabadwip	24	1,25,528	36	16	20	Windraw Composting	MRF	19.8	3.6	2.16	10.44	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	8.8	0.96	1.6	4.64	6.57	Yes	Yes	No	No	June, 2026	
68	Nadia	Ranaghat	20	75,365	20	0	20	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.74	Yes	Yes	No	No	June, 2026	
69	Nadia	Santipur	24	1,51,777	40	0	40	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	9.09	Yes	Yes	No	No	June, 2026	
70	Nadia	Taherpur NAA	13	20,894	5	4.1	0.9	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.255	0.246	0.41	1.189	0.55	Yes	Yes	Yes	Yes	Dec, 2025	
71	North 24 Parganas	Ashoknagar-Kalyangarh	23	1,21,592	35	6	29	Windraw Composting	MRF	19.25	3.5	2.1	10.15	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	3.3	0.36	0.6	1.74	5.26	No	No	No	No	June,2026	
72	North 24 Parganas	Baduria	17	52,500	6	4	2	Windraw Composting	MRF	3.3	0.6	0.36	1.74	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.2	0.24	0.4	1.16	0.65	Yes	Yes	Yes	Yes	Apr, 2026	
73	North 24 Parganas	Baranagar	34	2,45,213	134	554	0	Windraw Composting & Bio methanation	MRF	304.7	55.4	33.24	160.66	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	304.7	33.24	55.4	160.66	70.91	Yes	Yes	Yes	Yes	Started	
74	North 24 Parganas	Dum Dum	35	2,78,435	163																								
75	North 24 Parganas	South DumDum	24	1,52,783	40																								
76	North 24 Parganas	North Dum Dum	23	1,25,058	53																								
77	North 24 Parganas	New Barrackpur	35	3,85,867	164																								
78	North 24 Parganas	Kamarhati	41	6,34,107	287	0	287	Windraw Composting	MRF	157.85	55.4	33.24	160.66	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	17.52	Yes	Yes	Yes	No	Mary, 2026	
79	North 24 Parganas	Barasat	22	1,08,864	42	0	42	Windraw Composting	MRF	23.1	4.2	2.52	12.18	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	22.23	Yes	Yes	Yes	Yes	Mar, 2026	
80	North 24 Parganas	Barrackpore	22	1,14,786	50	0	50	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.48	Yes	No	No	No	Nov, 2026	
81	North 24 Parganas	Basirhat	21	85,336	35	53	-18	Windraw Composting	MRF	19.25	3.5	2.1	10.15	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	29.15	3.18	5.3	15.37	6.13	Yes	Yes	Yes	Yes	Apr, 2026	
82	North 24 Parganas	Bhatpara	17	45,392	12	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	22.45	No	No	No	No	Oct,2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to September, 2025																													
										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
83	North 24 Parganas	Bidhannagar Municipal Corporation	24	1,47,221	**44**	0	44	Bio-CNG	MRF	24.2	4.4	2.64	12.76	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	38.33	No	No	No	No	Dec, 2026	
84	North 24 Parganas	Bongaon	23	1,24,851	**38**	31	7	Windraw Composting	MRF	20.9	3.8	2.28	11.02	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	17.05	1.86	3.1	8.99	6.79	No	No	No	No	Oct,2026	
85	North 24 Parganas	Garulia	35	331163	**128**	0	128	Windraw Composting	MRF	70.4	12.8	7.68	37.12	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	3.92	Yes	No	No	No	Sept, 2026	
86	North 24 Parganas	Gobardanga	24	1,29,576	**37**	0	37	Windraw Composting	MRF	20.35	3.7	2.22	10.73	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.04	Yes	Yes	Yes	Yes	June, 2026	
87	North 24 Parganas	Habra	22	1,08,496	**38**	0	38	Windraw Composting	MRF	20.9	3.8	2.28	11.02	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	7.67	No	No	No	No	Jun,2026	
88	North 24 Parganas	Halisahar	28	1,96,127	**62**	0	62	Windraw Composting	MRF	34.1	6.2	3.72	17.98	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.69	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
89	North 24 Parganas	Kanchrapara	31	2,18,194	**72**	0	72	Windraw Composting	MRF	39.6	7.2	4.32	20.88	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	5.90	No	No	No	No	Oct,2026	
90	North 24 Parganas	Khardah	20	76,879	**22**	0	22	Windraw Composting	MRF	12.1	2.2	1.32	6.38	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.08	Yes	No	No	No	Sept, 2026	
91	North 24 Parganas	Madhyamgram	23	1,32,806	**46**	16	30	Windraw Composting	MRF	25.3	4.6	2.76	13.34	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	8.8	0.96	1.6	4.64	9.86	Yes	No	No	No	Sept, 2026	
92	North 24 Parganas	Naihati	34	2,49,142	**30**	0	30	Windraw Composting	MRF	16.5	3	1.8	8.7	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	11.72	Yes	Yes	Yes	Yes	May, 2026	
93	North 24 Parganas	North Barrackpore	35	3,77,351	**127**	0	127	Windraw Composting	MRF	69.85	12.7	7.62	36.83	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	7.99	Yes	No	No	No	Sept, 2026	
94	North 24 Parganas	Panihati	35	4,03,316	**287**	0	287	Windraw Composting	MRF	157.85	28.7	17.22	83.23	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	19.27	No	No	No	No	Dec,2026	
95	North 24 Parganas	Taki	16	38,263	**9**	8.4	0.6	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	4.62	0.504	0.84	2.436	1.53	Yes	Yes	Yes	Yes	Feb, 2026	
96	North 24 Parganas	Titagarh	23	1,16,541	**42**	0	42	Windraw Composting	MRF	23.1	4.2	2.52	12.18	Local Farmers/Hoticulture / Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.22	Yes	No	No	No	Nov, 2026	
97	Paschim Midnapore	Chandrakona	12	23,629	**8**	0	8	Windraw Composting	MRF	4.4	0.8	0.48	2.32	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.92	Yes	Yes	Yes	Yes	Dec, 2025	
98	Paschim Midnapore	Ghatal	17	54,591	**17**	0	17	Windraw Composting	MRF	9.35	1.7	1.02	4.93	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.92	No	No	No	No	Oct,2026	
99	Jhargram	Jhargram	18	61,682	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.12	Yes	Yes	Yes	Yes	May, 2026	
100	Paschim Midnapore	Kharagpur	35	2,07,604	**40**	25	15	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	13.75	1.5	2.5	7.25	8.98	Yes	Yes	Yes	Yes	Jun, 2026	
101	Paschim Midnapore	Kharar	10	12,220	**4**	0	4	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.59	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
102	Paschim Midnapore	Khirpai	10	16,385	**5**	0	5	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.74	Yes	Yes	No	No	March, 2026	
103	Paschim Midnapore	Midnapore	25	1,69,127	**62**	0	62	Windraw Composting	MRF	34.1	6.2	3.72	17.98	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	10.07	Yes	Yes	No	No	June, 2026	
104	Paschim Midnapore	Ramjibonpur	11	19,611	**5**	0	5	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.77	Yes	Yes	Yes	Yes	March, 2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to September, 2025

										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
105	Purba Midnapore	Contai	21	92,226	**40**	0	40	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	6.57	Yes	Yes	No	No	Nov, 2026	
106	Purba Midnapore	Egra	14	30,148	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.60	Yes	Yes	No	No	Jun, 2026	
107	Purba Midnapore	Haldia	29	2,00,827	**80**	80	0	Windraw Composting	MRF	44	8	4.8	23.2	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	44	4.8	8	23.2	8.76	Yes	Yes	Yes	Yes	Started	
108	Purba Midnapore	Panskura	18	57,932	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.97	No	No	No	No	Oct, 2026	
109	Purba Midnapore	**Tamralipta**	20	65,312	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.69	No	No	No	No	Oct, 2026	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Sept, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
110	Jhalda	Jhalda	12	19,540	**4**	0	4	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.71	No	No	No	No	Oct,2026	
111	Purulia	Purulia	23	1,21,067	**16**	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0		2.19	No	No	No	No	Dec,2026	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Sept, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
112	Purulia	Raghunathpur	13	25,621	**7**	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.20	No	No	No	No	Oct,2026	
113	South 24 parganas	Baruipur	17	53,128	**22**	0	22	Windraw Composting	MRF	12.1	2.2	1.32	6.38	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.68	Yes	Yes	No	No	Sep, 2026	
114	South 24 parganas	Budge Budge	20	76,858	**24**	0	24	Windraw Composting	MRF	13.2	2.4	1.44	6.96	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.29	Yes	Yes	No	No	May, 2026	
115	South 24 parganas	Diamond Harbour	16	43,169	**12**	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.14	Yes	Yes	Yes	No	May, 2026	
116	South 24 parganas	Jaynagar Majilpur	14	25,922	**6**	4	2	Windraw Composting & Bio Gas	MRF	3.3	0.6	0.36	1.74	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	1	1.2	0.24	0.4	1.16	0.99	Yes	Yes	Yes	Yes	Dec, 2025	
117	South 24 parganas	Maheshtala	35	4,49,423	**168**	5	163	Vermi Compost	MRF	92.4	16.8	10.08	48.72	Local Farmers/Hoticulture / Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	2.75	0.3	0.5	1.45	23.00	Yes	No	No	No	Sept, 2026	
118	South 24 parganas	Pujali	16	37,040	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.38	Yes	Yes	Yes	Yes	May, 2026	
119	South 24 parganas	Rajpur- Sonarpur	35	4,23,724	**279**	0	279	Windraw Composting & Bio Gas	MRF	153.45	27.9	16.74	80.91	Local Farmers/Hoticulture / Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		0	0	0	0	38.16	No	No	No	No	Oct,2026	
120	Uttar Dinajpur	Dalkhola	16	37,063	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.89	Yes	Yes	Yes	Yes	Apr, 2026	
121	Uttar Dinajpur	Islampur	17	54,340	**14**	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.38	Yes	Yes	No	No	May, 2026	
122	Uttar Dinajpur	Kaliyaganj	17	53,530	**22**	0	22	Windraw Composting	MRF	12.1	2.2	1.32	6.38	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.27	Yes	Yes	Yes	Yes	Apr, 2026	
123	Uttar Dinajpur	Raiganj	27	1,83,612	**60**	0	60	Windraw Composting	MRF	33	6	3.6	17.4	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	10.40	Yes	Yes	Yes	No	March, 2026	
124	Howrah	Howrah MC	50	10,70,645	**568**	10	558	Windraw Composting	MRF	312.4	56.8	34.08	164.72	Local Farmers/Hoticulture / Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	5.5	0.6	1	2.9	77.75	No	No	No	No	Dec,2026	
125	Howrah	Bally	35	2,91,916	**112**	0	112	Windraw Composting	MRF	61.6	11.2	6.72	32.48	Local Farmers/Hoticulture / Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	15.32	No	No	No	No	Dec,2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to September, 2025																												
										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
126	Jalpaiguri	Maynaguri	17	36,263	**8**	0	8	Windraw Composting	MRF	4.4	0.8	0.48	2.32	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.39	Yes	Yes	Yes	Yes	Dec, 2025	
127	Alipurduar	Falakata	18	54,039	**14**	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.41	Yes	Yes	Yes	Yes	March, 2026	
128	Kolkata	Kolkata MC	144	4594718	**3668**	609	3059	Windrow Compost & Bio-CNG	Material Recovery Facility & Plastic Processing Unit	2017.4	366.8	220.08	1063.72	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	5	500	2	0	102	600.00	No	No	No	No	Dec,2026	
	Total =		**2997**	**21532295**	**10227**	**2213.5**	**8013.5**																**1554.41**						

	Status and							(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
Sl. No.	(i) Name of District	ULB				Waste being processed per day (TPD)	Gap in processing (TPD)	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of 100% processing of Fresh waste	Proposal
1	Bankura	Bankura	24	1,37,386	**40**	0	40		0	0	0	0	Dec, 2025	6.68	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
2	Bankura	Bishnupur	19	67,783	**14**	0	14						Sept,2025	2.85	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
3	Bankura	Sonamukhi	15	34,228	**9**	0	9						Oct,2025	1.42	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
4	Paschim Bardhaman	Asansol MC	106	11,56,387	**566**	0	566						Dec, 2025	76.65	Yes	Yes	Yes	No	March, 2026	Work order issued to an agency for setting up of fresh waste processing unit at the ULB. After reclaimation of land from legacy waste the infrastrcure work for setting up of fresh waste processing unit will be started.
5	Purba Bardhaman	Barddhaman	35	3,14,638	**98**	0	98						Dec, 2025	18.40	No	No	No	No	Oct,2026	After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
6	Purba Bardhaman	Dainhat	14	24,397	**7**	0	7						Dec, 2025	1.16	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Sept, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
7	Paschim Bardhaman	Durgapur MC	43	5,66,517	**244**	0	244		0	0	0	0	Dec, 2025	33.29	Yes	Yes	Yes	No	Sept,2026	Work order issued to an agency for setting up of fresh waste processing unit at the ULB. Due to local agitation the agency could not start infrastrcure work for setting up of fresh waste processing unit at the reclaimed land of the dumpsite. For this, a feasible land is under identification.
8	Purba Bardhaman	Guskhara	16	35,374	**9**	0	9						Sept,2025	1.31	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
9	Purba Bardhaman	Kalna	18	56,722	**15**	0	15		0	0	0	0	Sept,2025	2.52	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
10	Purba Bardhaman	Katwa	20	81,615	**26**	0	26						Dec, 2025	5.16	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
11	Purba Bardhaman	Memari	16	41,455	**11**	0	11		0	0	0	0	Sept,2025	1.75	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
12	Birbhum	Bolpur	22	80,210	31	0	31		0	0	0	0	Dec, 2025	6.02	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
13	Birbhum	Dubrajpur	16	38,041	10	0	10						July,2025	1.70	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
14	Birbhum	Nalhati	16	41,244	9	0	9		0	0	0	0	Sept,2025	1.64	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
15	Birbhum	Rampurhat	18	57,833	15	0	15		0	0	0	0	Dec, 2025	3.07	Yes	Yes	No	No	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
16	Birbhum	Sainthia	16	44608	12	0	12		0	0	0	0	Sept,2025	2.08	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
17	Birbhum	Suri	21	90,314	26	0	26		0	0	0	0	Dec, 2025	4.05	Yes	Yes	No	No	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
18	Cooch Behar	Coochbehar	20	77935	20	0	20		0	0	0	0	Sept,2025	3.07	Yes	No	No	No	Sept, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
19	Cooch Behar	Dinhata	16	36,124	9	3	6		1.65	0.18	0.3	0.87	July,2025	1.70	Yes	Yes	Yes	Yes	Dec, 2025	Civil constrction for setting up of fresh waste processing unit has been completed. Procurement of machineries are under process.
20	Cooch Behar	Haldibari	11	14,404	4	2.5	1.5		1.375	0.15	0.25	0.725	Sept,2025	0.57	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
21	Cooch Behar	Mathabhanga	12	23,895	9	5	4		2.75	0.3	0.5	1.45	Sept,2025	1.56	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit was started but due to public agiatation it was disrupted.
22	Cooch Behar	Mekhliganj	9	9,123	5	4	1		2.2	0.24	0.4	1.16	July,2025	0.51	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
23	Cooch Behar	Tufanganj	12	20,998	7	6	1		3.3	0.36	0.6	1.74	Sept,2025	0.88	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
24	Dakshin Dinajpur	Balurghat	25	1,51,299	42	0	42		0	0	0	0	Sept,2025	8.21	Yes	Yes	Yes	Yes	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
25	Dakshin Dinajpur	Buniadpur	14	30183	8	0	8		0	0	0	0	Sept,2025	1.31	Yes	Yes	Yes	Yes	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
26	Dakshin Dinajpur	Gangarampur	18	56,217	14	0	14		0	0	0	0	Sept,2025	3.07	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
27	Darjeeling	Darjeeling	32	1,20,414	24	0	24		0	0	0	0	Dec,2025	3.83	No	No	No	No	Oct,2026	Constrction of allied works for setting up of fresh waste processing unit is in progress. After completion of those works, Tender to be floated for setting up of fresh waste processing plant.

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
28	Kalimpong	Kalimpong	23	49,403	**13**	0	13		0	0	0	0	Dec,2025	2.08	No	No	No	No	Oct,2026	Tender to be floated for engagement of agency for setting up fresh waste processing plant.
29	Darjeeling	Kurseong	20	42,346	**7**	0	7		0	0	0	0	Dec,2025	1.20	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process. Approach road construction completed.
30	Darjeeling	Mirik	9	11,513	**4**	0	4		0	0	0	0	Dec,2025	0.46	No	No	No	No	Oct,2026	Recently, land identied and process for taking possession is in progress. DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation
31	Darjeeling	Siliguri MC	47	5,13,264	**297**	297	0		163.35	17.82	29.7	86.13	Dec,2025	39.20	Yes	Yes	Yes	Yes	Started	Work order issued to an agency for setting up of fresh waste processing unit. Partial plant installed and in operation and Infrsatructre Work for remaining plant is in progress.
32	Howrah	**Uluberia**	32	2,32,290	**86**	0	86		0	0	0	0	Dec, 2025	13.14	Yes	Yes	Yes	No	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender to be floated for engagement of agency for setting up of fresh waste processing plant.
33	Hooghly	Arambagh	19	66,175	**16**	0	16		0	0	0	0		3.15	No	No	No	No	Oct,2026	State Government has provided a land to the ULB for setting up of fresh waste processing unit. But due to public agitation further action could not be taken. Local administration is trying to reslove the matter.Expected that the matter will be resloved within Oct, 2025. After that, tender will be folated for enagagement of agency for setting up of freh waste processing plant.
34	Hooghly	Baidyabati	23	1,21,110	**50**	50	0		27.5	3	5	14.5	NA	5.48	Yes	Yes	Yes	Yes	Started	Plant in operation.
35	Hooghly	Bansberia	22	1,03,920	**30**	0	30		0	0	0	0	Jan,2026	4.38	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
36	Hooghly	Bhadreswar	22	1,01,477	**26**	12	14		6.6	0.72	1.2	3.48	Dec,2025	3.50	Yes	Yes	Yes	Yes	March, 2026	Work order issued to an agency for setting up of fresh waste processing unit. Infrsatructre Work is in progress.
37	Hooghly	Champdany	22	1,11,251	**19**	19	0		10.45	1.14	1.9	5.51	NA	2.08	Yes	Yes	Yes	Yes	Started	PLant in operation.
38	Hooghly	Chandernagore municipal corporation	33	1,66,867	**52**	0	52		0	0	0	0	Dec, 2025	7.82	No	No	No	No	Oct,2026	Tender to be floated for engagement of agency for setting up fresh waste processing plant. Tender document prepared.
39	Hooghly	Dankuni	21	94,966	**32**	0	32		0	0	0	0	Dec,2025	4.60	Yes	Yes	Yes	Yes	Started	Work order issued to an agency for setting up of fresh waste processing unit. Infrsatructre Work is in progress.
40	Hooghly	Hooghly Chinsurah	30	1,77,259	**56**	0	56		0	0	0	0	Dec, 2025	8.21	No	No	No	No	Oct,2026	Tender to be floated for engagement of agency for setting up fresh waste processing plant. Tender document prepared.

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
41	Hooghly	Konnagar	20	76,172	26	25.5	0.5		14.025	1.53	2.55	7.395	NA	2.79	Yes	Yes	Yes	Yes	Started	Plant in operation.
42	Hooghly	Rishra	23	1,24,585	45	45	0		24.75	2.7	4.5	13.05	Sept,2025	5.91	Yes	Yes	Yes	Yes	March, 2026	Tender to be floated for upgradation of existing infrastracture for processing the remaing waste. Tender document under preparation.
43	Hooghly	Serampore	29	1,83,339	95	95	0		52.25	5.7	9.5	27.55	NA	10.40	Yes	Yes	Yes	Yes	Started	Plant in operation.
44	Hooghly	Tarakeswar	15	30,947	10	0	10		0	0	0	0	Dec, 2025	1.44	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit.DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
45	Hooghly	Uttarpara Kotrung	24	1,62,386	72	72	0		39.6	4.32	7.2	20.88	Dec.,2025	7.88	Yes	Yes	Yes	Yes	Started	Plant in operation.
46	Alipurduar	Alipurduar	20	65,232	21	21	0		11.55	1.26	2.1	6.09	NA	2.30	Yes	Yes	Yes	Yes	Started	Plant in operation.
47	Jalpaiguri	Dhupguri	16	44,719	7	0	7		0	0	0	0	Dec, 2025	1.15	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within June, 2025. After that the tender will be floated for enagagement of agency for setting up of freh waste processing plant.
48	Jalpaiguri	Jalpaiguri	25	1,07,341	38	3	35						Sept,2025	6.79	Yes	Yes	No	No	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
49	Jalpaiguri	Mal	15	25,218	6	0	6						Sept,2025	0.99	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process .
50	Malda	English Bazar	29	2,05,521	82	0	82						Sept,2025	16.97	Yes	Yes	Yes	No	Feb, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process .
51	Malda	Old Malda	20	84,012	23	0	23						Dec, 2025	4.05	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
52	Murshidabad	Beldanga	14	29,182	7	0	7						Sept,2025	1.20	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
53	Murshidabad	Berhampore	28	1,95,363	66	0	66						Dec, 2025	10.95	No	No	No	No	Oct,2026	After reclaimation of land from legacy waste the tender for infrastrcure work for setting up of fresh waste processing unit will be floated.
54	Murshidabad	Dhuliyan	21	95,706	18	0	18						Dec, 2025	4.19	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
55	Murshidabad	Domkol	21	1,21,927	**24**	0	24						Dec, 2025	4.38	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
56	Murshidabad	Jangipur	21	88,165	**29**	0	29		0	0	0	0	Sept,2025	5.26	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
57	Murshidabad	Jiaganj-Azimganj	17	51,790	**15**	0	15						Oct, 2025	1.79	No	No	No	No	Oct,2026	State Government identified a land for setting up of fresh waste processing unit for Jiagunj-Azimgunj Municipality, but due to local agitation further action could not be taken. Local administration are giving their best effort to reslove the matter.Expected that by Aug,2025 the matter will be resloved. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
58	Murshidabad	Kandi	18	55,632	**12**	0	12						Dec, 2025	2.08	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within July, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
59	Murshidabad	Murshidabad	16	44,064	**16**	0	16		0	0	0	0	Dec, 2025	2.19	Yes	Yes	Yes	Yes	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
60	Nadia	Birnagar	14	30799	**10**	8	2		4.4	0.48	0.8	2.32	Sept,2025	1.08	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
61	Nadia	Chakdaha	21	95,203	**19**	0	19						Dec, 2025	4.05	Yes	Yes	Yes	Yes	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
62	Nadia	Cooper's Camp	12	18,839	**5**	0	5						Dec.,2025	0.88	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
63	Nadia	Gayeshpur	18	58,998	**16**	0	16						Sept,2025	2.19	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
64	Nadia	Haringhata	17	45,953	**12**	0	12						Dec, 2025	2.19	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
65	Nadia	Kalyani	21	1,00,620	**50**	0	50		0	0	0	0	Sept, 2025	6.57	Yes	No	No	No	Sept, 2026	Tender floated for enagagement of agency for setting up of fresh waste processing plant.
66	Nadia	Krishnanagar	25	1,53,062	**90**	120	-30		66	7.2	12	34.8	NA	13.14	No	No	No	No	Oct,2026	Achieved

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
67	Nadia	Nabadwip	24	1,25,528	**36**	16	20		8.8	0.96	1.6	4.64	Dec, 2025	6.57	Yes	Yes	No	No	June, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
68	Nadia	Ranaghat	20	75,365	**20**	0	20		0	0	0	0	Dec, 2025	2.74	Yes	Yes	No	No	June, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
69	Nadia	Santipur	24	1,51,777	**40**	0	40						Dec, 2025	9.09	Yes	Yes	No	No	June, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
70	Nadia	Taherpur NAA	13	20,894	**5**	4.1	0.9		2.255	0.246	0.41	1.189	Sept,2025	0.55	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
71	North 24 Parganas	Ashoknagar-Kalyangarh	23	1,21,592	**35**	6	29		3.3	0.36	0.6	1.74	Sept,2025	5.26	No	No	No	No	Oct,2026	Work order issued to an agency for setting up of fresh waste processing unit at dumpsite of Ashokenagar-Kalyangarh municipality for Ashokenagar-Kalyangarh municipality & Habra municipality. After, reclaimation of land through bio-mining & bio-remediation of legacy waste, installation of infrastrucre for fresh waste processing unit will be started.
72	North 24 Parganas	Baduria	17	52,500	**6**	4	2		2.2	0.24	0.4	1.16	Dec,2025	0.65	Yes	Yes	Yes	Yes	Dec, 2025	Work order issued for engagement of agency for setting up fresh waste processing plant. Land development work is in progress.
73	North 24 Parganas	Baranagar	34	2,45,213	**134**	554	0		304.7	33.24	55.4	160.66	Jan,2026	70.91	Yes	Yes	Yes	Yes	Started	Work order issued to an agency for setting up of fresh waste processing unit at Promodnagar dumpsite for these 5 ULBs. Infrastrure Work is in progress. Gradually, the infrstrucre being extended at the reclaimed land being available after legacy waste processing. Partial processing is in progress.
74	North 24 Parganas	Dum Dum	35	2,78,435	**163**										Yes	Yes	Yes	Yes	Started	
75	North 24 Parganas	South DumDum	24	1,52,783	**40**										Yes	Yes	Yes	Yes	Started	
76	North 24 Parganas	North Dum Dum	23	1,25,058	**53**										Yes	Yes	Yes	Yes	Started	
77	North 24 Parganas	New Barrackpur	35	3,85,867	**164**										Yes	Yes	Yes	Yes	Started	
78	North 24 Parganas	Kamarhati	41	6,34,107	**287**	0	287						Sept,2025	17.52	Yes	Yes	Yes	No	March, 2026	Work order issued to an agency for setting up of fresh waste processing unit at Kamarhati dumpsite for the ULB.After reclaimation of land from legacy waste the infrastrcure work for setting up of fresh waste processing unit will be started.
79	North 24 Parganas	Barasat	22	1,08,864	**42**	0	42						Sept,2025	22.23	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
80	North 24 Parganas	Barrackpore	22	1,14,786	50	0	50		0	0	0	0	Dec,2026	5.48	Yes	No	No	No	Sept, 2026	Tender floated for enagagement of agency for setting up of fresh waste processing plant.
81	North 24 Parganas	Basirhat	21	85,336	35	53	-18		29.15	3.18	5.3	15.37	Dec.,2025	6.13	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
82	North 24 Parganas	Bhatpara	17	45,392	12	0	12						Dec,2026	22.45	No	No	No	No	Oct,2026	Tender to be floated for engagement of an agency for upgradation of Civil and/or Electro-Mechanical construction/installation, for processing of fresh waste at the identified land of Bhatpara Municipality. Prepartion of tender document is under process.
83	North 24 Parganas	Bidhannagar Municipal Corporation	24	1,47,221	44	0	44						Dec,2025	38.33	No	No	No	No	Dec, 2026	DPR prepared. Tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
84	North 24 Parganas	Bongaon	23	1,24,851	38	31	7		17.05	1.86	3.1	8.99	Dec, 2025	6.79	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
85	North 24 Parganas	Garulia	35	331163	128	0	128		0	0	0	0	Dec,2026	3.92	Yes	No	No	No	Sept, 2026	Tender to be floated for engagement of an agency for upgradation of Civil and/or Electro-Mechanical construction/installation, for processing of fresh waste at the identified land of Bhatpara Municipality. Prepartion of tender document is under process.
86	North 24 Parganas	Gobardanga	24	1,29,576	37	0	37		0	0	0	0	Sept,2025	2.04	Yes	Yes	Yes	Yes	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
87	North 24 Parganas	Habra	22	1,08,496	38	0	38						Sept,2025	7.67	No	No	No	No	Oct,2026	Work order issued to an agency for setting up of fresh waste processing unit at dumpsite of Ashokenagar-Kalyangarh municipality for Ashokenagar-Kalyangarh municipality & Habra municipality. After, reclaimation of land through bio-mining & bio-remediation of legacy waste, installation of infrastrucre for fresh waste processing unit will be started.
88	North 24 Parganas	Halisahar	28	1,96,127	62	0	62		0	0	0	0	Feb,2026	5.69	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
89	North 24 Parganas	Kanchrapara	31	2,18,194	72	0	72		0	0	0	0	Oct,2026	5.90	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
90	North 24 Parganas	Khardah	20	76,879	22	0	22		0	0	0	0	Dec.,2025	5.08	Yes	No	No	No	Sept, 2026	Tender to be floated for engagement of an agency for upgradation of Civil and/or Electro-Mechanical construction/installation, for processing of fresh waste at the identified land of Bhatpara Municipality. Prepartion of tender document is under process.
91	North 24 Parganas	Madhyamgram	23	1,32,806	46	16	30		8.8	0.96	1.6	4.64	Dec,2026	9.86	Yes	No	No	No	Sept, 2026	Tender floated for engagement of agency for setting up of fresh waste processing plant.
92	North 24 Parganas	Naihati	34	2,49,142	30	0	30		0	0	0	0	Dec, 2025	11.72	Yes	Yes	Yes	Yes	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.

Sl. No.	Status and (i) Name of District	ULB				Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
93	North 24 Parganas	North Barrackpore	35	3,77,351	**127**	0	127						Dec,2025	7.99	Yes	No	No	No	Sept, 2026	As per decision, wastes of North Barrackpore Municipality shall be processed at the dump land of Titagarh Muinicipality on Cluster Mode.
94	North 24 Parganas	Panihati	35	4,03,316	**287**	0	287						Dec,2026	19.27	No	No	No	No	Oct,2026	Tender to be floated for engagement of an agency for setting up of fresh waste processing plants, on the reclaimed land at Ramchandrapur and at the identified land at Mahishpota Mouza. Prepartion of tender document under process.
95	North 24 Parganas	Taki	16	38,263	**9**	8.4	0.6		4.62	0.504	0.84	2.436	Dec,2025	1.53	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
96	North 24 Parganas	Titagarh	23	1,16,541	**42**	0	42		0	0	0	0	Sept,2026	5.22	Yes	No	No	No	Sept, 2026	Tender floated for engagement of agency for setting up of fresh waste processing unit, on integrated module, where the selected agency shall process both the legacy waste and fresh waste simultaneously. After reclamation of land of the dumpyard through biomining of the existing legacy waste, they shall set up their processing units over the land reclaimed. 2nd call of the tender not matured. 3rd call shall be invited shortly.
97	Paschim Midnapore	Chandrakona	12	23,629	**8**	0	8						Sept,2025	0.92	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
98	Paschim Midnapore	Ghatal	17	54,591	**17**	0	17						Dec, 2025	2.92	No	No	No	No	Oct,2026	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Aug, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
99	Jhargram	Jhargram	18	61,682	**15**	0	15						Dec, 2025	3.12	Yes	Yes	Yes	Yes	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
100	Paschim Midnapore	Kharagpur	35	2,07,604	**40**	25	15		13.75	1.5	2.5	7.25	Sept,2025	8.98	Yes	Yes	Yes	Yes	March, 2026	Work order issued to an agency for setting up of fresh waste processing unit. Infrsatructre Work started but stopped due to local agitation. Effort given to reslove the matter and start the work at the earliest.
101	Paschim Midnapore	Kharar	10	12,220	**4**	0	4						Dec,2025	0.59	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
102	Paschim Midnapore	Khirpai	10	16,385	**5**	0	5						Dec,2025	0.74	Yes	Yes	No	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
103	Paschim Midnapore	Midnapore	25	1,69,127	**62**	0	62						Jan,2026	10.07	Yes	Yes	No	No	June, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
104	Paschim Midnapore	Ramjibonpur	11	19,611	**5**	0	5						Sept,2025	0.77	Yes	Yes	Yes	Yes	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
105	Purba Midnapore	Contai	21	92,226	**40**	0	40						Dec, 2025	6.57	Yes	Yes	No	No	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
106	Purba Midnapore	Egra	14	30,148	9	0	9						Dec, 2025	1.60	Yes	Yes	No	No	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
107	Purba Midnapore	Haldia	29	2,00,827	80	80	0		44	4.8	8	23.2	NA	8.76	Yes	Yes	Yes	Yes	Started	Achieved
108	Purba Midnapore	Panskura	18	57,932	11	0	11		0	0	0	0	Dec, 2025	1.97	No	No	No	No	Oct,2026	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Aug, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
109	Purba Midnapore	Tamralipta	20	65,312	15	0	15		0	0	0	0	Dec, 2025	2.69	No	No	No	No	Oct,2026	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Sept, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
110	Jhalda	Jhalda	12	19,540	4	0	4						Dec, 2025	0.71	No	No	No	No	Oct,2026	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within March, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
111	Purulia	Purulia	23	1,21,067	16	0	16						Dec, 2025	2.19	No	No	No	No	Oct,2026	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Sept, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
112	Purulia	Raghunathpur	13	25,621	7	0	7						Dec, 2025	1.20	No	No	No	No	Oct,2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
113	South 24 parganas	Baruipur	17	53,128	22	0	22		0	0	0	0	Dec,2026	2.68	Yes	Yes	No	No	June, 2026	After reclaimation of land from legacy waste the tender for infrastrcure work for setting up of fresh waste processing unit will be floated.
114	South 24 parganas	Budge Budge	20	76,858	24	0	24		0	0	0	0	Dec, 2025	3.29	Yes	Yes	No	No	May, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency .
115	South 24 parganas	Diamond Harbour	16	43,169	12	0	12		0	0	0	0	Dec,2025	2.14	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
116	South 24 parganas	Jaynagar Majilpur	14	25,922	6	4	2	1	1.2	0.24	0.4	1.16	Sept,2025	0.99	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
117	South 24 parganas	Maheshtala	35	4,49,423	168	5	163		2.75	0.3	0.5	1.45	Dec,2026	23.00	Yes	No	No	No	Sept, 2026	Tender floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
118	South 24 parganas	Pujali	16	37,040	11	0	11						Dec,2025	1.38	Yes	Yes	Yes	Yes	March, 2026	Tender floated for engagement of agency for setting up of fresh waste processing plant.

Sl. No.	(i) Name of District	ULB	Status and			Waste being processed per day (TPD)	Gap in processing (TPD)	(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste							
								Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	DPR Preparation (Yes/ No)	Tender Published (Yes/ No)	Work Order Issued (Yes/ No)	Work Started (Yes/ No)	Time line for starting of processing of remaining waste	Proposal
119	South 24 parganas	Rajpur-Sonarpur	35	4,23,724	279	0	279		0	0	0	0	Dec,2025	38.16	No	No	No	No	Oct,2026	Tender shall be floated by the ULB itself, for engagement of agency for setting up fresh waste processing unit. Tender document prepared.
120	Uttar Dinajpur	Dalkhola	16	37,063	11	0	11		0	0	0	0	Dec,2025	1.89	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
121	Uttar Dinajpur	Islampur	17	54,340	14	0	14		0	0	0	0	Dec.,2025	2.38	Yes	Yes	No	No	March, 2026	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
122	Uttar Dinajpur	Kaliyaganj	17	53,530	22	0	22		0	0	0	0	Dec,2025	4.27	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
123	Uttar Dinajpur	Raiganj	27	1,83,612	60	0	60		0	0	0	0	Dec,2025	10.40	Yes	Yes	Yes	No	March, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
124	Howrah	Howrah MC	50	10,70,645	568	10	558		5.5	0.6	1	2.9	Dec,2026	77.75	No	No	No	No	Dec,2026	After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
125	Howrah	Bally	35	2,91,916	112	0	112		0	0	0	0	Dec,2026	15.32	No	No	No	No	Dec,2026	After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
126	Jalpaiguri	Maynaguri	17	36,263	8	0	8		0	0	0	0	Nov,2025	1.39	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
127	Alipurduar	Falakata	18	54,039	14	0	14		0	0	0	0	Nov,2025	2.41	Yes	Yes	Yes	Yes	Dec, 2025	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
128	Kolkata	Kolkata MC	144	4594718	3668	609	3059	5	500	2	0	102	Dec, 2026	600.00	No	No	No	No	Dec,2026	Bio-CNG and windraw compost plant to be set up for remaining wet waste and for remaining dry waste MRF to be set up.
	Total =		2997	21532295	10227	2213.5	8013.5	6	1379.825	98.09	160.15	566.435	Total =	1554.41						

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
1	Bankura	Bankura	24	1,37,386	61	4	57	Windraw Composting	Material Recovery Facility (MRF)	33.55	6.1	3.66	17.69	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		33.55	3.66	6.1	17.69	Dec, 2025	6.68	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
2	Bankura	Bishnupur	19	67,783	26	0	26	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		14.3	1.56	2.6	7.54	Sept,2025	2.85	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
3	Bankura	Sonamukhi	15	29,085	13	0	13	Windraw Composting	MRF	7.15	1.3	0.78	3.77	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		7.15	0.78	1.3	3.77	Oct,2025	1.42	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
4	Paschim Bardhaman	Asansol MC	106	11,56,387	700	0	700	Windraw Composting	MRF	385	70	42	203	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		385	42	70	203	Dec, 2025	76.65	Work order issued to an agency for setting up of fresh waste processing unit at the ULB. After reclaimation of land from legacy waste the infrastrcure work for setting up of fresh waste processing unit will be started.
5	Purba Bardhaman	Barddhaman	35	3,14,638	168	0	168	Windraw Composting	MRF	92.4	16.8	10.08	48.72	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		92.4	10.08	16.8	48.72	Dec, 2025	18.40	After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
6	Purba Bardhaman	Dainhat	14	24,397	10.55	0	10.55	Windraw Composting	MRF	5.8025	1.055	0.633	3.0595	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		5.8025	0.633	1.055	3.0595	Dec, 2025	1.16	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within June, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
7	Paschim Bardhaman	Durgapur MC	43	5,66,517	304	25	279	Windraw Composting	MRF	167.2	30.4	18.24	88.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		167.2	18.24	30.4	88.16	Dec, 2025	33.29	Work order issued to an agency for setting up of fresh waste processing unit at the ULB. Due to local agitation the agency could not start infrastrcure work for setting up of fresh waste processing unit at the reclaimed land of the dumpsite. For this, a feasible land is under identification.
8	Purba Bardhaman	Guskhara	16	35,374	12	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		6.6	0.72	1.2	3.48	Sept,2025	1.31	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
9	Purba Bardhaman	Kalna	18	56,722	23	6	17	Windraw Composting	MRF	12.65	2.3	1.38	6.67	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		12.65	1.38	2.3	6.67	Sept,2025	2.52	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
10	Purba Bardhaman	Katwa	20	81,615	47.09	0	47.09	Windraw Composting	MRF	25.8995	4.709	2.8254	13.6561	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		25.8995	2.8254	4.709	13.6561	Dec, 2025	5.16	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within June, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
11	Purba Bardhaman	Memari	16	41,455	16	5	11	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		8.8	0.96	1.6	4.64	Sept,2025	1.75	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
12	Birbhum	Bolpur	22	80,210	54.98	17	37.98	Windraw Composting	MRF	30.239	5.498	3.2988	15.9442	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		30.239	3.2988	5.498	15.9442	Dec, 2025	6.02	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
13	Birbhum	Dubrajpur	16	38,041	15.54	0	15.54	Windraw Composting	MRF	8.547	1.554	0.9324	4.5066	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		8.547	0.9324	1.554	4.5066	July,2025	1.70	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
14	Birbhum	Nalhati	16	41,244	15	8	7	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		8.25	0.9	1.5	4.35	Sept,2025	1.64	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
15	Birbhum	Rampurhat	18	57,833	28	18	10	Windraw Composting	MRF	15.4	2.8	1.68	8.12	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		15.4	1.68	2.8	8.12	Dec, 2025	3.07	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
16	Birbhum	Sainthia	16	44,608	19	12	7	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		10.45	1.14	1.9	5.51	Sept,2025	2.08	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
17	Birbhum	Suri	21	90,314	37	11	26	Windraw Composting	MRF	20.35	3.7	2.22	10.73	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		20.35	2.22	3.7	10.73	Dec, 2025	4.05	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
18	Cooch Behar	Coochbehar	20	77,935	28	0	28	Windraw Composting	MRF	15.4	2.8	1.68	8.12	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		15.4	1.68	2.8	8.12	Sept,2025	3.07	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
19	Cooch Behar	Dinhata	16	36,124	15.52	7	8.52	Windraw Composting	MRF	8.536	1.552	0.9312	4.5008	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		8.536	0.9312	1.552	4.5008	July,2025	1.70	Civil constrction for setting up of fresh waste processing unit has been completed. Procurement of machineries are under process.
20	Cooch Behar	Haldibari	11	14,404	5.2	2.5	2.7	Windraw Composting	MRF	2.86	0.52	0.312	1.508	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		2.86	0.312	0.52	1.508	Sept,2025	0.57	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
21	Cooch Behar	Mathabhanga	12	23,890	14.27	8	6.27	Windraw Composting	MRF	7.8485	1.427	0.8562	4.1383	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		7.8485	0.8562	1.427	4.1383	Sept,2025	1.56	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
22	Cooch Behar	Mekhliganj	9	9,123	4.7	4	0.7	Windraw Composting	MRF	2.585	0.47	0.282	1.363	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		2.585	0.282	0.47	1.363	July,2025	0.51	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
23	Cooch Behar	Tufanganj	12	20,998	8	6	2	Windraw Composting	MRF	4.4	0.8	0.48	2.32	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		4.4	0.48	0.8	2.32	Sept,2025	0.88	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
24	Dakshin Dinajpur	Balurghat	25	1,51,299	75	25	50	Windraw Composting	MRF	41.25	7.5	4.5	21.75	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		41.25	4.5	7.5	21.75	Sept,2025	8.21	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
25	Dakshin Dinajpur	Buniadpur	14	34,280	12	7	5	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		6.6	0.72	1.2	3.48	Sept,2025	1.31	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
26	Dakshin Dinajpur	Gangarampur	18	56,175	28	14	14	Windraw Composting	MRF	15.4	2.8	1.68	8.12	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		15.4	1.68	2.8	8.12	Sept,2025	3.07	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
27	Darjeeling	Darjeeling	32	1,20,414	35	0	35	Windraw Composting	MRF	19.25	3.5	2.1	10.15	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		19.25	2.1	3.5	10.15	Dec,2025	3.83	Constrction of allied works for setting up of fresh waste processing unit is in progress. After completion of those works, Tender to be floated for setting up of fresh waste processing plant.
28	Kalimpong	Kalimpong	23	49,403	19	0	19	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		10.45	1.14	1.9	5.51	Dec,2025	2.08	Tender to be floated for engagement of agency for setting up fresh waste processing plant.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
29	Darjeeling	Kurseong	20	42,346	11	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		6.05	0.66	1.1	3.19	Dec,2025	1.20	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process. Approach road construction completed.
30	Darjeeling	Mirik	9	11,513	4.2	0	4.2	Windraw Composting	MRF	2.31	0.42	0.252	1.218	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		2.31	0.252	0.42	1.218	Dec,2025	0.46	Recently, land identied and process for taking possession is in progress. DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation
31	Darjeeling	Siliguri MC	47	5,13,264	358	200	158	Windraw Composting	MRF	196.9	35.8	21.48	103.82	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		196.9	21.48	35.8	103.82	Dec,2025	39.20	Work order issued to an agency for setting up of fresh waste processing unit. Partial plant installed and in operation and Infrsatructre Work for remaining plant is in progress.
32	Howrah	Uluberia Municipality	32	2,32,290	120	17	103	Windraw Composting	MRF	66	12	7.2	34.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		66	7.2	12	34.8	Dec, 2025	13.14	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender to be floated for engagement of agency for setting up of fresh waste processing plant.
33	Hooghly	Arambagh	19	66,175	28.76	7	21.76	Windraw Composting	MRF	15.818	2.876	1.7256	8.3404	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		15.818	1.7256	2.876	8.3404		3.15	State Government has provided a land to the ULB for setting up of fresh waste processing unit. But due to public agitation further action could not be taken. Local administration is trying to reslove the matter.Expected that the matter will be resloved within June, 2025. After that, tender will be folated for enagagement of agency for setting up of freh waste processing plant.
34	Hooghly	Baidyabati	23	1,21,110	50	50	0	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		27.5	3	5	14.5	NA	5.48	Plant in operation.
35	Hooghly	Bansberia	22	1,03,920	40	15	25	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		22	2.4	4	11.6	Jan,2026	4.38	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
36	Hooghly	Bhadreswar	22	1,01,477	32	12	20	Windraw Composting	MRF	17.6	3.2	1.92	9.28	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		17.6	1.92	3.2	9.28	Dec,2025	3.50	Work order issued to an agency for setting up of fresh waste processing unit. Infrsatructre Work is in progress.
37	Hooghly	Champdany	22	1,11,251	19	19	0	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		10.45	1.14	1.9	5.51	NA	2.08	PLant in operation.
38	Hooghly	Chandernagore municipal corporation	33	1,66,867	71.44	25	46.44	Bio-CNG	MRF	39.292	7.144	4.2864	20.7176	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	39.292	0	4.2864	7.144	20.7176	Dec, 2025	7.82	Tender to be floated for engagement of agency for setting up fresh waste processing plant. Tender document prepared.
39	Hooghly	Dankuni	21	94,966	42	0	42	Windraw Composting	MRF	23.1	4.2	2.52	12.18	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		23.1	2.52	4.2	12.18	Dec,2025	4.60	Work order issued to an agency for setting up of fresh waste processing unit. Infrsatructre Work is in progress.
40	Hooghly	Hooghly Chinsurah	30	1,77,259	75	16	59	Bio-CNG	MRF	41.25	7.5	4.5	21.75	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	41.25	0	4.5	7.5	21.75	Dec, 2025	8.21	Tender to be floated for engagement of agency for setting up fresh waste processing plant. Tender document prepared.
41	Hooghly	Konnagar	20	76,172	25.5	25.5	0	Windraw Composting	MRF	14.025	2.55	1.53	7.395	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		14.025	1.53	2.55	7.395	NA	2.79	Plant in operation.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
42	Hooghly	Rishra	23	1,24,585	54	45	9	Windraw Composting	MRF	29.7	5.4	3.24	15.66	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		29.7	3.24	5.4	15.66	Sept,2025	5.91	Tender to be floated for upgradation of existing infrastracture for processing the remaing waste. Tender document under preparation.
43	Hooghly	Serampore	29	1,83,339	95	95	0	Windraw Composting	MRF	52.25	9.5	5.7	27.55	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		52.25	5.7	9.5	27.55	NA	10.40	Plant in operation.
44	Hooghly	Tarakeswar	15	30,947	13.16	6	7.16	Windraw Composting	MRF	7.238	1.316	0.7896	3.8164	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		7.238	0.7896	1.316	3.8164	Dec, 2025	1.44	State Government identified the land for setting up of fresh waste processing unit.DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
45	Hooghly	Uttarpara Kotrung	24	1,62,386	72	72	0	Windraw Composting	MRF	39.6	7.2	4.32	20.88	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		39.6	4.32	7.2	20.88	Dec.,2025	7.88	Plant in operation.
46	Alipurduar	Alipurduar	20	65,232	21	21	0	Windraw Composting	MRF	11.55	2.1	1.26	6.09	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		11.55	1.26	2.1	6.09	NA	2.30	Plant in operation.
47	Jalpaiguri	Dhupguri	16	44,719	10.5	0	10.5	Windraw Composting	MRF	5.775	1.05	0.63	3.045	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		5.775	0.63	1.05	3.045	Dec, 2025	1.15	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within June, 2025. After that the tender will be floated for enagagement of agency for setting up of freh waste processing plant.
48	Jalpaiguri	Jalpaiguri	25	1,07,341	62	0	62	Windraw Composting	MRF	34.1	6.2	3.72	17.98	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		34.1	3.72	6.2	17.98	Sept,2025	6.79	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
49	Jalpaiguri	Mal	15	25,218	9	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		4.95	0.54	0.9	2.61	Sept,2025	0.99	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process .
50	Malda	English Bazar	29	2,05,521	155	0	155	Windraw Composting	MRF	85.25	15.5	9.3	44.95	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		85.25	9.3	15.5	44.95	Sept,2025	16.97	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process .
51	Malda	Old Malda	20	84,012	37	0	37	Windraw Composting	MRF	20.35	3.7	2.22	10.73	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		20.35	2.22	3.7	10.73	Dec, 2025	4.05	State Government identified the land for setting up of fresh waste processing unit. DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
52	Murshidabad	Beldanga	14	29,182	11	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		6.05	0.66	1.1	3.19	Sept,2025	1.20	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
53	Murshidabad	Berhampore	28	1,95,363	100	0	100	Windraw Composting	MRF	55	10	6	29	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		55	6	10	29	Dec, 2025	10.95	After reclaimation of land from legacy waste the tender for infrastrcure work for setting up of fresh waste processing unit will be floated.
54	Murshidabad	Dhuliyan	21	95,706	38.23	0	38.23	Windraw Composting	MRF	21.0265	3.823	2.2938	11.0867	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		21.0265	2.2938	3.823	11.0867	Dec, 2025	4.19	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
55	Murshidabad	Domkol	21	1,21,827	40	0	40	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		22	2.4	4	11.6	Dec, 2025	4.38	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
56	Murshidabad	Jangipur	21	88,165	48	25	23	Windraw Composting	MRF	26.4	4.8	2.88	13.92	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		26.4	2.88	4.8	13.92	Sept,2025	5.26	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
57	Murshidabad	Jiaganj-Azimganj	17	51,790	16.33	0	16.33	Windraw Composting	MRF	8.9815	1.633	0.9798	4.7357	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		8.9815	0.9798	1.633	4.7357	Oct, 2025	1.79	State Government identified a land for setting up of fresh waste processing unit for Jiagunj-Azimgunj Municipality, but due to local agitation further action could not be taken. Local administration are giving their best effort to reslove the matter.Expected that by Aug,2025 the matter will be resloved. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
58	Murshidabad	Kandi	18	55,632	19	0	19	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		10.45	1.14	1.9	5.51	Dec, 2025	2.08	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within July, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
59	Murshidabad	Murshidabad	16	44,064	20	12	8	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		11	1.2	2	5.8	Dec, 2025	2.19	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
60	Nadia	Birnagar	14	30,799	9.82	8	1.82	Windraw Composting	MRF	5.401	0.982	0.5892	2.8478	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		5.401	0.5892	0.982	2.8478	Sept,2025	1.08	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
61	Nadia	Chakdaha	21	95,203	37	0	37	Windraw Composting	MRF	20.35	3.7	2.22	10.73	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		20.35	2.22	3.7	10.73	Dec, 2025	4.05	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
62	Nadia	Cooper's Camp	12	18,839	8.04	0	8.04	Windraw Composting	MRF	4.422	0.804	0.4824	2.3316	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		4.422	0.4824	0.804	2.3316	Dec.,2025	0.88	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
63	Nadia	Gayeshpur	18	58,998	20	0	20	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		11	1.2	2	5.8	Sept,2025	2.19	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
64	Nadia	Haringhata	17	45,953	20	0	20	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		11	1.2	2	5.8	Dec, 2025	2.19	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within March, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
65	Nadia	Kalyani	21	1,00,620	60	16	44	Windraw Composting	MRF	33	6	3.6	17.4	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		33	3.6	6	17.4	Sept, 2025	6.57	Tender floated for enagagement of agency for setting up of fresh waste processing plant.
66	Nadia	Krishnanagar	25	1,53,062	120	120	0	Windraw Composting	MRF	66	12	7.2	34.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		66	7.2	12	34.8	NA	13.14	Achieved
67	Nadia	Nabadwip	24	1,25,528	60	16	44	Windraw Composting	MRF	33	6	3.6	17.4	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		33	3.6	6	17.4	Dec, 2025	6.57	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
68	Nadia	Ranaghat	20	75,365	25	20	5	Windraw Composting	MRF	13.75	2.5	1.5	7.25	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		13.75	1.5	2.5	7.25	Dec, 2025	2.74	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
69	Nadia	Santipur	24	1,51,777	83	0	83	Windraw Composting	MRF	45.65	8.3	4.98	24.07	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		45.65	4.98	8.3	24.07	Dec, 2025	9.09	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
70	Nadia	Taherpur NAA	13	20,894	5	4.1	0.9	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		2.75	0.3	0.5	1.45	Sept,2025	0.55	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
71	North 24 Parganas	Ashoknagar-Kalyangarh	23	1,21,592	48	35	13	Windraw Composting	MRF	26.4	4.8	2.88	13.92	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		26.4	2.88	4.8	13.92	Sept,2025	5.26	Work order issued to an agency for setting up of fresh waste processing unit at dumpsite of Ashokenagar-Kalyangarh municipality for Ashokenagar-Kalyangarh municipality & Habra municipality. After, reclaimation of land through bio-mining & bio-remediation of legacy waste, installation of infrastrucre for fresh waste processing unit will be started.
72	North 24 Parganas	Baduria	17	52,500	5.97	4	1.97	Windraw Composting	MRF	3.2835	0.597	0.3582	1.7313	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		3.2835	0.3582	0.597	1.7313	Dec,2025	0.65	Work order issued for engagement of agency for setting up fresh waste processing plant. Land development work is in progress.
73	North 24 Parganas	Baranagar	34	2,45,213	647.6	350	297.6	Windraw Composting & Bio methanation	MRF	356.18	64.76	38.856	187.804	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	100	256.18	38.856	64.76	187.804	Jan,2026	70.91	Work order issued to an agency for setting up of fresh waste processing unit at Promodnagar dumpsite for these 5 ULBs. Infrastrure Work is in progress. Gradually, the infrstrucre being extended at the reclaimed land being available after legacy waste processing. Partial processing is in progress.
74	North 24 Parganas	Dum Dum	22	1,14,786																					
75	North 24 Parganas	South DumDum	35	4,03,316																					
76	North 24 Parganas	North Dum Dum	34	2,49,545																					
77	North 24 Parganas	New Barrackpur	20	76,879																					
78	North 24 Parganas	Kamarhati	35	3,31,163	160	0	160	Windraw Composting	MRF	88	16	9.6	46.4	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		88	9.6	16	46.4	Sept,2025	17.52	Work order issued to an agency for setting up of fresh waste processing unit at Kamarhati dumpsite for the ULB.After reclaimation of land from legacy waste the infrastrcure work for setting up of fresh waste processing unit will be started.
79	North 24 Parganas	Barasat	35	2,78,435	203	0	203	Windraw Composting	MRF	111.65	20.3	12.18	58.87	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		111.65	12.18	20.3	58.87	Sept,2025	22.23	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
80	North 24 Parganas	Barrackpore	24	1,52,783	50	15	35	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		27.5	3	5	14.5	Dec,2026	5.48	Tender floated for enagagement of agency for setting up of fresh waste processing plant.
81	North 24 Parganas	Basirhat	23	1,25,058	56	53	3	Windraw Composting	MRF	30.8	5.6	3.36	16.24	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		30.8	3.36	5.6	16.24	Dec.,2025	6.13	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
82	North 24 Parganas	Bhatpara	35	3,85,867	205	0	205	Windraw Composting	MRF	112.75	20.5	12.3	59.45	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		112.75	12.3	20.5	59.45	Dec,2026	22.45	Tender to be floated for engagement of an agency for upgradation of Civil and/or Electro-Mechanical construction/installation, for processing of fresh waste at the identified land of Bhatpara Municipality. Prepartion of tender document is under process.
83	North 24 Parganas	Bidhannagar Municipal Corporation	41	6,34,107	350	0	350	Bio-CNG	MRF	192.5	35	21	101.5	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	192.5		21	35	101.5	Dec,2025	38.33	DPR prepared. Tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
84	North 24 Parganas	Bongaon	22	1,08,864	62	31	31	Windraw Composting	MRF	34.1	6.2	3.72	17.98	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		34.1	3.72	6.2	17.98	Dec, 2025	6.79	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
85	North 24 Parganas	Garulia	21	85,336	35.77	12	23.77	Windraw Composting	MRF	19.6735	3.577	2.1462	10.3733	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		19.6735	2.1462	3.577	10.3733	Dec,2026	3.92	Tender to be floated for engagement of an agency for upgradation of Civil and/or Electro-Mechanical construction/installation, for processing of fresh waste at the identified land of Bhatpara Municipality. Prepartion of tender document is under process.
86	North 24 Parganas	Gobardanga	17	45,392	18.64	8	10.64	Windraw Composting	MRF	10.252	1.864	1.1184	5.4056	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		10.252	1.1184	1.864	5.4056	Sept,2025	2.04	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
87	North 24 Parganas	Habra	24	1,47,221	70	0	70	Windraw Composting	MRF	38.5	7	4.2	20.3	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		38.5	4.2	7	20.3	Sept,2025	7.67	Work order issued to an agency for setting up of fresh waste processing unit at dumpsite of Ashokenagar-Kalyangarh municipality for Ashokenagar-Kalyangarh municipality & Habra municipality. After, reclaimation of land through bio-mining & bio-remediation of legacy waste, installation of infrastrucre for fresh waste processing unit will be started.
88	North 24 Parganas	Halisahar	23	1,24,851	52	21	31	Windraw Composting	MRF	28.6	5.2	3.12	15.08	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		28.6	3.12	5.2	15.08	Feb,2026	5.69	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within June, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
89	North 24 Parganas	Kanchrapara	24	1,29,576	53.84	12	41.84	Windraw Composting	MRF	29.612	5.384	3.2304	15.6136	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		29.612	3.2304	5.384	15.6136	Oct,2026	5.90	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation.
90	North 24 Parganas	Khardah	22	1,08,496	46.43	14	32.43	Windraw Composting	MRF	25.5365	4.643	2.7858	13.4647	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		25.5365	2.7858	4.643	13.4647	Dec.,2025	5.08	Tender to be floated for engagement of an agency for upgradation of Civil and/or Electro-Mechanical construction/installation, for processing of fresh waste at the identified land of Bhatpara Municipality. Prepartion of tender document is under process.
91	North 24 Parganas	Madhyamgram	28	1,96,127	90	16	74	Windraw Composting	MRF	49.5	9	5.4	26.1	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		49.5	5.4	9	26.1	Dec,2026	9.86	Tender floated for engagement of agency for setting up of fresh waste processing plant.
92	North 24 Parganas	Naihati	31	2,18,194	107	20	87	Windraw Composting	MRF	58.85	10.7	6.42	31.03	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		58.85	6.42	10.7	31.03	Dec, 2025	11.72	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
93	North 24 Parganas	North Barrackpore	23	1,32,806	73	0	73	Windraw Composting	MRF	40.15	7.3	4.38	21.17	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		40.15	4.38	7.3	21.17	Dec,2025	7.99	As per decision, wastes of North Barrackpore Municipality shall be processed at the dump land of Titagarh Muinicipality on Cluster Mode.
94	North 24 Parganas	Panihati	35	3,77,351	176	0	176	Windraw Composting	MRF	96.8	17.6	10.56	51.04	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		96.8	10.56	17.6	51.04	Dec,2026	19.27	Tender to be floated for engagement of an agency for setting up of fresh waste processing plants, on the reclaimed land at Ramchandrapur and at the identified land at Mahishpota Mouza. Prepartion of tender document under process.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
95	North 24 Parganas	Taki	16	38,263	14	8.4	5.6	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		7.7	0.84	1.4	4.06	Dec,2025	1.53	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
96	North 24 Parganas	Titagarh	23	1,16,541	47.7	9	38.7	Windraw Composting	MRF	26.235	4.77	2.862	13.833	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		26.235	2.862	4.77	13.833	Sept,2026	5.22	Tender floated for engagement of agency for setting up of fresh waste processing unit, on integrated module, where the selected agency shall process both the legacy waste and fresh waste simultaneously. After reclamation of land of the dumpyard through biomining of the existing legacy waste, they shall set up their processing units over the land reclaimed. 2nd call of the tender not matured. 3rd call shall be invited shortly.
97	Paschim Midnapore	Chandrakona	12	23,629	8.42	0	8.42	Windraw Composting	MRF	4.631	0.842	0.5052	2.4418	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		4.631	0.5052	0.842	2.4418	Sept,2025	0.92	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
98	Paschim Midnapore	Ghatal	17	54,591	26.7	0	26.7	Windraw Composting	MRF	14.685	2.67	1.602	7.743	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		14.685	1.602	2.67	7.743	Dec, 2025	2.92	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Aug, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
99	Jhargram	Jhargram	18	61,682	28.5	0	28.5	Windraw Composting	MRF	15.675	2.85	1.71	8.265	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		15.675	1.71	2.85	8.265	Dec, 2025	3.12	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
100	Paschim Midnapore	Kharagpur	35	2,07,604	82	25	57	Windraw Composting	MRF	45.1	8.2	4.92	23.78	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		45.1	4.92	8.2	23.78	Sept,2025	8.98	Work order issued to an agency for setting up of fresh waste processing unit. Infrsatructre Work started but stopped due to local agitation. Effort given to reslove the matter and start the work at the earliest.
101	Paschim Midnapore	Kharar	10	12,220	5.4	0	5.4	Windraw Composting	MRF	2.97	0.54	0.324	1.566	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		2.97	0.324	0.54	1.566	Dec,2025	0.59	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
102	Paschim Midnapore	Khirpai	10	16,385	6.76	0	6.76	Windraw Composting	MRF	3.718	0.676	0.4056	1.9604	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		3.718	0.4056	0.676	1.9604	Dec,2025	0.74	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
103	Paschim Midnapore	Midnapore	25	1,69,127	92	0	92	Windraw Composting	MRF	50.6	9.2	5.52	26.68	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		50.6	5.52	9.2	26.68	Jan,2026	10.07	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency.
104	Paschim Midnapore	Ramjibonpur	11	19,611	7	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		3.85	0.42	0.7	2.03	Sept,2025	0.77	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
105	Purba Midnapore	Contai	21	92,226	60	0	60	Windraw Composting	MRF	33	6	3.6	17.4	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		33	3.6	6	17.4	Dec, 2025	6.57	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
106	Purba Midnapore	Egra	14	30,148	14.6	0	14.6	Windraw Composting	MRF	8.03	1.46	0.876	4.234	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		8.03	0.876	1.46	4.234	Dec, 2025	1.60	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared. Tender floated for engagement of agency for setting up of fresh waste processing plant.
107	Purba Midnapore	Haldia	29	2,00,827	80	80	0	Windraw Composting	MRF	44	8	4.8	23.2	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		44	4.8	8	23.2	NA	8.76	Achieved

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
108	Purba Midnapore	Panskura	15	57,932	18	8	10	Windraw Composting	MRF	9.9	1.8	1.08	5.22	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		9.9	1.08	1.8	5.22	Dec, 2025	1.97	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Aug, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
109	Purba Midnapore	Tamluk	20	65,312	24.6	12	12.6	Windraw Composting	MRF	13.53	2.46	1.476	7.134	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		13.53	1.476	2.46	7.134	Dec, 2025	2.69	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Aug, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
110	Jhalda	Jhalda	12	19,540	6.48	0	6.48	Windraw Composting	MRF	3.564	0.648	0.3888	1.8792	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		3.564	0.3888	0.648	1.8792	Dec, 2025	0.71	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within March, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
111	Purulia	Purulia	23	1,21,067	20	0	20	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		11	1.2	2	5.8	Dec, 2025	2.19	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Sept, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
112	Purulia	Raghunathpur	13	25,621	11	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		6.05	0.66	1.1	3.19	Dec, 2025	1.20	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
113	South 24 parganas	Baruipur	17	53,128	24.5	6	18.5	Windraw Composting	MRF	13.475	2.45	1.47	7.105	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		13.475	1.47	2.45	7.105	Dec,2026	2.68	After reclaimation of land from legacy waste the tender for infrastrcure work for setting up of fresh waste processing unit will be floated.
114	South 24 parganas	Budge Budge	20	76,858	30	25	5	Windraw Composting	MRF	16.5	3	1.8	8.7	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		16.5	1.8	3	8.7	Dec, 2025	3.29	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant prepared & tender floated for enagagement of agency .
115	South 24 parganas	Diamond Harbour	16	43,169	19.53	4	15.53	Windraw Composting	MRF	10.7415	1.953	1.1718	5.6637	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		10.7415	1.1718	1.953	5.6637	Dec,2025	2.14	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
116	South 24 parganas	Jaynagar Majilpur	14	25,922	9	6	3	Windraw Composting & Bio Gas	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	1	3.95	0.54	0.9	2.61	Sept,2025	0.99	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
117	South 24 parganas	Maheshtala	35	4,49,423	210	14	196	Vermi Compost	MRF	115.5	21	12.6	60.9	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		115.5	12.6	21	60.9	Dec,2026	23.00	Tender floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
118	South 24 parganas	Pujali	16	37,040	12.63	0	12.63	Windraw Composting	MRF	6.9465	1.263	0.7578	3.6627	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		6.9465	0.7578	1.263	3.6627	Dec,2025	1.38	Tender floated for engagement of agency for setting up of fresh waste processing plant.
119	South 24 parganas	Rajpur-Sonarpur	35	4,23,724	348.52	5	343.52	Windraw Composting & Bio Gas	MRF	191.686	34.852	20.911	101.071	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	25	166.686	20.9112	34.852	101.0708	Dec,2025	38.16	Tender shall be floated by the ULB itself, for engagement of agency for setting up fresh waste processing unit. Tender document prepared.
120	Uttar Dinajpur	Dalkhola	16	37,063	17.29	4	13.29	Windraw Composting	MRF	9.5095	1.729	1.0374	5.0141	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		9.5095	1.0374	1.729	5.0141	Dec,2025	1.89	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal upto May, 2025

Sl. No.	(i) Name of District	ULB	No. of ward	Population (Census 2011)	(ii) Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of wet Waste processing Unit	Type of dry Waste processing Unit	(iv) Method of treatment in TPD				(v) Final destination each of the componentsof (iv)				(vi) Break up details of waste processing					(vii) Action plan to process 100% of waste		
										Organic material (Wet Waste)	Inerts	RDF	Others	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	Others uses of inerts	Time line for starting of processing of remaining waste	Budget outlay (Rs. In Cr)	Proposal
121	Uttar Dinajpur	Islampur	17	54,340	21.73	12	9.73	Windraw Composting	MRF	11.9515	2.173	1.3038	6.3017	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		11.9515	1.3038	2.173	6.3017	Dec.,2025	2.38	DPR (Drawing,Design & Estimate) for Fresh Waste Processing Plant is under preparation & simultaneously prepartion of tender document for enagagement of agency is under process.
122	Uttar Dinajpur	Kaliyaganj	17	53,530	39		39	Windraw Composting	MRF	21.45	3.9	2.34	11.31	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		21.45	2.34	3.9	11.31	Dec,2025	4.27	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
123	Uttar Dinajpur	Raiganj	27	1,83,612	95	16	79	Windraw Composting	MRF	52.25	9.5	5.7	27.55	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		52.25	5.7	9.5	27.55	Dec,2025	10.40	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
124	Howrah	Howrah MC	50	10,70,645	710	10	700	Windraw Composting	MRF	390.5	71	42.6	205.9	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		390.5	42.6	71	205.9	Dec,2026	77.75	After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
125	Howrah	Bally	35	2,91,916	139.93	16	123.93	Windraw Composting	MRF	76.9615	13.993	8.3958	40.5797	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		76.9615	8.3958	13.993	40.5797	Dec,2026	15.32	After reclaimation of land through legacy waste processing, tender to be floated for engagement of agency for setting up of fresh waste processing plant. Prepartion of tender document under process.
126	Jalpaiguri	Maynaguri	17	36,263	12.7	0	12.7	Windraw Composting	MRF	6.985	1.27	0.762	3.683	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		6.985	0.762	1.27	3.683	Nov,2025	1.39	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
127	Alipurduar	Falakata	18	54,039	22	0	22	Windraw Composting	MRF	12.1	2.2	1.32	6.38	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants		12.1	1.32	2.2	6.38	Nov,2025	2.41	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
128	Kolkata	Kolkata MC	144	4496694	4500	609	3891	Windrow Compost & Bio-CNG	Material Recovery Facility & Plastic Processing Unit	2475	450	270	1305	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	350	2125	270	450	1305	Dec, 2026	600.00	Bio-CNG and windraw compost plant to be set up for remaining wet waste and for remaining dry waste MRF to be set up.
	Total =		**2994**	**21433481**	**13216.07**	**2486.5**	**10730**			**7268.839**	**1321.6**	**792.96**	**3832.66**					**749.042**	**6519.797**	**792.9642**	**1321.607**	**3832.66**	**Total =**	**1554.41**	

Status of Bio-mining & Bio-remediation of Legacy Waste of 128 ULBs of West Bengal up to September, 2025

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Composition of the Waste				Process adopted to remidiate at each site	Final Destination of the Components at				Earmarked Budget (Rs. In Crore)	Action plan to remidiate and recover the sites				Remarks
																		Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)		Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)		P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	
1	ALIPURDUAR	Alipurduar	1	Beside Radhamadhab Mandir	26°29'33"N 89°32'29"E	0.33	4274	4274	Completed	0.33	0	0	4274	0	4274	Completed	0.33	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.24	NA	NA	NA	NA	Total area recliamed
2	BANKURA	Bankura	1	Keshra Trenching Ground	23.267285° N 87.035388°E	16.53	172937.6	172938	Completed	6.50	187000	0	359937.6	187000	172938	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	19.80	Yes	Yes	Yes	Yes	
3	BANKURA	Sonamukhi	1	Adrab Bazar	23.300813° N 87.398289°E	1.50	2400	2400	Completed	1.50	0	0	2400	0	2400	Completed	1.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.13	NA	NA	NA	NA	Total area recliamed
4	BIRBHUM	Bolpur	1	Bolpur, Khoskadambatur, P. S. Bolpur, JL No. 95, Plot No. 2590, 2703	23.677955° N, 87.721413°E	3.33	60814	60814	Completed	1.20	108870	0	169684	108870	60814	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.33	Yes	Yes	Yes	Yes	
5	BIRBHUM	Dubrajpur	1	Mahaprabhu Gate	23.78196°N 87.36859°E	1.20	6122	6122	Completed	0.75	1,05,914	0	112036	105914	6122	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.16	Yes	No	No	No	
6	BIRBHUM	Rampurhat	1	Bonat & Kusumba Road	24.18826°N 87.75746°E	3.85	24212	24212	Completed	0.85	49280	0	73492	49280	24212	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.04	Yes	Yes	Yes	Yes	
7	BIRBHUM	Sainthia	1	Ward No. 14	23.5657°N 87.4039°E	1.10	7261	7261	Completed	0.40	80,805	0	88066	80805	7261	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.84	Yes	No	No	No	
8	BIRBHUM	Suri	1	Dhanyogram (JL No. - 206)	23.95225°N 87.48576°E	2.00	16428	16428	Completed	0.60	48870	0	65298	48870	16428	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.59	Yes	Yes	Yes	Yes	
9	BIRBHUM	Nalhati	1	Khanpur	24.30658°N 87.825631°E	5.00	56000	56000	Completed	5	36800	0	92800	36800	56000	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.10	Yes	No	No	No	
10	COOCH BEHAR	Cooch Behar	1	Guriahati-II	26.299124° N 89.468282°E	6.75	67319.21	67319	Completed	2.20	177600	0	244919.21	177600	67319	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	13.47	Yes	No	No	No	
11	COOCH BEHAR	Dinhata	1	Buri dharia	26.821°N 89.2652°E	3.20	12432	12432	Completed	1.20	30220	0	42652	30220	12432	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.35	Yes	No	No	No	
12	COOCH BEHAR	Haldibari	1	DBDH	26°19'27.4" N 88°47'6.5"E	0.73	6491.17	6491	Completed	0.20	41400	0	47891.17	41400	6491	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.63	Yes	No	No	No	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
13	COOCH BEHAR	Mathabhanga	2	Ward No. - 4 (behind Jangli Kalibari and Manasi River) & Ward No. - 2, KhadanGhat (Beside Manasi and Sutunga River)	26.2041°N 89.137°E & 26.2017°N 89.1316°E	2.20	8830.16	8830	Completed	1.00	14800	0	23630.16	14800	8830	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.30	Yes	No	No	No	
14	COOCH BEHAR	Tufanganj	1	Kamat Phoolbari	26.1846°N 89.4014°E	2.70	8918.15	8918	Completed	1.00	19640	0	28558.15	19640	8918	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.57	Yes	No	No	No	
15	DAKSHIN DINAJPUR	Balurghat	1	5 no. Bhatpara, Dangi Under Bhatpara Gram panchayat	25.2052169° N 88.76702841 °E	9.99	72514.595	72515	Completed	3.00	15453	0	87967.595	15453	72515	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.84	Yes	Yes	Yes	Yes	
16	DAKSHIN DINAJPUR	Gangarampore	1	Naroi Dump-pit, 6 no. Anchol, Gangarappur	25.402148° N 88.532081°E	2.25	4275	4275	Completed	1.10	29100	0	33375	29100	4275	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.84	Yes	Yes	Yes	Yes	
17	DARJEELING	Siliguri MC	1	Don Bosco colony	26.746839° N 88.452293°E	26.00	379382	379382	Completed	10.50	1150000	0	1529382	1150000	379382	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	84.12	Yes	Yes	Yes	Yes	
18	HOOGHLY	Chandannagore MC	1	Kalupukur Vermi-Compost Plant, Kolupukur Bhagar more, Ward No. 8	22°52'13"N, 88°21'32"E	4.94	215916	215916	Completed	1.00	106252	0	322168	106252	215916	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	17.72	Yes	Yes	Yes	Yes	
19	HOOGHLY	Hooghly Chinsurah	1	Kedia – I GP, Sukantanagar Rabindranagar	22°53'35"N 88°22'44"E	6.50	126266	126266	Completed	2.50	102159	0	228425	102159	126266	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	12.56	Yes	Yes	Yes	Yes	
20	HOOGHLY	Baidyabati	1	RWMC	22.7888N, 88.31202E	52.00	220794	130254	Dec-25	5.00	0	0	220794	90540	130254	46082	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	12.14	No	No	No	No	
21	HOOGHLY	Champdany																														
22	HOOGHLY	Rishra																														
23	HOOGHLY	Serampore																														
24	HOOGHLY	Uttarpara-Kotrung																														
25	HOOGHLY	Konnagar																														
26	HOOGHLY	Bhadreswar	1	Sanjay colony, N S Road,	22.834139°N, 88.349718°E	0.42	320000	0	Jun-26	0	337000	0	657000	657000	0	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	36.14	Yes	No	No	No	
27	HOOGHLY	Dankuni	1	Beside Parbatipur Road, Ramanathpur (Panchayet Area)	22°40'31".N , 88°13'58".E	2.40	48078	48078	Completed	5	0	0	48078	0	48078	0	5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.64	NA	NA	NA	NA	Total area recliamed
28	HOOGHLY	Bansberia	2	Ward no. 8 & 18	22° 57'45.1" N 88° 23'45.3" E	2.79	47000	0	Sep-25	0	108000	0	155000	155000	0	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.53	Yes	No	No	No	
29	HOOGHLY	Arambagh	1	Kalipur (Ward No 6)	22.88525N, 87.77549E	1.20	37750	0	Sep-25	0	37750	0	75500	75500	0	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.15	Yes	Yes	Yes	Yes	
30	HOOGHLY	Tarakeswar	1	Kadamtala, Ward No. 13	22.88326N, 88.02701E	0.44	16610	0	Sep-25	0	16610	0	33220	33220	0	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.83	Yes	Yes	Yes	Yes	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
31	HOWRAH	Uluberia	2	Banitala, Ward No. 31 (Beside NH 6) & Ward No. 6, Bauria	22.478330° N 88.078462°E & 22.499437° N 88.169112°E	6.50	28394	28394	Completed	3.00	105000	0	133394	105000	28394	Sep-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.34	Yes	Yes	Yes	Yes	
32	HOWRAH	Bally	1	Chandmari	22.635658° N 88.334197°E	3.00	120000	30132.59	Dec-25	0.50	0	0	120000	89867	30133	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.60	Yes	Yes	Yes	Yes	After completion of 1st Phase, Phase-2 processing will be started after assessment of quantity
33	HOWRAH	Howrah MC	1	Belgachia	22°36'35"N 88°19'34"E	21.99	9,61,567	364026.87	Oct-26	1.80	750000	0	1711567	1347540	364027	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	94.14	Yes	Yes	Yes	Yes	
34	JALPAIGURI	Jalpaiguri	1	Paharpur	26.564305° N 88.736121°E	2.50	25891.6	25892	Completed	2.50	160000	0	185891.6	160000	25892	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	10.22	Yes	No	No	No	
35	JHARGRAM	Jhargram	1	Jhargram (Near Jaralat)	22°26'36"N 86°58'29"E	12.00	3739	3739	Completed	12.00	10000	0	13739	10000	3739	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.76	No	NA	NA	NA	
36	KOLKATA	Kolkata MC	2	Garden Reach	Lat 22.530578° N Long 88.291576° E	19.77	1500000	10000	Mar-26	0.80	0	0	1500000	1490000	10000	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	82.50	Yes	No	No	No	
				DHAPA Under W-58 OF BR-VII/KMC	22°32'32.6" N 88°25'17.6"E	60.00	4000000	1813000	Mar-26	25.00	2000000	0	6000000	4187000	1813000	Mar-27	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	330.00	Yes	No	No	No	
37	MALDA	English Bazar	1	English Bazar (muza Bahadurpur)	24°54'59.18" N 88°6'57.87"E	3.52	3250	3250	Completed	0.52	240000	0	243250	240000	3250	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	13.38	Yes	No	No	No	
38	MURSHIDABAD	Berhampore	1	Banappare ring road	Komolapur Khadamkhandi	2.16	123981	123981	Completed	1.00	230000	0	353981	230000	123981	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	19.47	Yes	Yes	Yes	Yes	
39	MURSHIDABAD	Jangipur	1	Azgarpara near Milanpur	24°28'43.79" N 88°3'10.75"E	0.28	3211	3211	Completed	0.10	65180	0	68391	65180	3211	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.76	Yes	No	No	No	
40	MURSHIDABAD	Jiaganj-Azimganj	1	Ghoramari (Azimganj Side)	24°14'14.8" N 88°15'56.8" E	3.00	19426	19426	Completed	1.00	53000	0	72426	53000	19426	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.98	Yes	No	No	No	
41	MURSHIDABAD	Murshidabad	1	Kathgola bagan, Ward No. - 15	Kathgola bagan, Ward No. 15	5.38	94059	94059	Completed	1.00	62500	0	156559	62500	94059	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.61	Yes	No	No	No	
42	MURSHIDABAD	Dhulian	1	Dhuliyan (near Malancha, Ratanpur)	24°39'29.89" N 87°55'50.74" E	2.00	0	0	0	0	60000	0	60000	60000	0	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.30	Yes	NA	NA	NA	
43	MURSHIDABAD	Kandi	1	Kandi (Jafadanga, Ward No. 12)	23°56'51.56" N 88°4'3.47"E	5.82	0	0	0	0	5000	0	5000	5000	0	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.28	Yes	NA	NA	NA	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
44	NADIA	Birnagar	1	Mathurapukur	23.268035° N 88.55683°E	3.00	6799	6799	Completed	3.00	0	0	6799	0	6799	Completed	3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.37	NA	NA	NA	NA	Total area recliamed
45	NADIA	Gayeshpur	2	1) Near VS Club, Ward No.-16 & Near SHG Training Centre, Ward No.- 15	22.955519° N 88.472313°E & 22.953232° N 88.48228°E	5.00	12465	12465	Completed	1.20	34400	0	46865	34400	12465	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.58	Yes	No	No	No	
46	NADIA	Kalyani	2	Near Kacharipara, Ward No.-6 & Beside highway, Ward No.-10	22.960863° N, 88.439684°E & 22.960863° N 88.439684°E	2.1 & 1.4	60543	60543	Completed	1.20	115000	0	175543	115000	60543	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.65	Yes	Yes	Yes	Yes	
47	NADIA	Krishnanagar	1	Godadanga, Ward – 5	(23.4052240 °N 88.5116291° E	8.00	51802	51802	Completed	3.00	412000	0	463802	412000	51802	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	25.51	Yes	No	No	No	
48	NADIA	Nabadwip	1	Near Bishnupriya Halt Station, Ward No. – 1	23.4150386° N 88.3562766° E	12.35	83900	83900	Completed	5.00	111870	0	195770	111870	83900	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	10.77	Yes	Yes	Yes	Yes	
49	NADIA	Ranaghat	1	Anulia GP	23.268035° N 88.55683°E	6.31	65374	65374	Completed	3.30	99750	0	165124	99750	65374	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.08	Yes	No	No	No	
50	NADIA	Santipur	1	Moylar math, Ward no. – 10	23.25010210° N 88.4116394° E	4.55	22097	22097	Completed	2.20	86840	0	108937	86840	22097	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.99	Yes	Yes	Yes	Yes	
51	NADIA	Taherpur	1	Cremation Ground Road, Ward No.-1	23.270603° N 88.521961°E	1.26	6119	6119	Completed	0.50	14140	0	20259	14140	6119	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.11	Yes	No	No	No	
52	NADIA	Chakdah	1	Ward No - 19	23.062613N, 88.517296E	5.00	19426	19426	Completed	5.00	0	0	19426	0	19426	Completed	5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.07	NA	NA	NA	NA	Total area recliamed
53	NADIA	Cooper's Camp	1	Ward 2- near burning ghat	23.270603N, 88.521961E	0.50	19620	0	Dec-25	0	22860	0	42480	42480	0	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.34	Yes	No	No	No	
54	NORTH 24-PARGANAS	Barasat	1	Kadambagachi	22.70483°N 88.51908°E	3.50	67846.935	67847	Completed	3.50	0	0	67847	0	67847	Completed	3.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.73	NA	NA	NA	NA	Total area recliamed
55	NORTH 24-PARGANAS	Barrackpore	1	Kolkata Road	22.748542° N 88.382122°E	5.00	72846	72846	Completed	3.00	57812	0	130658	57812	72846	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.19	Yes	Yes	No	No	
56	NORTH 24-PARGANAS	Basirhat	1	Ward 8	22.65254°N 88.87294°E	4.00	24273.065	24273	Completed	4.00	0	0	24273	0	24273	Completed	4	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.34	NA	NA	NA	NA	Total area recliamed

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
57	NORTH 24-PARGANAS	Bongaon	1	Beside Indira Park, Ward No. – 19 (opposite Truck Parking lot)	23°1'44.13" N 88°50'31.40" E	2.26	7013	7013	Completed	1.20	84832	0	91845	84832	7013	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.05	Yes	No	No	No	
58	NORTH 24-PARGANAS	Habra	1	Near Banipur Home, Ward No.-3	22.818064° N 88.635827°E	1.20	9458.1	9458	Completed	0.98	91700	0	101158.1	91700	9458	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.56	Yes	No	No	No	
59	NORTH 24-PARGANAS	Kanchrapara	1	Bidhanpally	23.4150386° N 88.3562766° E	3.00	24282	24282	Completed	1.20	136000	0	160282	136000	24282	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.82	Yes	No	No	No	
60	NORTH 24-PARGANAS	Khardah	1	Ruiyaiswaripur	22°44'31"N 88°24'25"E	2.75	46118	46118	Completed	1.00	38140	0	84258	38140	46118	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.63	Yes	Yes	No	No	
61	NORTH 24-PARGANAS	Madhyamgram	1	Digberia	22.69264° 88.50134°E	7.17	116068	116068	Completed	1.19	87700	0	203768	87700	116068	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	11.21	Yes	Yes	No	No	
62	NORTH 24-PARGANAS	Panihati	1	Ramchandra Pur	22°41'31"N 88°23'10"E	1.50	51763.391	51763	Completed	0.20	120000	0	171763.391	120000	51763	May-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.45	Yes	Yes	Yes	Yes	
63	NORTH 24-PARGANAS	Taki	1	Mansing road	22.57787°N 88.93308°E	0.80	3625	3625	Completed	0.35	13400	0	17025	13400	3625	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.94	Yes	No	No	No	
64	NORTH 24-PARGANAS	Titagarh	1	Mathpara	22.88326°N 88.02701°E	4.90	120886	120886	Completed	1.00	44716	0	165602	44716	120886	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.11	Yes	No	No	No	
65	NORTH 24-PARGANAS	Bhatpara	2	Madral & Jilabi Math	22.87426°N 88.41807°E & 22.85932°N 88.39001°E	2.57	58260	58260	Completed	1.00	71905	0	130165	71905	58260	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.16	Yes	No	No	No	
66	NORTH 24-PARGANAS	Garulia	1	Fanching Ground Road	22.817161° N 88.372613°E	1.80	52499	51991.017	Completed	1.00	38218	0	90717	38726	51991	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.99	Yes	Yes	No	No	
67	NORTH 24-PARGANAS	Halisahar	1	Niraljan Trenching Ground	23.2501021° N 88.4116394° E	0.84	6799	6789	Completed	0.25	43905	0	50704	43915	6789	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.79	Yes	Yes	Yes	No	
68	NORTH 24-PARGANAS	Bidhannagar MC	1	Mollar Bheri	22.35'52" N 88.26'47" E	55.00	300000	300000	Completed	55.00	0	0	300000	0	300000	Completed	55	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	16.50	NA	NA	NA	NA	Total area recliamed
69	NORTH 24-PARGANAS	Baranagar	1	Pramodnagar, Beside Belghoria Expressway	22.648657N, 88.397365E	22.68	845400	845400	Completed	2.00	1100000	0	1945400	1100000	845400	46722	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	107.00	Yes	Yes	Yes	Yes	
70	NORTH 24-PARGANAS	Dum Dum																														
71	NORTH 24-PARGANAS	New Barrackpore																														
72	NORTH 24-PARGANAS	North Dum Dum																														

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
73	NORTH 24-PARGANAS	South Dum Dum																														
74	NORTH 24-PARGANAS	Kamarhati	1	Matagiri Hama Pally, Kamarhati	22.679309N, 88.379746E	8.00	50000	50000	Completed	0.50	900000	0	950000	900000	50000	Dec-27	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	52.25	**Yes**	**Yes**	**Yes**	**Yes**	
75	NORTH 24-PARGANAS	Naihati	3	Along Patterson road, Chighat, W.No. 14, Naihati	22.897030N, 88.410584E	23.94	300000	300000	Completed	15.00	144000	0	444000	144000	300000	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	24.42	**Yes**	**Yes**	**Yes**	**Yes**	
76	NORTH 24-PARGANAS	Ashoknagar-Kalyangarh	1	Ward 22 beside Naihati-Habra Road	22.50'21" N, 88.35'44 E	21.49	81585	41275	Dec-25	9.13	0	0	81585	40310	41275	0	9.13	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.49	**NA**	**NA**	**NA**	**NA**	
77	NORTH 24-PARGANAS	Gobardanga	1	Ward 3- near Belluni bridge	22.52'49" N, 88.44'37 E"	4.00	19296	19296	Completed	3.50	0	0	19296	0	19296	Completed	3.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.06	**NA**	**NA**	**NA**	**NA**	Total area recliamed
78	PaSCHIM BARDHAMAN	Asansol MC	5	a.Asansol-Kalipahari, b.Burnpur-Hirapur, c.Raniganj- Ronai, d.Jamuria- 6 No. Bypass, e.Kulti- Aldi	a.23.614345°N;87.133207°E, b.23.661219°N; 86.939790°E, c.23.614345°N;87.133207°E, d.23.707714°N;87.074470°E, e.23.703844°N;86.883500°E	36.95	1100000	496284	Mar-26	11.00	700000	0	1800000	1303716	496284	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	99.00	**Yes**	**No**	**No**	**No**	After completion of 1st Phase, Phase-2 processing will be started
79	PaSCHIM BARDHAMAN	Durgapur MC	1	Sankarpur	23.530679° N 87.356380°E	6.60	300000	300000	Completed	3.00	730000	0	1030000	730000	300000	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	56.65	**Yes**	**Yes**	**Yes**	**Yes**	
80	PASCHIM MEDINIPUR	Ghatal	1	Argora Shyampur	22.6636275° N 87.7241965° E	1.25	16038.41	16038	Completed	0.50	41520	0	57558.41	41520	16038	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.17	**Yes**	**No**	**No**	**No**	
81	PASCHIM MEDINIPUR	Kharagpur	1	Hiradih, Ward No. - 32	22.321856° 87.280617°E	1.50	29995.51	29996	Completed	1.50	50000	0	79995.51	50000	29996	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.40	**No**	**NA**	**NA**	**NA**	
82	PASCHIM MEDINIPUR	Khirpai	1	Bhutdanga	22.706906° N 87.615709°E	2.00	693.34	693	Completed	1.00	9480	0	10173.34	9480	693	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.56	**Yes**	**No**	**No**	**No**	
83	PASCHIM MEDINIPUR	Midnapore	1	Dharma Dumping Ground, Hosnabad Mouuza	22.421732° N 87.340956°E	4.00	168814.31	168814	Completed	1.50	264000	0	432814.31	264000	168814	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	23.80	**Yes**	**Yes**	**Yes**	**Yes**	
84	PASCHIM MEDINIPUR	Chandrakona	1	Ransagar, Ward No - 02	22.7191N, 88.3800E	2.00	40902	40902	Completed	1.20	21720	0	62622	21720	40902	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.44	**Yes**	**No**	**No**	**No**	
85	PASCHIM MEDINIPUR	Kharar	2	Kharar ByPass Road	30.750526N, 76.640536E & 30.750528N, 76.640539E	0.57	2044	2044	Completed	0.30	0	0	2044	0	2044	Completed	0.3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.11	**NA**	**NA**	**NA**	**NA**	Total area recliamed

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
86	PASCHIM MEDINIPUR	Ramjibanpur	1	Bypass Road	22.824006N, 87.62073E	0.20	4611	4611	Completed	0.10	0	0	4611	0	4611	Completed	0.1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.25	NA	NA	NA	NA	Total area recliamed
87	PURBA BARDHAMAN	Barddhaman	1	Kapilbagan	25°14'16.5" N 87°51'7.3"E	6.85	180825	180825	Completed	1.20	390000	0	570825	390000	180825	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	31.40	Yes	Yes	Yes	Yes	
88	PURBA BARDHAMAN	Gushkara	1	Ratani Kalitala	23.498347° N, 87.744647°E	2.00	7285	7285	Completed	0.50	54235	0	61520	54235	7285	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.38	Yes	No	No	No	
89	PURBA BARDHAMAN	Kalna	1	Beside Kalna Rail Station, kalayanpur Gram Payanchat Ambika Kalna	23.213381° N 88.353344°E	3.33	36850	36850	Completed	0.50	71900	0	108750	71900	36850	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.98	Yes	No	No	No	
90	PURBA BARDHAMAN	Katwa	1	Stadium Para, W-12	22.71923N, 88.38046E	2	3885	3885	Completed	1.00	67720	0	71605	67720	3885	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.94	Yes	No	No	No	
91	PURBA BARDHAMAN	Memari	1	Lock gate, Nudipur Bridge Memari Burdwan	Lock gate, Nudipur Bridge	2.50	38851	38851	Completed	1.25	28425	0	67276	28425	38851	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.70	Yes	No	No	No	
92	PURBA MIDNAPORE	Egra	1	Ramkrishnapur	22°23'58.04" N 87°45'19.13" E	0.32	2122.51	2123	Completed	0.12	41160	0	43282.51	41160	2123	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.38	Yes	No	No	No	
93	PURBA MIDNAPORE	Panskura	1	Panskura Railway Station	22°23'58.04" N 87°45'19.13" E	2.28	667.3	667	Completed	1.20	23840	0	24507.3	23840	667	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.35	Yes	Yes	Yes	Yes	
94	PURBA MIDNAPORE	Tamralipta	1	Malia Bari	22°16'6"N 87°55'48"E	0.49	23890.48	23890	Completed	0.20	28720	0	52610.48	28720	23890	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.89	Yes	Yes	Yes	Yes	
95	PURBA MIDNAPORE	Contai	1	Contai Digha Road	21.765423N, 87.730407E	4.59	62385	62385	Completed	2.00	98000	0	160385	98000	62385	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.82	Yes	No	No	No	
96	PURULIA	Purulia	3	a.Chharra, b.Banga Bari Samsan, c.Hutmura	a.23.3753°N 86.42805°E, b.23.34977° N 86.38601°E, c.23.3495°N 86.4992°E	10.83	77325	77325	Completed	4.00	119800	0	197125	119800	77325	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	10.84	Yes	No	No	No	
97	PURULIA	Raghunathpur	3	a.W–2 (Between Lohar & Mondal Petrol Pump), b.W-7 (beside Gara Kiari Mandir), c.W -11 (Stadium More)	a.23.53709° N 86.6746°E, b.23.52927° N 86.6763°E, c.23.52928° N 86.6763°E	1.00	8201	8201	Completed	0.50	27960	0	36161	27960	8201	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.99	Yes	No	No	No	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
98	PURULIA	Jhalda	3	a.Beside Panagarh-Moregram SH. bPat Jhalda Road Railway Cabin Side, c.Ward 5	a.23.361579 °N 85.971785°E , b.23.37796N , 85.98471E, c.23.34956N , 85.97531E	2.00	16318.43	16318	Completed	0.50	0	0	16318	0	16318	Completed	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.90	NA	NA	NA	NA	Total area recliamed
99	SOUTH 24-PARGANAS	Baruipur	1	Kritankhola	22°20'14"N 88°26'49"E	2.30	19685	19685	Completed	1.20	113000	0	132685	113000	19685	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.30	Yes	No	No	No	
100	SOUTH 24-PARGANAS	Budge Budge	1	Subhas Udyan trenching ground Ward No. - 17	22.47335°N 88.18879°E	3.48	20721	20721	Completed	2.20	41100	0	61821	41100	20721	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.40	Yes	No	No	No	
101	SOUTH 24-PARGANAS	Diamond Harbour	1	Doloanghata, Beside NH 117 (Panchayet Area)	22°10'17"N 88°13'44"E	2.00	9421.092	9421	Completed	0.50	34710	0	44131.092	34710	9421	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.43	Yes	No	No	No	
102	SOUTH 24-PARGANAS	Jaynagar-Mazilpur	1	Shahajadpur	22°10'85"N 88°26'2"E	4.00	1379	1379	Completed	1.00	21140	0	22519	21140	1379	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.24	Yes	No	No	No	
103	SOUTH 24-PARGANAS	Maheshtala	1	Sarengabad, Ward No. – 35	22.49216°N 88.20567°E	19.61	230517	230517	Completed	4.00	104000	0	334517	104000	230517	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	18.40	Yes	Yes	Yes	Yes	
104	SOUTH 24-PARGANAS	Rajpur-Sonarpur	1	Mailapota	22°25'16"N 88°25'37"E	10.00	18511.329	18511	Completed	2.00	4223	0	22734.329	4223	18511	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.25	Yes	No	No	No	
105	UTTAR DINAJPUR	Dalkhola	1	Uttar Dalkhola	25°53'6.6"N 87°50'26.1"E	0.68	7375	7375	Completed	0.68	28550	0	35925	28550	7375	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.98	Yes	No	No	No	
106	UTTAR DINAJPUR	Islampur	1	Sonakhoda Gurujbasti Trenching Ground; Ward No. – 9	26°15'32.5" N 88°12'13.1" E	0.17	1469	1469	Completed	0.10	24570	0	26039	24570	1469	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.43	Yes	No	No	No	
107	UTTAR DINAJPUR	Kaliaganj	1	Mahadebpur, Ward No. - 17)	25°38'25.6" N 88°18'26.6"E	2.84	28144	28144	Completed	1.00	33930	0	62074	33930	28144	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.41	Yes	No	No	No	
108	UTTAR DINAJPUR	Raiganj	1	Bandar Sashan, Ward No. – 22	25°36'31"N 88°7'0.9"E	3.00	38429.02	38429	Completed	1.00	141665	0	180094.02	141665	38429	Aug-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.91	Yes	No	No	No	
109	DARJEELING	Darjeeling	1	Darjeeling (Near Gorkha Road and Victoria Road)	27° 2'26.60"N 88°15'33.05" E	3.33	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	NA	NA	NA	NA	As legacy waste is lying in the slope so no technology could be adopted to process the same
110	DARJEELING	Kurseong	1	Kurseong (Down Hill from Pankhabari Road)	26°51'53.26" N 88°15'56.05" E	5.00	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	NA	NA	NA	NA	As legacy waste is lying in the slope so no technology could be adopted to process the same
111	DARJEELING	Mirik	1	Mirik Notified Area (Near DP Rai Road)	26°52'59.28" N 88°10'12.35" E	4.00	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	NA	NA	NA	NA	As legacy waste is lying in the slope so no technology could be adopted to process the same

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
112	KALIMPONG	Kalimpong	1	Kalimpong (near BhalulhopKhasmahal)	27° 5'24.23"N 88°28'39.82" E	8.25	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	NA	NA	NA	NA	As legacy waste is lying in the slope so no technology could be adopted to process the same
113	Malda	Old Malda	1	Near Fata Kesta Club, School para Mongolbari, Ward No-09	23.0172470° "N 88.1457094° E	0.5	0	0	NA		57200	0	57200	57200	0	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.15	Yes	No	No	No	
114	Murshidabad	Beldanga	1	Bagdanga math, Mouza-Maniknagar, J.L no.-54, P.S-Beldanga, Dist-Murshidabad	23.93300, 88.30323	2.05					57761	0	57761	57761	0	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.18	Yes	No	No	No	
115	Pur Burdwan	Dainhat	1	Ganga Rasta, Ward-02	23.614199°" N 88.17797°E	0.75					17960	0	17960	17960	0	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.99	Yes	No	No	No	
TOTAL			**126**			**694.82**	13930062.71	**8389591.18**		**276.20**	**13861680.00**	**0.00**	**27791742.71**	**19402151.52**	**8389591.18**		**90.86**										**1528.55**					

**** No Dumpsite Present at 13 ULBs i.e. Haldia, Pujali, Domkal, Falakata, Bishnupur, Mekhliganj, Buniadpur, Dhupguri, Mal, Maynaguri, Haringhata, Baduria, North Barrackpore,**

Legacy Waste Status

																		Composition of the Waste						Final Destination of the Components at					Action plan to remidiate and recover the sites				
Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	P-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	P-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	Remarks	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)
1	ALIPURDUAR	Alipurduar	1	Beside Radhamadhab Mandir	26°29'33"N 89°32'29"E	0.33	4274	4274	Completed	0.33	0	0	4274	0	4274	0	0.33	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
2	BANKURA	Bankura	1	Keshra Trenching Ground	23.267285° N 87.035388°E	16.53	172937.6	172938	Completed	6.50	187000	0	359937.6	187000	172938	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	10.285		Yes	Yes	Yes	Yes
3	BANKURA	Sonamukhi	1	Adrab Bazar	23.300813° N 87.398289°E	1.50	2400	2400	Completed	1.50	0	0	2400	0	2400	0	1.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
4	BIRBHUM	Bolpur	1	Bolpur, Khoskadambatur, P. S. Bolpur, JL No. 95, Plot No. 2590, 2703	23.677955° N, 87.721413°E	3.33	60814	60814	Completed	1.20	108870	0	169684	108870	60814	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.98785		Yes	Yes	Yes	Yes
5	BIRBHUM	Dubrajpur	1	Mahaprabhu Gate	23.78196°N 87.36859°E	1.20	6122	6122	Completed	0.75	1,05,914	0	112036	105914	6122	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.82527		Yes	No	No	No
6	BIRBHUM	Rampurhat	1	Bonat & Kusumba Road	24.18826°N 87.75746°E	3.85	24212	24212	Completed	0.85	49280	0	73492	49280	24212	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.7104		Yes	Yes	Yes	Yes
7	BIRBHUM	Sainthia	1	Ward No. 14	23.5657°N 87.4039°E	1.10	7261	7261	Completed	0.40	80,805	0	88066	80805	7261	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.444275		Yes	No	No	No
8	BIRBHUM	Suri	1	Dhanyogram (JL No. - 206)	23.95225°N 87.48576°E	2.00	16428	16428	Completed	0.60	48870	0	65298	48870	16428	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.68785		Yes	Yes	Yes	Yes
9	BIRBHUM	Nalhati	1	Khanpur	24.30658°N 87.825631°E	5.00	56000	56000	Completed	5	36800	0	92800	36800	56000	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.024		Yes	No	No	No
10	COOCH BEHAR	Cooch Behar	1	Guriahati-II	26.299124° N 89.468282°E	6.75	67319.21	67319	Completed	2.20	177600	0	244919.21	177600	67319	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.768		Yes	No	No	No
11	COOCH BEHAR	Dinhata	1	Buri dharia	26.821°N 89.2652°E	3.20	12432	12432	Completed	1.20	30220	0	42652	30220	12432	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.6621		Yes	No	No	No
12	COOCH BEHAR	Haldibari	1	DBDH	26°19'27.4" N 88°47'6.5"E	0.73	6491.17	6491	Completed	0.20	41400	0	47891.17	41400	6491	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.277		Yes	No	No	No
13	COOCH BEHAR	Mathabhanga	2	Ward No. - 4 (behind Jangli Kalibari and Manasi River) & Ward No. - 2, KhadanGhat (Beside Manasi and Sutunga River)	26.2041°N 89.137°E & 26.2017°N 89.1316°E	2.20	8830.16	8830	Completed	1.00	14800	0	23630.16	14800	8830	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.814		Yes	No	No	No
14	COOCH BEHAR	Tufanganj	1	Kamat Phoolbari	26.1846°N 89.4014°E	2.70	8918.15	8918	Completed	1.00	19640	0	28558.15	19640	8918	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.0802		Yes	No	No	No
15	DAKSHIN DINAJPUR	Balurghat	1	5 no. Bhatpara, Dangi Under Bhatpara Gram panchayat	25.2052169° N 88.76702841 °E	9.99	72514.595	72515	Completed	3.00	15453	0	87967.595	15453	72515	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.849915		Yes	Yes	Yes	Yes
16	DAKSHIN DINAJPUR	Gangarampore	1	Naroi Dump-pit, 6 no. Anchol, Gangarappur	25.402148° N 88.532081°E	2.25	4275	4275	Completed	1.10	29100	0	33375	29100	4275	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.6005		Yes	Yes	Yes	Yes
17	DARJEELING	Siliguri MC	1	Don Bosco colony	26.746839° N 88.452293°E	26.00	379382	379382	Completed	10.50	1150000	0	1529382	1150000	379382	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	63.25		Yes	Yes	Yes	Yes

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	P-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	P-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	Remarks	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)
18	HOOGHLY	Chandannagore MC	1	Kalupukur Vermi-Compost Plant, Kolupukur Bhagar more, Ward No. 8	22°52'13"N, 88°21'32"E	4.94	215916	215916	Completed	1.00	106252	0	322168	106252	215916	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.84386		Yes	Yes	Yes	Yes
19	HOOGHLY	Hooghly Chinsurah	1	Kedia – I GP, Sukantanagar Rabindranagar	22°53'35"N 88°22'44"E	6.50	126266	126266	Completed	2.50	102159	0	228425	102159	126266	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.618745		Yes	Yes	Yes	Yes
20	HOOGHLY	Baidyabati	1	RWMC	22.7888N, 88.31202E	52.00	220794	130254	Jun-25	5.00	0	0	220794	90540	130254	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.9797	Legacy Present	No	No	No	No
21	HOOGHLY	Champdany									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		0	0	0	0
22	HOOGHLY	Rishra									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		0	0	0	0
23	HOOGHLY	Serampore									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		0	0	0	0
24	HOOGHLY	Uttarpara-Kotrung									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		0	0	0	0
25	HOOGHLY	Konnagar									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		0	0	0	0
26	HOOGHLY	Bhadreswar	1	Sanjay colony, N S Road,	22.834139°N , 88.349718°E	0.42	320000	0	Jun-26	0	337000	0	657000	657000	0	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	36.135		Yes	No	No	No
27	HOOGHLY	Dankuni	1	Beside Parbatipur Road, Ramanathpur (Panchayet Area)	22°40'31".N , 88°13'58".E	2.40	48078	48078	Completed	5	0	0	48078	0	48078	0	5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
28	HOOGHLY	Bansberia	2	Ward no. 8 & 18	22° 57'45.1" N 88° 23'45.3" E	2.79	47000	0	Sep-25	0	108000	0	155000	155000	0	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.525		Yes	No	No	No
29	HOOGHLY	Arambagh	1	Kalipur (Ward No 6)	22.88525N, 87.77549E	1.20	37750	0	Sep-25	0	37750	0	75500	75500	0	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.1525		Yes	Yes	Yes	Yes
30	HOOGHLY	Tarakeswar	1	Kadamtala, Ward No. 13	22.88326N, 88.02701E	0.44	16610	0	Sep-25	0	16610	0	33220	33220	0	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.8271		Yes	Yes	Yes	Yes
31	HOWRAH	Uluberia	2	Banitala, Ward No. 31 (Beside NH 6) & Ward No. 6, Bauria	22.478330° N 88.078462°E & 22.499437° N 88.169112°E	6.50	28394	28394	Completed	3.00	105000	0	133394	105000	28394	Sep-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.775		Yes	Yes	Yes	Yes
32	HOWRAH	Bally	1	Chandmari	22.635658° N 88.334197°E	3.00	120000	30132.59	Dec-25	0.00	0	0	120000	89867	30133	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.94270755	Legacy Present	No	No	No	No
33	HOWRAH	Howrah MC	1	Belgachia	22°36'35"N 88°19'34"E	21.99	9,61,567	364026.87	Oct-26	1.80	750000	0	1711567	1347540	364027	Oct-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	74.11470715		Yes	Yes	Yes	No
34	JALPAIGURI	Jalpaiguri	1	Paharpur	26.564305° N 88.736121°E	2.50	25891.6	25892	Completed	2.50	160000	0	185891.6	160000	25892	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.8	Legacy Present	Yes	No	No	No
35	JHARGRAM	Jhargram	1	Jhargram (Near Jaralat)	22°26'36"N 86°58'29"E	12.00	3739	3739	Completed	12.00	10000	0	13739	10000	3739	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.55		No	NA	NA	NA
36	KOLKATA	Kolkata MC	2	Garden Reach	Lat 22.530578° N Long 88.291576° E	19.77	1500000	10000	Mar-26	0.80	0	0	1500000	1490000	10000	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	81.95		Yes	No	No	No

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	P-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	P-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	Remarks	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)
	[illegible]	[illegible]	2	DHAPA Under W-58 OF BR-VII/KMC	22°32'32.6" N 88°25'17.6" E	60.00	4000000	1813000	Mar-26	25.00	2000000	0	6000000	4187000	1813000	Mar-27	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	230.285		Yes	No	No	No
37	MALDA	English Bazar	1	English Bazar (muza Bahadurpur)	24°54'59.18" N 88°6'57.87" E	3.52	3250	3250	Completed	0.52	240000	0	243250	240000	3250	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	13.2		Yes	No	No	No
38	MURSHIDABAD	Berhampore	1	Banappare ring road	Komolapur Khadamkhandi	2.16	123981	123981	Completed	1.00	230000	0	353981	230000	123981	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	12.65		Yes	Yes	Yes	Yes
39	MURSHIDABAD	Jangipur	1	Azgarpara near Milanpur	24°28'43.79" N 88°3'10.75" E	0.28	3211	3211	Completed	0.10	65180	0	68391	65180	3211	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.5849		Yes	No	No	No
40	MURSHIDABAD	Jiaganj-Azimganj	1	Ghoramari (Azimganj Side)	24°14'14.8" N 88°15'56.8" E	3.00	19426	19426	Completed	1.00	53000	0	72426	53000	19426	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.915		Yes	No	No	No
41	MURSHIDABAD	Murshidabad	1	Kathgola bagan, Ward No. - 15	Kathgola bagan, Ward No. 15	5.38	94059	94059	Completed	1.00	62500	0	156559	62500	94059	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.4375		Yes	No	No	No
42	MURSHIDABAD	Dhulian	1	Dhuliyan (near Ratanpur)	24°39'29.89" N 87°55'50.74" E	2.00	0	0	Sep-25	0	0	0	0	0	0	0	2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
43	MURSHIDABAD	Kandi	1	Kandi (Ward No. 12)	23°56'51.56" N 88°4'3.47"E	5.82	0	0	Sep-25	0	0	0	0	0	0	0	5.82	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
44	NADIA	Birnagar	1	Mathurapukur	23.268035° N 88.55683°E	3.00	6799	6799	Completed	3.00	0	0	6799	0	6799	0	3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
45	NADIA	Gayeshpur	2	1) Near VS Club, Ward No.-16 & Near SHG Training Centre, Ward No.- 15	22.955519° N 88.472313°E & 22.953232° N 88.48228°E	5.00	12465	12465	Completed	1.20	34400	0	46865	34400	12465	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.892		Yes	No	No	No
46	NADIA	Kalyani	2	Near Kacharipara, Ward No.-6 & Beside highway, Ward No.-10	22.960863° N, 88.439684°E & 22.960863° N 88.439684°E	2.1 & 1.4	60543	60543	Completed	1.20	115000	0	175543	115000	60543	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.325		Yes	Yes	Yes	Yes
47	NADIA	Krishnanagar	1	Godadanga, Ward – 5	(23.4052240 °N 88.5116291° E	8.00	51802	51802	Completed	3.00	412000	0	463802	412000	51802	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	22.66	Legacy Present	Yes	No	No	No
48	NADIA	Nabadwip	1	Near Bishnupriya Halt Station, Ward No. – 1	23.4150386° N 88.3562766° E	12.35	83900	83900	Completed	5.00	111870	0	195770	111870	83900	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.15285		Yes	Yes	Yes	Yes
49	NADIA	Ranaghat	1	Anulia GP	23.268035° N 88.55683°E	6.31	65374	65374	Completed	3.30	99750	0	165124	99750	65374	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.48625		Yes	No	No	No
50	NADIA	Santipur	1	Moylar math, Ward no. – 10	23.2501021° N 88.4116394° E	4.55	22097	22097	Completed	2.20	86840	0	108937	86840	22097	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.7762		Yes	Yes	Yes	Yes
51	NADIA	Taherpur	1	Cremation Ground Road, Ward No.-1	23.270603° N 88.521961°E	1.26	6119	6119	Completed	0.50	14140	0	20259	14140	6119	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.7777		Yes	No	No	No
52	NADIA	Chakdah	1	Ward No - 19	23.062613N, 88.517296E	5.00	19426	19426	Completed	5.00	0	0	19426	0	19426	0	5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
53	NADIA	Cooper's Camp	1	Ward 2- near burning ghat	23.270603N, 88.521961E	0.50	19620	0	Dec-25	0	22860	0	42480	42480	0	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.3364		Yes	No	No	No

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	P-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	P-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	Remarks	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)
54	NORTH 24-PARGANAS	Barasat	1	Kadambagachi	22.70483°N 88.51908°E	3.50	67846.935	67847	Completed	3.50	0	0	67846.935	0	67847	0	3.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
55	NORTH 24-PARGANAS	Barrackpore	1	Kolkata Road	22.748542° N 88.382122°E	5.00	72846	72846	Completed	3.00	57812	0	130658	57812	72846	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.17966	Legacy Present	Yes	Yes	No	No
56	NORTH 24-PARGANAS	Basirhat	1	Ward 8	22.65254°N 88.87294°E	4.00	24273.065	24273	Completed	4.00	0	0	24273.065	0	24273	0	4	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		NA	NA	NA	NA
57	NORTH 24-PARGANAS	Bongaon	1	Beside Indira Park, Ward No. - 19 (opposite Truck Parking lot)	23°1'44.13" N 88°50'31.40" E	2.26	7013	7013	Completed	1.20	84832	0	91845	84832	7013	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.66576		Yes	No	No	No
58	NORTH 24-PARGANAS	Habra	1	Near Banipur Home, Ward No.- 3	22.818064° N 88.635827°E	1.20	9458.1	9458	Completed	0.98	91700	0	101158.1	91700	9458	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.0435		Yes	No	No	No
59	NORTH 24-PARGANAS	Kanchrapara	1	Bidhanpally	23.4150386° N 88.3562766° E	3.00	24282	24282	Completed	1.20	136000	0	160282	136000	24282	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.48		Yes	No	No	No
60	NORTH 24-PARGANAS	Khardah	1	Ruiyaiswaripur	22°44'31"N 88°24'25"E	2.75	46118	46118	Completed	1.00	38140	0	84258	38140	46118	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.0977		Yes	Yes	No	No
61	NORTH 24-PARGANAS	Madhyamgram	1	Digberia	22.69264° 88.50134°E	7.17	116068	116068	Completed	1.19	87700	0	203768	87700	116068	May-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.8235		Yes	Yes	No	No
62	NORTH 24-PARGANAS	Panihati	1	Ramchandra Pur	22°41'31"N 88°23'10"E	1.50	51763.391	51763	Completed	0.20	120000	0	171763.391	120000	51763	May-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.6		Yes	Yes	Yes	Yes
63	NORTH 24-PARGANAS	Taki	1	Mansing road	22.57787°N 88.93308°E	0.80	3625	3625	Completed	0.35	13400	0	17025	13400	3625	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.737		Yes	No	No	No
64	NORTH 24-PARGANAS	Titagarh	1	Mathpara	22.88326°N 88.02701°E	4.90	120886	120886	Completed	1.00	44716	0	165602	44716	120886	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.45938		Yes	No	No	No
65	NORTH 24-PARGANAS	Bhatpara	2	Madral & Jilabi Math	22.87426°N 88.41807°E & 22.85932°N 88.39001°E	2.57	58260	58260	Completed	1.00	71905	0	130165	71905	58260	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.954775		Yes	No	No	No
66	NORTH 24-PARGANAS	Garulia	1	Fanching Ground Road	22.817161° N 88.372613°E	1.80	52499	51991.017	Completed	1.00	38218	0	90717	38726	51991	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.129929065		Yes	Yes	No	No
67	NORTH 24-PARGANAS	Halisahar	1	Niraljan Trenching Ground	23.2501021° N 88.4116394° E	0.84	6799	6789	Completed	0.25	43905	0	50704	43915	6789	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.415325		Yes	Yes	Yes	No
68	NORTH 24-PARGANAS	Bidhannagar MC	1	Mollar Bheri	22.35'52" N 88.26'47" E	55.00	300000	300000	Completed	55.00	0	0	300000	0	300000	0	55	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		NA	NA	NA	NA
69	NORTH 24-PARGANAS	Baranagar	1	Pramodnagar, Beside Belghoria Expressway	22.648657N, 88.39736SE	22.68	845400	845400	Completed	2.00	1100000	0	1945400	1100000	845400	Dec-27	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio	Low land filling	Low land filling & used	Cement Plants of	Moisture Loss and	60.5		Yes	Yes	Yes	Yes
70	NORTH 24-PARGANAS	Dum Dum									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		Yes	Yes	Yes	Yes
71	NORTH 24-PARGANAS	New Barrackpore									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		Yes	Yes	Yes	Yes
72	NORTH 24-PARGANAS	North Dum Dum									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		Yes	Yes	Yes	Yes

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	P-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	P-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	Remarks	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)
73	NORTH 24-PARGANAS	South Dum Dum									0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		Yes	Yes	Yes	Yes
74	NORTH 24-PARGANAS	Kamarhati	1	Matagiri Hana Pally, Kamarhati	22.679309N, 88.379746E	8.00	50000	50000	Completed	0.50	900000	0	950000	900000	50000	Dec-27	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	49.5		Yes	Yes	Yes	Yes
75	NORTH 24-PARGANAS	Naihati	3	Along Patterson road, Chighat, W.No. 14, Naihati	22.897030N, 88.410584E	23.94	300000	300000	Completed	15.00	144000	0	444000	144000	300000	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.92		Yes	Yes	Yes	Yes
76	NORTH 24-PARGANAS	Ashoknagar-Kalyangarh	1	Ward 22 beside Naihati-Habra Road	22.50'21" N, 88.35'44 E	21.49	81585	41275	Sep-25	6.13	0	0	81585	40310	41275	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil	Cement Plants of other states	Moisture Loss and other	2.21705	Legacy Present	No	No	No	No
77	NORTH 24-PARGANAS	Gobardanga	1	Ward 3- near Belluni bridge	22.52'49" N, 88.44'37 E"	4.00	19296	19296	Completed	3.50	0	0	19296	0	19296	0	3.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
78	PaSCHIM BARDHAMAN	Asansol MC	5	a.Asansol-Kalipahari, b.Bumpur-Hirapur, c.Raniganj- Ronai, d.Jamuria- 6 No. Bypass, e.Kulti- Aldi	a.23.614345°N,87.133207°E, b.23.661219°N; 86.939790°E , c.23.614345°N,87.133207°E, d.23.707714°N,87.074470°E, e.23.703844°N,86.883500°E	36.95	1100000	496284	Mar-26	11.00	700000	0	1800000	1303716	496284	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	71.70438		Yes	No	No	No
79	PaSCHIM BARDHAMAN	Durgapur MC	1	Sankarpur	23.530679° N 87.356380°E	6.60	300000	300000	Completed	3.00	730000	0	1030000	730000	300000	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	40.15		Yes	Yes	Yes	Yes
80	PASCHIM MEDINIPUR	Ghatal	1	Argora Shyampur	22.6636275° N 87.7241965° E	1.25	16038.41	16038	Completed	0.50	41520	0	57558.41	41520	16038	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.2836		Yes	No	No	No
81	PASCHIM MEDINIPUR	Kharagpur	1	Hiradih, Ward No. - 32	22.321856° 87.280617°E	1.50	29995.51	29996	Completed	1.50	50000	0	79995.51	50000	29996	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.75		No	NA	NA	NA
82	PASCHIM MEDINIPUR	Khirpai	1	Bhutdanga	22.706906° N 87.615709°E	2.00	693.34	693	Completed	1.00	9480	0	10173.34	9480	693	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.5214		Yes	No	No	No
83	PASCHIM MEDINIPUR	Midnapore	1	Dharma Dumping Ground, Hosnabad Mouuza	22.421732° N 87.340956°E	4.00	168814.31	168814	Completed	1.50	264000	0	432814.31	264000	168814	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	14.52		Yes	Yes	Yes	Yes
84	PASCHIM MEDINIPUR	Chandrakona	1	Ransagar, Ward No - 02	22.7191N, 88.3800E	2.00	40902	40902	Completed	1.20	21720	0	62622	21720	40902	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.1946		Yes	No	No	No
85	PASCHIM MEDINIPUR	Kharar	2	Kharar ByPass Road	30.750526N, 76.640536E & 30.750528N, 76.640539E	0.57	2044	2044	Completed	0.30	0	0	2044	0	2044	0	0.3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
86	PASCHIM MEDINIPUR	Ramjibanpur	1	Bypass Road	22.824006N, 87.62073E	0.20	4611	4611	Completed	0.10	0	0	4611	0	4611	0	0.2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0		NA	NA	NA	NA
87	PURBA BARDHAMAN	Barddhaman	1	Kapilbagan	25°14'16.5" N 87°51'7.3"E	6.85	180825	180825	Completed	1.20	390000	0	570825	390000	180825	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	21.45		Yes	Yes	Yes	Yes
88	PURBA BARDHAMAN	Gushkara	1	Ratani Kalitala	23.498347° N, 87.744647°E	2.00	7285	7285	Completed	0.50	54235	0	61520	54235	7285	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.982925		Yes	No	No	No
89	PURBA BARDHAMAN	Kalna	1	Beside Kalna Rail Station, kalayanpur Gram Payanchat Ambika Kalna	23.213381° N 88.353344°E	3.33	36850	36850	Completed	0.50	71900	0	108750	71900	36850	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.9545		Yes	No	No	No

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	P-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	P-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	Remarks	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)
90	PURBA BARDHAMAN	Katwa	1	Stadium Para, W-12	22.71923N, 88.38046E	2	3885	3885	Completed	1.00	67720	0	71605	67720	3885	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.7246		Yes	No	No	No
91	PURBA BARDHAMAN	Memari	1	Lock gate, Nudipur Bridge Memari Burdwan	Lock gate, Nudipur Bridge	2.50	38851	38851	Completed	1.25	28425	0	67276	28425	38851	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil	Cement Plants of other states	Moisture Loss and other	1.563375		Yes	No	No	No
92	PURBA MIDNAPORE	Egra	1	Ramkrishnapur	22°23'58.04" N 87°45'19.13" E	0.32	2122.51	2123	Completed	0.12	41160	0	43282.51	41160	2123	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.2638		Yes	No	No	No
93	PURBA MIDNAPORE	Panskura	1	Panskura Railway Station	22°23'58.04" N 87°45'19.13" E	2.28	667.3	667	Completed	1.20	23840	0	24507.3	23840	667	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.3112		Yes	Yes	Yes	Yes
94	PURBA MIDNAPORE	Tamralipta	1	Malia Bari	22°16'6"N 87°55'48"E	0.49	23890.48	23890	Completed	0.20	28720	0	52610.48	28720	23890	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.5796		Yes	Yes	Yes	Yes
95	PURBA MIDNAPORE	Contai	1	Contai Digha Road	21.765423N, 87.730407E	4.59	62385	62385	Completed	2.00	98000	0	160385	98000	62385	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.39		Yes	No	No	No
96	PURULIA	Purulia	3	a.Chharra, b.Banga Bari Samsan, c.Hutmura	a.23.3753°N 86.42805°E, b.23.3497°N 86.38601°E, c.23.3495°N 86.4992°E	10.83	77325	77325	Completed	4.00	119800	0	197125	119800	77325	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.589		Yes	No	No	No
97	PURULIA	Raghunathpur	3	a.W–2 (Between Lohar & Mondal Petrol Pump), b.W-7 (beside Gara Kiari Mandir), c.W -11 (Stadium More)	a.23.53709° N 86.6746°E, b.23.52927° N 86.6763°E, c.23.52928° N 86.6763°E	1.00	8201	8201	Completed	0.50	27960	0	36161	27960	8201	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.5378		Yes	No	No	No
98	PURULIA	Jhalda	3	a.Beside Panagarh-Moregram SH. bPat Jhalda Road Railway Cabin Side, c.Ward 5	a.23.361579 °N 85.971785°E , b.23.37796 N, 85.98471E, c.23.34956N , 85.97531E	2.00	16318.43	16318	Completed	0.50	0	0	16318.43	0	16318	0	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	No Legacy	NA	NA	NA	NA
99	SOUTH 24-PARGANAS	Baruipur	1	Kritankhola	22°20'14"N 88°26'49"E	2.30	19685	19685	Completed	1.20	113000	0	132685	113000	19685	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.215		Yes	No	No	No
100	SOUTH 24-PARGANAS	Budge Budge	1	Subhas Udyan trenching ground Ward No. - 17	22.47335°N 88.18879°E	3.48	20721	20721	Completed	2.20	41100	0	61821	41100	20721	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.2605		Yes	No	No	No
101	SOUTH 24-PARGANAS	Diamond Harbour	1	Doloanghata, Beside NH 117 (Panchayet Area)	22°10'17"N 88°13'44"E	2.00	9421.092	9421	Completed	0.50	34710	0	44131.092	34710	9421	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.90905		Yes	No	No	No
102	SOUTH 24-PARGANAS	Jaynagar-Mazilpur	1	Shahajadpur	22°10'85"N 88°26'2"E	4.00	1379	1379	Completed	1.00	21140	0	22519	21140	1379	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.1627		Yes	No	No	No
103	SOUTH 24-PARGANAS	Maheshtala	1	Sarengabad, Ward No. – 35	22.49216°N 88.20567°E	19.61	230517	230517	Completed	4.00	104000	0	334517	104000	230517	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.72		Yes	Yes	Yes	Yes
104	SOUTH 24-PARGANAS	Rajpur-Sonarpur	1	Mailapota	22°25'16"N 88°25'37"E	10.00	18511.329	18511	Completed	2.00	4223	0	22734.329	4223	18511	Dec-25	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.232265		Yes	No	No	No
105	UTTAR DINAJPUR	Dalkhola	1	Uttar Dalkhola	25°53'6.6"N 87°50'26.1" E	0.68	7375	7375	Completed	0.68	28550	0	35925	28550	7375	Mar-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.57025		Yes	No	No	No
106	UTTAR DINAJPUR	Islampur	1	Sonakhoda Gurujbasti Trenching Ground; Ward No. – 9	26°15'32.5" N 88°12'13.1" E	0.17	1469	1469	Completed	0.10	24570	0	26039	24570	1469	Jan-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.35135		Yes	No	No	No

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	P-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	P-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	Remarks	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)
107	UTTAR DINAJPUR	Kaliaganj	1	Mahadebpur, Ward No. - 17)	25°38'25.6" N 88°18'26.6" E	2.84	28144	28144	Completed	1.00	33930	0	62074	33930	28144	Feb-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.86615		Yes	No	No	No
108	UTTAR DINAJPUR	Raiganj	1	Bandar Sashan, Ward No. – 22	25°36'31"N 88°7'0.9"E	3.00	38429.02	38429	Completed	1.00	141665	0	180094.02	141665	38429	Aug-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.791575		Yes	No	No	No
109	DARJEELING	Darjeeling	1	Darjeeling (Near Gorkha Road and Victoria Road)	27° 2'26.60"N 88°15'33.05" E	3.33	0	0	Mar-26	0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	Slope Problem	NA	NA	NA	NA
110	DARJEELING	Kurseong	1	Kurseong (Down Hill from Pankhabari Road)	26°51'53.26" N 88°15'56.05" E	5.00	0	0	Mar-26	0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	Slope Problem	NA	NA	NA	NA
111	DARJEELING	Mirik	1	Mirik Notified Area (Near DP Rai Road)	26°52'59.28" N 88°10'12.35" E	4.00	0	0	Mar-26	0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	Slope Problem	NA	NA	NA	NA
112	KALIMPONG	Kalimpong	1	Kalimpong (near BhalulhopKhasmahal)	27° 5'24.23"N 88°28'39.82" E	8.25	0	0	Mar-26	0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0	Slope Problem	NA	NA	NA	NA
113	Malda	Old Malda	1								57200	0	57200	57200	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.146		Yes	No	No	No
114	Murshidabad	Beldanga	1	Bagdanga math, Mouza-Maniknagar, J.L. no.-54, P.S-Beldanga, Dist-Murshidabad	23.93300, 88.30323	2.05					57761	0	57761	57761	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.176855		Yes	No	No	No
115	Pur Burdwan	Dainhat	1	Ganga Rasta, Ward-02	23.614199°° N 88.17797°E	0.75					17960	0	17960	17960	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.9878		Yes	No	No	No
TOTAL			**126**			**694.32**	**13930062.71**	**8389591.18**		**272.70**	**13796680.00**	**0.00**	**27726742.71**	**19337151.52**	**8389591.18**	**3459110.00**	**89.65**															
											137.9668	0	277.2674271	193.3715152	83.89591184	34.5911															

** No Dumpsite Present at 13 ULBs i.e. Haldia, Pujali, Domkal, Falakata, Bishnupur, Mekhliganj, Buniadpur, Dhupguri, Mal, Maynaguri, Haringhata, Baduria, North Barrackpore

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site
1	ALIPURDUAR	Alipurduar									
2	BANKURA	Bankura									
3	BANKURA	Sonamukhi									
4	BIRBHUM	Bolpur									
5	BIRBHUM	Dubrajpur									
6	BIRBHUM	Rampurhat									
7	BIRBHUM	Sainthia									
8	BIRBHUM	Suri									
9	BIRBHUM	Nalhati									
10	COOCH BEHAR	Cooch Behar									
11	COOCH BEHAR	Dinhata									
12	COOCH BEHAR	Haldibari									
13	COOCH BEHAR	Mathabhanga									
14	COOCH BEHAR	Tufanganj									
15	DAKSHIN DINAJPUR	Balurghat									
16	DAKSHIN DINAJPUR	Gangarampore									

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site
17	DARJEELING	Siliguri MC									
18	HOOGHLY	Chandannagore MC									
19	HOOGHLY	Hooghly Chinsurah									
20	HOOGHLY	Baidyabati									
21	HOOGHLY	Champdany									
22	HOOGHLY	Rishra									
23	HOOGHLY	Serampore									
24	HOOGHLY	Uttarpara-Kotrung									
25	HOOGHLY	Konnagar									
26	HOOGHLY	Bhadreswar									
27	HOOGHLY	Dankuni									
28	HOOGHLY	Bansberia									
29	HOOGHLY	Arambagh									
30	HOOGHLY	Tarakeswar									
31	HOWRAH	Uluberia									
32	HOWRAH	Bally									
33	HOWRAH	Howrah MC									
34	JALPAIGURI	Jalpaiguri									
35	JHARGRAM	Jhargram									
36	KOLKATA	Kolkata MC									
37	MALDA	English Bazar									

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site
38	MURSHIDABAD	Berhampore									
39	MURSHIDABAD	Jangipur									
40	MURSHIDABAD	Jiaganj-Azimganj									
41	MURSHIDABAD	Murshidabad									
42	MURSHIDABAD	Dhulian									
43	MURSHIDABAD	Kandi									
44	NADIA	Birnagar									
45	NADIA	Gayeshpur									
46	NADIA	Kalyani									
47	NADIA	Krishnanagar									
48	NADIA	Nabadwip									
49	NADIA	Ranaghat									
50	NADIA	Santipur									
51	NADIA	Taherpur									

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site
52	NADIA	Chakdah									
53	NADIA	Cooper's Camp									
54	NORTH 24-PARGANAS	Barasat									
55	NORTH 24-PARGANAS	Barrackpore									
56	NORTH 24-PARGANAS	Basirhat									
57	NORTH 24-PARGANAS	Bongaon									
58	NORTH 24-PARGANAS	Habra									
59	NORTH 24-PARGANAS	Kanchrapara									
60	NORTH 24-PARGANAS	Khardah									
61	NORTH 24-PARGANAS	Madhyamgram									
62	NORTH 24-PARGANAS	Panihati									
63	NORTH 24-PARGANAS	Taki									
64	NORTH 24-PARGANAS	Titagarh									
65	NORTH 24-PARGANAS	Bhatpara									
66	NORTH 24-PARGANAS	Garulia									
67	NORTH 24-PARGANAS	Halisahar									

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site
68	NORTH 24-PARGANAS	Bidhannagar MC									
69	NORTH 24-PARGANAS	Baranagar									
70	NORTH 24-PARGANAS	Dum Dum									
71	NORTH 24-PARGANAS	New Barrackpore									
72	NORTH 24-PARGANAS	North Dum Dum									
73	NORTH 24-PARGANAS	South Dum Dum									
74	NORTH 24-PARGANAS	Kamarhati									
75	NORTH 24-PARGANAS	Naihati									
76	NORTH 24-PARGANAS	Ashoknagar-Kalyangarh									
77	NORTH 24-PARGANAS	Gobardanga									
78	PaSCHIM BARDHAMAN	Asansol MC									
79	PaSCHIM BARDHAMAN	Durgapur MC									
80	PASCHIM MEDINIPUR	Ghatal									
81	PASCHIM MEDINIPUR	Kharagpur									
82	PASCHIM MEDINIPUR	Khirpai									
83	PASCHIM MEDINIPUR	Midnapore									
84	PASCHIM MEDINIPUR	Chandrakona									

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site
85	PASCHIM MEDINIPUR	Kharar									
86	PASCHIM MEDINIPUR	Ramjibanpur									
87	PURBA BARDHAMAN	Barddhaman									
88	PURBA BARDHAMAN	Gushkara									
89	PURBA BARDHAMAN	Kalna									
90	PURBA BARDHAMAN	Katwa									
91	PURBA BARDHAMAN	Memari									
92	PURBA MIDNAPORE	Egra									
93	PURBA MIDNAPORE	Panskura									
94	PURBA MIDNAPORE	Tamralipta									
95	PURBA MIDNAPORE	Contai									
96	PURULIA	Purulia									
97	PURULIA	Raghunathpur									
98	PURULIA	Jhalda									

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site
99	SOUTH 24-PARGANAS	Baruipur									
100	SOUTH 24-PARGANAS	Budge Budge									
101	SOUTH 24-PARGANAS	Diamond Harbour									
102	SOUTH 24-PARGANAS	Jaynagar-Mazilpur									
103	SOUTH 24-PARGANAS	Maheshtala									
104	SOUTH 24-PARGANAS	Rajpur-Sonarpur									
105	UTTAR DINAJPUR	Dalkhola									
106	UTTAR DINAJPUR	Islampur									
107	UTTAR DINAJPUR	Kaliaganj									
108	UTTAR DINAJPUR	Raiganj									
109	DARJEELING	Darjeeling									
110	DARJEELING	Kurseong									
111	DARJEELING	Mirik									
112	KALIMPONG	Kalimpong									
113	Malda	Old Malda									
114	Murshidabad	Beldanga									
115	Pur Burdwan	Dainhat									

Sl No	District	ULB	P-II RfP prepared (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued (Y/N)	P-II Work Started (Y/N)	RfP prepared	Tender floated	Work order issued	Work Started	Timeline to process at each site

** No Dumpsite Present at 12 ULBs i.e. Haldia, Pujali, Domkal, Falakata, Bishnupur, Mekhliganj, Buniadpur, Dhupguri, Mal, Maynaguri, Haringhata, Baduria,

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
1	Bankura	Bankura	**5.67**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
2	Bankura	Bishnupur	**2.8**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
3	Bankura	Sonamukhi	**1.41**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
4	Paschim Burdwan	Asansol MC	**47.7**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
5	Purba Burdwan	Barddhaman	**12.98**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
6	Purba Burdwan	Dainhat	**1.01**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
7	Paschim Burdwan	Durgapur MC	**23.37**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
8	Purba Burdwan	Gushkara	**1.46**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
9	Purba Burdwan	Kalna	**2.34**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
10	Purba Burdwan	Katwa	**3.95**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
11	Purba Burdwan	Memari	**1.71**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
12	Birbhum	Bolpur	**3.31**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
13	Birbhum	Dubrajpur	**1.57**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
14	Birbhum	Nalhati	**1.7**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
15	Birbhum	Rampurhat	**2.39**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
16	Birbhum	Sainthia	**1.84**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
17	Birbhum	Suri	**3.73**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
18	Cooch Behar	Cooch Behar	**3.21**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
19	Cooch Behar	Dinhata	**1.49**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
20	Cooch Behar	Haldibari	**0.59**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
21	Cooch Behar	Mathabhanga	**0.99**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
22	Cooch Behar	Mekhliganj	**0.38**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
23	Cooch Behar	Tufanganj	**0.87**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
24	Dakshin Dinajpur	Balurghat	**6.24**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
25	Dakshin Dinajpur	Buniadpur	**1.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
26	Dakshin Dinajpur	Gangarampore	**2.32**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
27	Darjeeling	Darjeeling	**4.97**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
28	Kalimpong	Kalimpong	**2.04**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
29	Darjeeling	Kurseong	**1.75**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
30	Darjeeling	Mirik	**0.47**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
	Darjeeling	Siliguri MC	**21.17**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
32	Howrah	Uluberia	**10.85**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
33	Hooghly	Arambagh	**2.73**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
34	Hooghly	Baidyabati	**7**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
35	Hooghly	Bansberia	**6**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
36	Hooghly	Bhadreswar	**5.58**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
37	Hooghly	Champdany	**6**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
38	Hooghly	Chandannagore MC	**9.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
39	Hooghly	Dankuni	**3.92**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
40	Hooghly	Hooghly Chinsurah	**9.63**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
41	Hooghly	Konnagar	**3.85**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
42	Hooghly	Rishra	**5.89**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
43	Hooghly	Serampore	**7.68**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
44	Hooghly	Tarakeswar	**1.28**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
45	Hooghly	Uttarpara Kotrung	**6.89**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
46	Alipurduar	Alipurduar	**2.69**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
47	Jalpaiguri	Dhupguri	**1.84**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
48	Jalpaiguri	Jalpaiguri	**4.43**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
49	Jalpaiguri	Mal	**1.04**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
50	Malda	English Bazar	**8.48**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
51	Malda	Old Malda	**3.47**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
52	Murshidabad	Beldanga	**1.2**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
53	Murshidabad	Berhampore	**7.9**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
54	Murshidabad	Dhuliyan	**4.36**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
55	Murshidabad	Domkal	**5.03**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
56	Murshidabad	Jangipur	**4.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
57	Murshidabad	Jiaganj-Azimganj	**1.75**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
58	Murshidabad	Kandi	**2.29**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
59	Murshidabad	Murshidabad	**2.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
60	Nadia	Birnagar	**1.27**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
61	Nadia	Chakdah	**4.86**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
62	Nadia	Cooper's Camp	**0.78**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
63	Nadia	Gayeshpur	**3.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
64	Nadia	Haringhata	**1.9**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
65	Nadia	Kalyani	**5.15**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025

Sl No	District	ULB	Total per day generation of C&D waste (TPD)	The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization	Remarks
66	Nadia	Krishnanagar	**8.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
67	Nadia	Nabadwip	**6.75**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
68	Nadia	Ranaghat	**3.11**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
69	Nadia	Santipur	**6.26**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
70	Nadia	Taherpur	**0.86**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
71	North 24 Parganas	Ashokenagar-Kalyangarh	**5.02**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
72	North 24 Parganas	Baduria	**2.17**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
73	North 24 Parganas	Baranagar	**10.12**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
74	North 24 Parganas	Barasat	**11.49**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
75	North 24 Parganas	Barrackpore	**6.3**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
76	North 24 Parganas	Basirhat	**5.16**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
77	North 24 Parganas	Bhatpara	**15.92**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
78	North 24 Parganas	Bidhan Nagar MC	**26.16**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
79	North 24 Parganas	Bongaon	**4.49**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
80	North 24 Parganas	Dum Dum	**4.73**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
81	North 24 Parganas	Garulia	**2.43**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
82	North 24 Parganas	Gobardanga	**1.87**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
83	North 24 Parganas	Habra	**6.07**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
84	North 24 Parganas	Halisahar	**5.15**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
85	North 24 Parganas	Kamarhati	**13.66**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
86	North 24 Parganas	Kanchrapara	**5.35**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
87	North 24 Parganas	Khardah	**4.48**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
88	North 24 Parganas	Madhyamgram	**8.09**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
89	North 24 Parganas	Naihati	**9**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
90	North 24 Parganas	New Barrackpore	**3.17**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
91	North 24 Parganas	North Barrackpore	**5.48**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
92	North 24 Parganas	North Dum Dum	**10.29**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
93	North 24 Parganas	Panihati	**15.57**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
94	North 24 Parganas	South Dum Dum	**16.64**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
95	North 24 Parganas	Taki	**1.58**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
96	North 24 Parganas	Titagarh	**4.81**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
97	Paschim Midnapore	Chandrakona	**0.97**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
98	Paschim Midnapore	Ghatal	**2.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
99	Jhargram	Jhargram	**2.54**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
100	Paschim Midnapore	Kharagpur	**8.56**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
101	Paschim Midnapore	Kharar	**0.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
102	Paschim Midnapore	Khirpai	**0.68**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
103	Paschim Midnapore	Midnapore	**6.98**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
104	Paschim Midnapore	Ramjibanpur	**0.81**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
105	Purba Midnapore	Contai	**3.8**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
106	Purba Midnapore	Egra	**1.24**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
107	Purba Midnapore	Haldia	**8.28**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
108	Purba Midnapore	Panskura	**2.39**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
109	Purba Midnapore	Tamluk	**2.69**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
110	Jhalda	Jhalda	**0.81**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025

Sl No	District	ULB	Total per day generation of C&D waste (TPD)	The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization	Remarks
111	Purulia	Purulia	**4.99**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
112	Purulia	Raghunathpur	**1.06**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
113	South 24 parganas	Baruipur	**2.19**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
114	South 24 parganas	Budge Budge	**3.17**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
115	South 24 parganas	Diamond Harbour	**1.78**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
116	South 24 parganas	Jainagar-Mazilpur	**1.07**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
117	South 24 parganas	Maheshtala	**18.54**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
118	South 24 parganas	Pujali	**1.53**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
119	South 24 parganas	Rajpur-Sonarpur	**17.48**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
120	Uttar Dinajpur	Dalkhola	**1.53**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
121	Uttar Dinajpur	Islampur	**2.24**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
122	Uttar Dinajpur	Kaliaganj	**2.21**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
123	Uttar Dinajpur	Raiganj	**7.57**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
124	Howrah	Howrah MC	**44.16**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to September, 2025					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
125	Howrah	Bally	**12.04**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
126	Jalpaiguri	Maynaguri	**1.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
127	Alipurduar	Falakata	**2.23**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
128	Kolkata	Kolkata MC	**245.65**	**500**	
		Total =	965.79	500	

Status report of SLWM on Ganga bordering GPs for the month of Nov, 2025 (O.A. 200/2014)

Sl. No.	Name of the Districts	Total No. of Blocks	Total No. of GPs	Solid Waste Management		Grey Water Management	
				Construction of MRF completed	MRF functional	No. of Soak pit/ Leach pit	No. of Filter Chamber
1	Hooghly	2	12	12	10	9	532
2	Howrah	3	18	16	12	1019	1118
3	Malda	4	22	22	21	2195	3
4	Murshidabad	13	65	64	50	8180	111
5	Nadia	9	39	39	35	5736	101
6	Purba Bardhaman	6	19	16	14	1346	373
7	South-24 Parganas	10	49	47	42	6316	1199
Total		**47**	**224**	**216**	**184**	**24801**	**3537**

State Sanitation Cell
P&RD Department
Govt. of West Bengal

O.A. 673/2018 updated report till September, 2025

Plantation Activities

Sl. No.	River	Division	Details of plantation activities along the river
1	Ganga	24 – ParganaNorth	Nil
		Nadia Murshidabad	3rd year maintenance work over 02 ha qn going under Namami Gange -Scheme. (One Side Plantation)
2	Churni	Nadia Murshidabad	Advance (Nursery work) 100% completed. Creation work 100% completed during 2021-22. 3rd year monitoring work of One side of Churni, over 7.265 Ha is going on.

Development of Bio-Diversity Park

Sl. No	Division	River	Details of setting up Bio-diversity Parks by removing encroachment along the river.
1	24 – ParganaNorth	Ganga	Nil
		Churni	
2	Nadia Murshidabad	Ganga	Awaiting for final discussion from District Level Bio diversity Committee.

1. Kraberty
02/12/2025

Chief Conservator of Forests, SDP
& Member Secretary, WBSFDA

Capacity Utilization of Functional STPs in River Ganga in West Bengal as on Sept 2025

Sl NO.	Name of STP	Executing Agency	Built up Capacity (MLD)	Design flow to come as on Sept 25 (MLD)	Actual Utilization as on Sept 25 (MLD)	Percentage Utilization (%)	Technology
[1]	[2]	[3]	[4]	[5]	[6]	[7]	[8]
1	Jagaddal Bhatpara New	KMDA	31.0	25.10	16.18	64.46	FBAS
2	Shyamnagar	KMDA	10.0	8.10	3.80	46.91	FBAS
3	Jagaddal Bhatpara old	KMDA	9.50	7.69	1.57	20.42	ASP
4	Kankinara STP, Madrail, Bhatpara	KMDA	10.0	8.10	1.55	19.14	WSP
5	STP Kalyani-I	KMDA	11.0	11.00	10.15	92.27	TRICKLING FILTER
6	STP Kalyani-II	KMDA	10.0	10.00	9.22	92.20	WSP
7	Gayeshpur	KMDA	8.33	4.80	3.34	69.58	SBR
8	Bansberia	KMDA	0.30	0.30	0.28	93.33	WSP
9	Konnagar	KMDA	22.00	22.00	17.09	77.68	WSP
10	Naihati	KMDA	11.56	11.56	9.36	80.97	ASP
11	Barrackpore	KMDA	18.0	12.50	8.41	67.28	SBR
12	Barrackpore	KMDA	6.0	3.60	2.68	74.44	SBR
13	Halisahar	KMDA	16.0	10.75	10.53	97.95	SBR
14	Budge-Budge	KMDA	9.30	8.48	8.48	100.00	SBR
15	Nabadwip	KMDA	9.50	7.80	5.24	67.18	Extended Areation Tube Settler
16	Baidyabati	KMDA	6.00	6.00	4.89	81.50	Areated Lagoon
17	Bhadreswar	KMDA	7.60	7.60	3.48	45.79	Areated Lagoon
18	Garulia	KMDA	4.10	4.10	3.76	91.71	WSP
19	Chandannagar, Khalisani, Chinsurah- Hooghly	KMDA	18.16	18.16	5.80	31.94	TRICKLING FILTER
20	Chandannagar, Khalisani, Chinsurah- Hooghly	KMDA	4.54	4.54	1.45	31.94	OP
21	Titagarh	KMDA	4.54	4.54	4.45	98.02	ASP
22	Titagarh	KMDA	4.54	4.54	4.45	98.02	OP
23	Bandipur (Khardaha)	KMDA	14.10	14.10	12.32	87.38	WSP
24	Naihati	KMDA	6.50	6.50	5.01	77.08	WSP
25	Panihati	KMDA	12.00	12.00	11.12	92.67	WSP
26	Kanchrapara	KMDA	18.00	13.92	8.73	62.72	WSP
27	Howrah	KMDA	65.00	55.57	24.00	43.19	ASP
28	Bally	KMDA	62.00	53.00	31.00	58.49	ASP+WSP
29	Baranagar	KMDA	60.00	41.10	14.00	34.06	ASP
30	Hooghly-Chinsurah	KMDA	26.50	23.00	5.08	22.09	SBR
31	Jangipur	KMDA	8.00	1.00	1.00	100.00	SBR
32	Maheshtala	KMDA	35.00	31.25	13.00	41.60	SBR
33	Garden Reach	KMC	57.00	57.00	53.68	94.18	ASP
34	Keorapukur	KMC	45.00	45.00	36.00	80.00	
35	Rania	KMC	23.00	21.00	2.00	9.52	SBR
36	Nabadwip Municipality	PHED	10.50	10.50	6.72	64.00	WSP
37	Katwa Municipality,	PHED	4.36	4.36	2.36	54.13	WSP

38	Diamond Harbour Municipality	PHED	2.03	2.03	0.20	9.85	
39	Murshidabad Municipality	PHED	1.96	1.96	0.24	12.09	WSP
40	JiagunjAzimgunjTakia	MED	0.69	0.69	0.95	68.84	OP
41	JiagunjAzimgunjTakia	MED	0.69	0.69			OP
42	Berhampore	PHED	3.70	3.70	1.78	48.11	
	Total (in MLD)		**688.0**	**599.63**	**365.35**		
Note 1: Sl. No. 31, 32 & 35 are put under Trial Run							
