National Mission for Clean Ganga/State Mission for Clean Ganga WB

Monthly Progress Report in the NGT Matter O.A.No.673 from the month of December 2025 till February 2026 for the State of West Bengal as per Reports received from various stakeholders

The Main Report

Overall status of the State:

I. Total Population: Urban Population & Rural Population: **10.09 Cr.**

(3.09 Cr. Urban population & 7 cr. Rural population)
(estimated population for 2020)
(Source: www.census2011.co.in)

II. Estimated Sewage Generation (MLD):
a. 2758 MLD (Urban area)
b. 1400 MLD (Rural area)

III. Details of Sewage Treatment Plant (Urban Area):

a. Existing no. of operational STPs including East Kolkata Wetland and Primary Treatment facilities: **59 (2080.73MLD)**

b. No. of STPs under construction **11 (178.25 MLD)**
c. No. of STPs under renovation **4 (69.90 MLD)**
d. No. of STPs under proposal/tender stage **23 (529.40 MLD)**

IV. Total Treatment Capacity (a+b+c+d) **2858.28 MLD**

- To address the sewage generation in Rural areas, Sanitation Wing of Department of P&RD, GoWB has taken a separate Programme which includes setting up of FSTPs.
- Sewage treatment capacity in Private STP is approximately 78 MLD as per data received from WBPCB.

N.B.

1. STP at Chakdah with a capacity of 15 MLD has been put under Trial Run.
2. a) *Two STPs (Garden Reach and Keorapukur) which were earlier under operational list is now currently shown in under renovation. This decision was taken in the RRC Meeting held on 30.06.2023 as the sanction received from NMCG vide F.No. Pr-12013/7/2022-TECH CONSTRUCTION NMCG dated 25.10.2022 and F.No. Pr-12013/15/2018-TECH CONSTRUCTION NMCG dated 07.09.2022, these two Projects have been shown as 'rehabilitation (renovation)'.*

b) For Garden Reach (57 MLD) and Keorapukur (45 MLD) STPs which are currently under operational list, additional augmented capacity of 8 MLD for Garden Reach and 5 MLD for Keorapukur are considered and listed under Renovation list.

3. To reduce the Faecal Coliform of River Ganga, State has been considering to set up Chlorination units at Bhatpara, Uttarpara, Kalyani, Naihati, Garulia, Panihati, Titagarh, Bandipur STPs, DPRs for which have already been sanctioned by NMCG. Draft Bid Document is under preparation stage. For Bhatpara, the Bid document is with NMCG for approval.
4. STP at Katwa with a capacity of 14 MLD is currently under Construction stage funded by NMCG.
5. State has also proposed for Setting up Chlorination unit at Bhadreswar, Baidyabati STPs from state fund which are currently in tendering stage.
6. KMC has proposed construction of a new STP of capacity 41 MLD at Hossainpur as communicated through **Annexure –III.**

Details of operational STPs in the State

EA=Executing Agency

Sl.No.	River/ Coastal Stretch	EA	Location	Existing STP Capacity (MLD)
1	Ganga	KMDA	STP Kalyani-I	11.00
2	Ganga	KMDA	STP Kalyani-II	10.00
3	Ganga	KMDA	Nabadwip	9.50
4	Ganga	KMDA	Gayeshpur	8.33
5	Ganga	KMDA	Konnagar	22.00
6	Ganga	KMDA	Baidyabati	6.00
7	Ganga	KMDA	Bhadreswar	7.60
8	Ganga	KMDA	Chandannagar, Khalisani, Chinsurah- Hooghly	18.16
9	Ganga	KMDA	Chandannagar, Khalisani, Chinsurah- Hooghly	4.54
10	Ganga	KMDA	Bansberia	0.30
11	Ganga	KMDA	Naihati	11.56
12	Ganga	KMDA	Naihati	6.50
13	Ganga	KMDA	Garulia	4.10
14	Ganga	KMDA	Titagarh	4.54
15	Ganga	KMDA	Titagarh	4.54
16	Ganga	KMDA	Bandipur (Khardah)	14.10
17	Ganga	KMDA	Panihati	12.00
18	Ganga	KMDA	Jagaddal Bhatpara New	31.00
19	Ganga	KMDA	Shyamnagar	10.00
20	Ganga	KMDA	Jagaddal Bhatpara old	9.50
21	Ganga	KMDA	Kankinara STP, Madrail, Bhatpara	10.00
22	Ganga	KMDA	Barrackpore	18.00
23	Ganga	KMDA	Barrackpore	6.00
24	Ganga	KMDA	Halisahar	16.00
25	Ganga	KMDA	Kanchrapara	18.00
26	Ganga	KMDA	Budge-Budge	9.30
27	Ganga	KMDA	Bally (Kona)- Kona, Chakpara	62.00
28	Ganga	KMDA	Howrah-Arupara	65.00
29	Ganga	KMDA	Kamarhati - Baranagar -Kamarhati, Mathkol, near Belgachia Metro Car Shed	60.00
30	Ganga	KMDA	Hooghly-Chinsurah	26.50
31	Ganga	KMDA	Jangipur	8.00
32	Ganga	KMDA	Maheshtala	35.00
33	Ganga	KMDA	Raghunathganj	5.00

Sl.No.	River/ Coastal Stretch	EA	Location	Existing STP Capacity (MLD)
34	Ganga	KMDA	North-Barrackpore	30.00
35	Ganga	KMDA	Chakdah	15.00
36	Churni	KMDA	Sreenathpur	4.00
37	Churni	KMDA	Silver Jubilee Road	2.60
38	Ganga	KMC	Keorapukur	45.00
39	Ganga	KMC	Garden Reach	57.00
40	Ganga	KMC	Rania	23.00
41	Vidyadhari	KMC	Bangur	52.00
42	Vidyadhari	KMC	Baghajatin	15.00
43	Vidyadhari	KMC	Hatisur	10.00
44	Vidyadhari	KMC	East Kolkata Wetlands	910.00
45	Ganga	PHED	Nabadwip Municipality Nadia	10.50
46	Ganga	PHED	Diamond Harbour Municipality	2.03
47	Ganga	PHED	Murshidabad Municipality	1.96
48	Ganga	PHED	Berhampore Murshidabad	3.70
49	Vidyadhari	PHED	New Town Kolkata (Action Area IIC)	31.00
50	Vidyadhari	PHED	New Town Kolkata (Action Area IIB)	14.00
51	Vidyadhari	PHED	New Town, Rajarhat Action Area- IIID	24.00
52	Dwarka	PHED	Tarapith	4.25
53	Coastal	PHED	Digha Sankarpur Development Area	6.70
54	Ganga	MED	Jiagunj-Azimgunj Takia Oxidation Pond	0.69
55	Ganga	MED	Jiagunj-Azimgunj Takia Oxidation Pond	0.69
56	Mirik Lake	MED	Mirik (STP -2; Adjacent to Aquarium Ward No: 3)	0.30
57	Vidyadhari	UDMA (SLRDC)	Kestopur	27.24
58	Vidyadhari	NKDA, PHED	DhilerBheri	150.00
59	Damodar	DMC	Durgapur City Centre	1.00
Primary Treatment			Kaljani/Karola/Mayurakshi /Shilabati/Kansi/Rupnaray an/Dwarkeswar/Jalangi Rivers	95.00
Total				**2080.73**

Details of under Construction STPs in the State

EA-Executing Agency

No.	River/ Coastal Stretch	EA	Location	Capacity of the plant in MLD	Completion Timeline
1	Ganga	KMDA	Baharampore	3.50	EOT Proposed upto March, 2026
2	Ganga	KMDA	Santragachi Jheel	1.50	EOT Proposed upto Aug, 2026
3	Ganga	KMDA	Khardah	8.15	March, 2027 (Including Trial Run)
4	Ganga	KMDA	Krishnanagar	14.00	December, 2026 (Including Trial Run)
5	Ganga	KMDA	Katwa	14.00	September, 2027 (Including Trial Run)
6	Vidyadhari	KMDA	South Dum Dum	27.00	March, 2027 (Including Trial Run)
7	Ganga	KMC	Joka	45.00	Aug, 2026
8	Ganga	KMC	M.G. Road	40.00	Aug, 2026
9	Ganga	KMC	Bansdroni (TNP)	11.60	July, 2028 (Including Trial Run) Under Adi Ganga Project
10	Ganga	KMC	Golf Green (TNP)	3.50	
11	Ganga	KMC	Birji Road (TNP)	10.00	
	Total			**178.25**	

Details of STPs in the State under Renovation

EA- Executing Agency

SL. No.	River/ Coastal Stretch	EA	Location	Existing STP Capacity (MLD)	Compliance Status of STP
1	Mahananda	KMDA	Mahananda Left Bank, Siliguri	24.00	Under Rejuvenation
2	Mahananda	KMDA	Jorapani & Fuleswari River, Siliguri	32.00	Under Rejuvenation
3	Mirik Lake	MED	Mirik (STP - 1; Krishnagar Ward No: 5)	0.60	Under Rejuvenation
4	Mirik Lake	MED	Mirik (STP - 3; Home Dara Ward No: 3)	0.30	Under Rejuvenation
Additional capacity of Garden Reach STP				8.00	Work started, New construction with augmented capacity of 65 MLD. Completion Date: October, 2026 (including Trial Run)
Augmentation of Keorapukur STP				5.00	Augmented capacity of 50 MLD. (Presently under Renovation stage) Completion Date: December, 2026
Total				**69.90**	

Details of STPs under Tendering/proposal stage in the State

EA-Executing Agency

SL. No.	River/ Coastal Stretch	EA	Location	Capacity of the STP proposed in MLD
1.	Ganga	KMDA	Murshidabad	5.00 (Under Tendering Stage)
2.	Ganga	KMDA	Uluberia	11.00
3.	Ganga	KMDA	Kestopur	41.00
4.	Ganga	KMDA	Santipur	18.10
5.	Ganga	KMDA	Champdani	30.00
6.	Ganga	KMDA	Serampore	115.00
7.	Ganga	KMDA	North-Barrackpore	12.00
8.	Ganga	MED	Diamond-Harbour	10.40
9.	Ganga	MED	Jiaganj - Azimganj	1.50
10.	Ganga	KMDA	Kalyani added area	3.00 (Under Tendering Stage)
11.	Churni	KMDA	Jianagar	5.20
12.	Damodar& Barakar	MED	Durgapur/Asansol	4.00
13.	Mahananda	KMDA	Right Bank	27.00 (Under Tendering Stage)
14.	Mahananda	KMDA	Left Bank	22.00 (Under Tendering Stage)
15.	Vidyadhari	KMDA	Baranagar	8.70 (Under Tendering Stage)
16.	Vidyadhari	KMDA	North Dumdum	33.00 (Under Tendering Stage)
17.	Vidyadhari	BMC	Bidhannagar	7.50 (Under Tendering Stage)
18.	Ganga	KMC	Badartala	25.00
19.	Ganga	KMC	Bhanga Khal, Garden Reach	35.00
20.	Ganga	KMC	New Keorapukur	25.00
21.	Ganga	KMC	Hossianpur STP	41.00
22.	Ganga	KMC	Strand Road	23.00
23.	Non-Ganga	KMC	New Baghajatin	26.00
Total			**23 STPs**	**529.40**

IV. Details of Industrial Pollution:

No. of industries in the State (Red = 4297, Orange = 14611) =18908
No. of water polluting industries in the State =456
Effluent generation from industries =1360.87 MLD
No. of industries having ETPs =456
Total treatment capacity of ETPs =1360.87 MLD
No. and capacity of existing CETP (8modules each of 5 MLD) =40 MLD
All industries in the Calcutta Leather complex are connected to CETP

V. Bio-medical Waste Management:

No. of Hospitals and Health Care Facilities =9927
Total Bio-medical generation =43120.87 kg / day
Status of Treatment Facility / CBMWTF = 9 CBMWTF are operating
Treatment capacity = 2,11,000 bed

All Biomedical wastes generated in the state are treated at the Nine (9) Common BMW Treatment, Storage & Disposal Facilities. Setting up of few more CBMWTSDF are in progress.

VI. Hazardous Waste Management:

No. of Industries generating Hazardous waste =843
Total Hazardous Waste generation =244005.0 MTA
Treatment Capacity of all CHTSDFs
Land fill capacity =2,20,000 MTPA
Land fill after treatment =1,20,000 MTPA
Incineration =14,400 MTPA
Average quantity of hazardous Waste reaching TSDF = 52404.00 MT

Two Nos CHWTSDF at Haldia, East Medinipur and at Saltora, Bankura are in operation.

VII. Details of Nodal Officer appointed by Chief Secretary in the State /UT:

- Principal Secretary, Department of Environment, Govt. of West Bengal.

VIII. Ground water regulation:

River	Groundwater regulation
Vidyadhari	• Groundwater extraction is regulated according to West Bengal Ground Water Resources (Management, Control and Regulation) Act, 2005 by SWID, GoWB. • Water meter without telemetry system is installed at industrial tube well permitted by SWID. • Groundwater Resources Estimation and Assessment (2016-2017) is done as per GEC'97 guidelines. • Groundwater level (GWL) monitoring is done periodically four times a year (Jan, April, Aug & Nov). A few manual GW Level Monitoring stations is converted to Real-Time GW Level Monitoring stations by installation of Digital Water Level Recorder (DWLR). GWL data for the month of Jan, April, Aug'20, Nov'20 & Jan'22 has been generated. GWL monitoring for the month of April'22 is continued.
Mathabhanga Dwarka	• Groundwater extraction is regulated according to West Bengal Ground Water Resources (Management, Control and Regulation) Act, 2005 by SWID, GoWB. • Water meter without telemetry system is installed at industrial tube well permitted by SWID. • Groundwater Resources Estimation and Assessment (2016-2017) is done as per GEC'97 guidelines. • Groundwater level (GWL) monitoring is done periodically four times a year (Jan, April, Aug & Nov). A few manual GW Level Monitoring stations is converted to Real-Time GW Level Monitoring stations by installation of Digital Water Level Recorder (DWLR). Post-Monsoon (Nov'22) GW level data is generated. All are "safe" categorized block along polluted stretches of Dwarka & Mathabhanga River except the following Block. • **Dwarka River Stretch:** *Semi-Critical*- Rampurhat-II (Birbhum Dist) • **Mathabhanga river stretch:** *Semi-Critical*- Deganga (North 24 Parganas dist.) • Periodic groundwater sampling for its Physio-chemical tests is done twice a year (April & Nov).
Damodar	• Water meter without telemetry system is installed at industrial tube well permitted by SWID. • Groundwater Resources Estimation and Assessment is done as per GEC'97guidelines.
Barakar	• Groundwater level (GWL) monitoring is done periodically four times a year (Jan, April, Aug & Nov). GWL database for Aug'20 (monsoon) has been generated. • All are "safe" categorized blocks along polluted stretch of Damodar and Barakar river. • Groundwater sampling for its Physio-chemical tests is done twice a year (April & Nov).Post-Monsoon (Nov'22) GW level data is

River	Groundwater regulation
	generated.
Ganga	Ground water regulation: • Installation of Water Meter with telemetry system at industrial Tube Wells for monitoring of real-time GW withdrawal is in progress. • Implementation of Real-Time GW Level monitoring system is in progress. • Ground water monitoring: Post-Monsoon (Nov'22) GW level data against 136 GW monitoring stations under the blocks along polluted stretch of River Ganga is generated. GW Monitoring Stations (136)= 92 (Manual) + 44 (Real-Time) Post-Monsoon (Nov'22) GW sampling from 52 GW monitoring stations under the blocks along polluted stretch of River Ganga is completed
Churni	Groundwater regulation: • Water meter without telemetry system is installed industrial tube-well. • Physio-chemical quality of groundwater samples collected from GW monitoring wells during pre-monsoon and post-monsoon period is tested every year. Groundwater monitoring: Post-Monsoon (Nov'21) GW level data against 136 GW monitoring stations under the blocks along polluted stretch of River Churni is generated. GW Monitoring Stations (52) = 42 (Manual) + 10 (Real-Time) Post-Monsoon (Nov'22) GW sampling from 52 GW monitoring stations under the blocks along polluted stretch of River Churni is completed.
Kansi Mayurakshi Rupnarayan Jalongi	• Groundwater extraction is regulated according to West Bengal Ground Water Resources (Management, Control and Regulation) Act, 2005 by SWID, GoWB. • Water meter without telemetry system is installed at industrial tube well permitted by SWID. • Groundwater Resources Estimation and Assessment (2016-2017) is done as per GEC'97 guidelines. • Groundwater level (GWL) monitoring is done periodically four times a year (Jan, April, Aug & Nov). A few manual GW Level Monitoring stations is converted to Real-Time GW Level Monitoring stations by installation of Digital Water Level Recorder (DWLR). Post-Monsoon (Nov'22) GW level data is generated. • All are "safe" categorized block along polluted stretches of Kansi, Mayurakshi, Rupnarayan, Jalangi River except the following Blocks. ✓ **Kansi River Stretch:** *Semi-Critical*- Keshpur, Debra (Paschim Medinipur Dist) *Critical*- Panshkura (Purba Medinipur Dist) ✓ **Mayurakshi River Stretch:** *Semi-Critical*- Suti-I (Murshidabad Dist), Labhpur (Birbhum Dist) ✓ **Jalangi River Stretch:**

River	Groundwater regulation
	Semi-Critical- Berhampur, Nowda (Murshidabad Dist), Tehatta-II, Chapra (Nadia Dist) *Critical*- Domkal (Murshidabad Dist), Karimpur-II, Tehatta-I, Nakashipara, Krishnagar-II, Krishnagar-I (Nadia Dist) • Groundwater sampling for its Physio-chemical tests is done twice a year (April & Nov). Post-Monsoon(Nov'22) GW sampling is completed.
Silabai Dwarekeswar Kaljani Karola	• Control and Regulation) Act, 2005 by SWID, GoWB. • Water meter without telemetry system is installed at industrial tube well permitted by SWID. • Groundwater Resources Estimation and Assessment (2016-2017) is done as per GEC'97 guidelines. • Groundwater level (GWL) monitoring is done periodically four times a year (Jan, April, Aug & Nov). A few manual GW Level Monitoring stations is converted to Real-Time GW Level Monitoring stations by installation of Digital Water Level Recorder (DWLR). Post-Monsoon (Nov'22) GW level data is generated. All are "safe" categorized block along polluted stretches of Silabati, Darakeswar, Kaljani and Karala River. • Groundwater sampling for its Physio-chemical tests is done twice a year (April &Nov). Post-Monsoon(Nov'22) GW sampling is completed.
Mahananda Teesta	Groundwater regulation: • Groundwater extraction is regulated according to West Bengal Ground Water Resources (Management, Control and Regulation) Act, 2005. • Water meter without telemetry system is installed at industrial tube well permitted by SWID. • Groundwater Resources Estimation and Assessment (2016-2017) is done as per GEC'97 guidelines. • Groundwater level (GWL) monitoring is done periodically four times a year (Jan, April, Aug & Nov). A few manual GW Level Monitoring stations is converted to Real-Time GW Level Monitoring stations by installation of Digital Water Level Recorder (DWLR). Post-Monsoon (Nov'22) GW level data is generated. All are "safe" categorized blocks along polluted stretch of Teesta and Mahananda river. Groundwater sampling for its Physio-chemical tests is done twice a year (April &Nov).

IX. Good irrigation practices being adopted by the State:

River	Stretch of the river	Good irrigation practices
Dwarka	Tarapith to SadhakBamdeb Ghat	A command area of 6735 ha in Rampurhat-II block is irrigated by the canal system of Mayurakshi barrage project belonging to I&W Department. At present a major canal renovation work of the Mayurakshi Reservoir Project for a total length of 67 km. is going on since 2018-19 which inter alia includes the canal system of length of 19 km in Rampurhat-II block.

Ganga	Tribeni to Diamond Harbour	By diverting tidal water through the sluices on the bank of the river irrigation is provided at **(a)** Mograhat-I & II, Mandirbazar, Diamond Harbour-I & II through Diamond Harbour Canal system (1500 ha), at Budge Budge-I & II blocks, Bishnupur-I & II blocks through Charial Canal (1580 ha) Uluberia, Shyampur, Bagnan-I and Bagnan-II blocks. Through Rajapur Canal, Purana canal, Chandanpara canal and Nakal canal (1500 ha). Repair of sluices and canal system are taken up as and when required.
Kansi	Midnapore to Ramnagar	Irrigation is provided at Kharagpur-II and Debra blocks through Medinipur Main Canal System originating from Medinipur Anicut. This canal system along with Medinipur structure has been rehabilitated recently which also includes the canal system in Medinipur, Kharagpur- I and Debra blocks. As a result irrigation has been started in these areas after a decade.
Dwarekeswar	Along Bankura	Irrigation is provided in Onda block from the canal system of Kangsabati Reservoir Project. Moreover there are four medium and minor irrigation schemes in Bankura-I and Onda blocks namely Niada (405 ha), Birai (2700 ha), Horajore (80 ha) and Abarda (80 ha) through which 3265 ha area is irrigated. The canal system of the aforesaid schemes and the regulating structure has undergone major rehabilitation during last two years.
Kaljani	Bitala to Alipurduar	Irrigation is provided at 1000 ha of area in Kalchini block through 2 minor surface irrigation schemes on streams out falling into Kaljani river.
Karola	Jalpaiguri to ThakurerKamat	A command area of 24385 ha in Rajganj block is irrigated through the Canal system of Teesta Barrage Project.
Mayurakshi	Suri to Durgapur	A command area of 1196 ha in Suri-I block is irrigated through the canal system of Mayurakshi Reservoir Project.
Rupnarayan	Kolaghat to Benapur	Areas of different blocks are irrigated from tidal water through the sluice and canals belonging to I& W Department like in Amta-II (4807 ha), Sahid Matangini (3765 ha), Bagnan-I (2024 ha), Bagnan-II (1518 ha) and Shyampur-I & II (8805 ha).
Teesta	Siliguri to Paharpur	Command areas of 24385 ha in Rajganj block, 5080 ha in Mal block, 400 ha in Maynaguri block and 14760 ha in Jalpaiguri Sadar block are irrigated through the canal system of Teesta Barrage Project.

X. Rain Water Harvesting:

River	Roof Top Rainwater Harvesting and Reuse and / or Artificial Recharge to Groundwater
Damodar	1 in Kanksa Block is in progress.
Barakar	

Ganga	1)Barrackpur-II Block- 2 (2 completed) 2) KMC- 10 (existing) & 3 (3 completed in 2020-2021 3)Diamond Harbour-I Block- 1 (existing) 4)Diamond Harbour-II Block- 1 (existing)
Churni	Hanskhali- 5 (existing)

In Ganga and Churni 12 Rooftop Rain Water Harvesting infrastructure have been constructed.

XI. Department of Environment has received a Report on demarcation of Flood Plain Zone of river Ganga which has been prepared by the Department of Geography, University of Calcutta. The final Report after considering the observation from different Departments is under preparation.

River	Demarcation of flood plain, removal of illegal encroachments from embankments and protection and management of flood
Vidyadhari	There is no illegal encroachment on the river embankments. Total 2.60 km bank protection works amounting Rs.14.40Crore will be taken up at right bank of river Vidhyadhari during 2020-21.
Mahananda	There is no embankment on either side of the river in this stretch. Bank protection works are taken up as and when required to protect the adjoining areas. 1.40 km bank protection work amounting Rs. 3.58 Crore is already completed by which 18900 people under 112 Ha areas may be benefitted. 3.00 km bank protection work amounting Rs.7.64Crore will be taken up during 2020-21, by which 32000 people under 465 Ha areas may be benefitted.
Churni	There is no embankment on either side of the river in this stretch. Bank protection works are taken up as and when required to protect the adjoining areas. 0.5 km bank protection work of Rs. 1.88 Crore will be taken up during 2020-21, by which 2000 people in 98 Ha of areas may be benefitted.
Dwarka	There is no embankment on either side of the river in this stretch. For this stretch, Bank protection works are being taken by Tarapith-Rampurhat Development Authority (TRDA).
Ganga	There is no illegal encroachment on the river embankments. In left bank, 0.135 km bank protection work of Rs. 2.61 Crore is under running and 1.045 km bank protection work of Rs.11.17Crore will be taken during 2020-21. In right bank, 0.900 km bank protection work of Rs. 6.21 Crore will be executed during 2020-21.
Damodar	There is no embankment on either side of the river in this stretch. Bank protection works are taken up as and when required to protect the adjoining areas. At present there is no such requirement of taking up anti erosion work in this stretch of river.
Jalangi	There is no embankment on either side of the river in this stretch. Bank protection works are taken up as and when required to protect the adjoining areas. 1.05 km bank protection work of Rs. 3.15 Crore is under progress, by which 3500 people under 205 Ha

River	Demarcation of flood plain, removal of illegal encroachments from embankments and protection and management of flood
	areas may be benefitted.
Kansi	There is no illegal encroachment on the river embankments. 1.5 km bank protection work of Rs. 3.62 Crore is already completed by which 13800 people under 700Ha areas may be benefitted.
Mathabhanga	There is no embankment on either side of the river in this stretch. Bank protection works are taken up as and when required to protect the adjoining areas. At present, there is no such vulnerable zone noticed in this stretch. However, protection work will be taken up as & when required.
Barakar	There is no embankment on either side of the river in this stretch. Bank protection works are taken up as and when required to protect the adjoining areas. At present, there is no such vulnerable zone noticed in this stretch. However, protection work will be taken up as & when required.
Dwarekeswar	There is no embankment on either side of the river in this stretch. Bank protection works are taken up as and when required to protect the adjoining areas. A bank protection work of length 300 m of amounting Rs. 0.87croreis already executed in 2020-21 by which 790 people under 1.67 Ha area will be benefitted.
Kaljani	There is no illegal encroachment on the river embankments. 2.92 km bank protection work of Rs. 4.49Crore is already completed by which 5900 people under 96 Ha areas may be benefitted. Further, 1.01 km bank protection work of Rs. 1.52 Crore will be taken during 2020-21, by which 3000 people under 74 Ha areas may be benefitted.
Karola	There is no illegal encroachment on the river embankments. 2.03 km bank protection work of Rs. 3.78 Crore is already completed by which 9000 people under 102 Ha areas may be benefitted.
Mayurakshi	There is no illegal encroachment on the river embankments. No such work envisaged for this stretch of river Mayurakhshi. There is no such vulnerable zone noticed in both sides of the river stretch. So at present no future plan is there for execution of protection work.
Rupnarayan	The Department has taken appropriate measure to remove illegal encroachment on the river embankments. A1.132 km bank protection work of Rs. 3.68 Crore is already completed, by which 4600 people under 158 Ha areas may be benefitted. Further, 4.50 km bank protection work of Rs. 12.96 Crore is also completed during 2020-21.
Teesta	There is no illegal encroachment on the river embankments. 10.61 km bank protection work of Rs. 31.41 Crore is under running, by which 42000 people under 1580 Ha areas may be benefitted.

XII. Maintaining minimum e-flow of river:

River	Maintaining minimum environmental flow of river
Vidyadhari	The river is a perennial river. There is no regulating structure exists on this river for regulation of river flow. The environmental flow is naturally maintained from the river flow which is a combination of surface flow and base flow.
Mahananda	Average flow about 15.00 cumec is being released from Mahananda Barrage throughout the day during lean season since last three year, for maintaining minimum environmental flow of river.
Churni	The river is non-perennial. There is no regulating structure exists on this river for regulation of river flow. The environmental flow is naturally maintained from the river flow which is a combination of surface flow and base flow.
Dwarka	
Janangi	
Mathabhanga	
Kaljani	
Dwarekeswar	
Karola	
Silabati	
Ganga	The river is a perennial river. The environmental flow is maintained through the release from the Farakka Barrage throughout the year.
Damodar	There is no regulating structure in West Bengal. However, there is a dam in Panchet over Damodar River in Jharkhand under the control of DVC, which regulates the flow through this river. This release from the Dam, along with the contribution from the uncontrolled catchment of the d / s of the dam, maintains environmental flow in the river.
Kansi	The discharge through Kansabati river is regulated from the major dam at Mukutmanipur, Bankura. The regulated release from dam, along with the contribution from the uncontrolled catchment of the d / s of the dam, maintains environmental flow in the river.
Barakar	There is no regulating structure in West Bengal. However, there is a dam in Mithon over Barakar river in Jharkhand under the control of DVC, which regulates the flow through this river. This Release from the Dam, along with the contribution from the uncontrolled catchment of the d / s of the dam, maintains environmental flow in the river.
Mayurakshi	There is no regulating structure in West Bengal. However, there is a dam in Massanjore over Mayurakashi river, which regulates the flow through this river. This release from the Dam, along with the contribution from the uncontrolled catchment of the d / s of the

River	Maintaining minimum environmental flow of river
	dam, maintains environmental flow in the river.
Rupnarayan	The river is perennial river. There is no regulating structure exists on this river for regulation of river flow. The environmental flow is naturally maintained from the river flow which is a combination of surface flow and base flow.
Teesta	Depending on water availability, down-stream release is regulated.

XIII. Plantation activities along the rivers:

River	Plantation activity planned	Status of plantation
Vidyadhari	0.275 ha	Advance (Nursery work): completed.
Mahananda	29.8 ha	
Churni	7.265 ha	
Ganga	6 ha	
Damodar	20 ha	
Jalongi	8.49 ha	
Kansi	10 ha	
Barakar	50 ha	
Dwarekeswar	40.6 ha	
Rupnarayan	20 ha	
Karola	30 ha	

Total 107.1 km of Vetiver plantation has been done in the Ganga and Churni adjoining districts.

XIV. Development of Bio-Diversity Park:

River	Number of biodiversity parks	Status of the biodiversity parks
Vidyadhari	4 nos. (Haroa: 3 nos; Minakhan: 1 nos)	Ongoing projects
Churni	1 no.	Ongoing project
Jalongi	3 nos.	Ongoing projects
Kansi	6 nos. (Chandrakona II : 2 nos.; Daspur I: 1 no.; Kharagpur I: 1 no.; Midnapore: 1 no.; Sabang: 1 no.	Ongoing projects
Ganga	3 nos. (Budge Budge II: 1 no.; Diamond I: 1 no.; Diamond II: 1	Ongoing projects

	no.)	
Dwarekeswar	2 nos. (Bankura I: 1 no.; Onda I: 1 no.)	Ongoing projects
Mahananda	2 nos. (Phansidewa: 1 no.; Matigara: 1 no.)	Ongoing projects
Rupnarayan	3 nos. (Baidyanathpur: 1 no.; Orphuli: 1 no.; Antila: 1 no.)	Ongoing projects
Mayurakshi	Plan of 18 ha biodiversity park	

Total 18 bio-diversity parks have been set up.

XV. Reuse of Treated Water:

GoWB has notified a policy on Re-use of Treated Waste Water on 30th June, 2020.

- State is considering to update the policy framed on 30.06.2020 aligning with the National Framework on safe reuse of treated waste water (released by NMCG in November 2022).

Use of treated Sewage Water at Garden Reach -

- KMC and CESC are exploring the possibility of the re-use of treated waste water from Garden Reach STP in nearby Power plant.

Use of treated Sewage Water at Maheshtala-

- Concessionaire of 35 MLD at Maheshtala has been requested to prepare and submit a Reuse plan of Treated Waste Water to Budge Budge thermal power plant. They are preparing the feasibility of the plan.

Use of treated Sewage Water at DVC (Durgapur) –

- Treated effluent is planned to be re-used in DVC after completion and commissioning of upcoming Asansol and Durgapur STP project.

XVI. Status of Preparation of Action Plan by the 13 Coastal States: Action Plan for Digha Coastal town has been prepared and it is under discussion.

XVII. Regulation of Mining Activities in the State /UT:
State Environmental Impact Assessment Authority-West Bengal has notified a policy on Environmental Clearance on Mining projects.

XVIII. Action against identified polluters, law violators and officers responsible for failure for vigorous monitoring:

1. West Bengal River Rejuvenation Committee is holding meeting regularly to examine the progress of work.
2. State Environmental Monitoring Committee is holding meetings to assess the activities of all NGT cases.
3. Liquid Waste Monitoring Committee has been constituted by the UD&MA Dept. GoWB and meetings are being held fortnightly.
4. A Task Force for Solid Waste Management has been constituted by the UD&MA Dept., GoWB and the Task Force is regularly reviewing the progress of activities related to Solid Waste Management & Legacy Waste Management across the State.

List of Good Works alongwith Monitoring and Supervision of Pollution Abatement Measures taken in Polluted River Stretches

- **Improvement in Water Quality:** BOD level for the entire stretch of Ganga is below 3 mg/l. The BOD has drops significantly from 12mg/l (in 2018) to 2.95 mg/l (Presently).

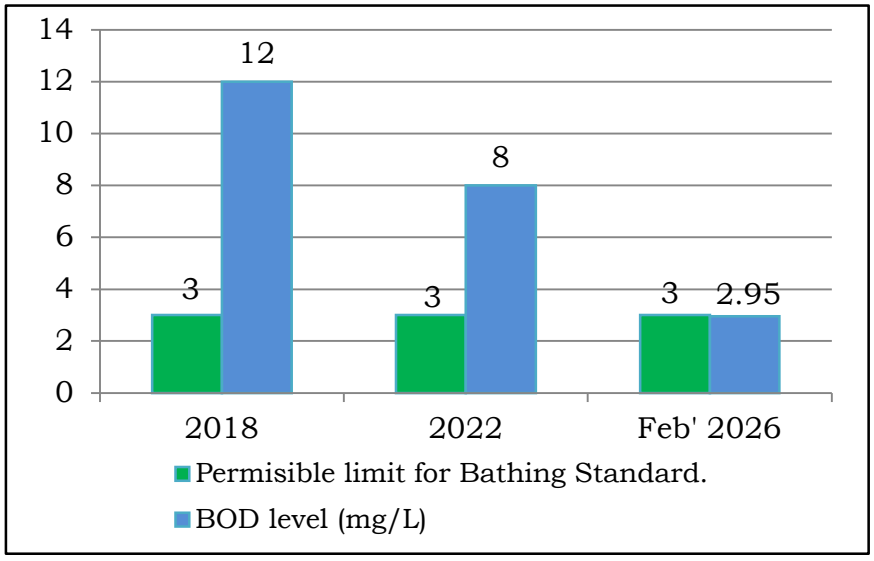

Comparative Analysis of BOD in River Ganga

As per the latest CPCB report of 2025, Polluted River Stretches came down from 13 to 11, with de-listing of 6 river stretches and addition of 4 river stretches (Karola, Silabati, Tarapith, Jaldhaka).

- **Dolphin sighting:** Improved water quality in River Ganga has resulted in increased sighting of Gangetic River Dolphins. This has been reported by NMCG vide the following communication in social media,

  Namami Gange - They're not just sightings. They're... | Facebook

  Namami Gange - Over the last few months, something quietly... | Facebook

- **STP at Chakdah has been put under Trial Run. It will enhance a total capacity of 15 MLD.**

- **An Electric Crematorium at Kalyani has been put on trial run on 10th February 2026.**

Co Treatment of Sewage and Septage

- Presently, Septage and Sewage is co-treated in operational STPs of Gayeshpur, Nabadwip, Barrackpore, Budge Budge, Halisahar, Chandannagar, Chinsurah, Naihati, Kalyani, Bhatpara, Panihati & Howrah ULBs.

Total Septage co-treated upto 28.02.2026 in the functional STPs by ULBs as below:

Sl. No	Name of ULB	Co-Treated Septage (KL)
1	Gayeshpur	132.00
2	Nabadwip	779.00
3	Halisahar	596.20
4	Budge Budge	1023.60
5	Barrackpore	2870.35
6	Chandannagar & Chinsurah	7175.75
7	Naihati	2802.00
8	Kalyani	2967.00
9	Bhatpara	2723.20
10	Panihati	3012.90
11	Howrah	244.00
	Total Capacity (KL)	**24326.00**

- **Total Amount of Septage emptied up to November 2025 - 20957.05 KL**
- **Incremental progress of co-Treatment from the submission of last OA 673 (for the period from Sept 2025 to Nov 2025) is 3368.95 KL.**

► The Pilot FSTP Projects at Siliguri and Kharagpur (on the reclaimed land of Legacy Waste Dumpsite); works are in progress. Both of which are proposed to be completed by May 2026.

► Regional Waste Management Centre (RWMC) at Baidyabati with total capacity of 125 KLD has been rejuvenated by KMDA for treatment of Faecal Sludge of nearby 6 Municipal Towns (Uttarpara-Kotrung, Konnagar, Rishra, Serampore, Champdany & Baidyabati).

District Ganga Committee and Monitoring Mechanism

► Ganga District Performance Monitoring System (GDPMS), a dedicated portal for uploading Minutes of the Meeting (MoM) by District Ganga Committees (DGCs) which has been developed by NMCG to capture DGC related activities across each DGC and provides an interactive dashboard to review activities of all DGCs by NMCG. 2 numbers of MoMs have been uploaded in this portal during December, 2025 to February, 2026.

► As per mandate of the Hon'ble NGT, Online Continuous Effluent Monitoring System (OCEMS) must be installed at the all functional STPs in Ganga river basin areas. In this connection, installation & integration of OCEMS for 30 number STPs have been completed and connected to the Ganga pulse portal of NMCG for Online Effluent Management. The web link of Ganga pulse is in public domain and the link is **https://www.gangapulse.in/public/**

► NMCG has launched a dedicated project to install Closed-Circuit Television cameras at STPs for real-time visual monitoring. This will

support functional monitoring and enhance transparency and accountability. In view of this, installation of CCTV cameras at inlet and outlet points and one pole-mounted rotating has been done in 9 STP sites namely Bhatpara (31 MLD), Bhatpara (10 MLD), Gayeshpur (8.33 MLD), Halisahar (16 MLD), Budge Budge (9.3 MLD), Nabadwip (9.5 MLD), Bally (62 MLD), Howrah (65 MLD) and Baranagar (60 MLD) STP sites.

Reuse of Treated Waste Water

- West Bengal is using the treated water extensively in Agricultural activities, Pisciculture and Gardening at different locations including EKW, Durgapur, Nabadwip, Bandipur, Konnagar and Khardah.
- The draft policy of Safe Reuse of Treated Wastewater is ready and will be webhosted for comments and feedback.

IEC Campaigns

- SMCG WB is setting up stalls in different Melas and Ghats, various types of events for mass awareness towards pollution abatement and also showcasing the use of treated water for gardening, agricultural activities and Pisciculture.
- SMCG WB is arranging Education visit to functional STPs for school & college students on a regular basis.

PHOTO GALLERY

Communication and Public Outreach Activities from December, 2025 to February, 2026 undertaken by the SMCG- WB

Educational Visit of Students at STPs

Hooghly

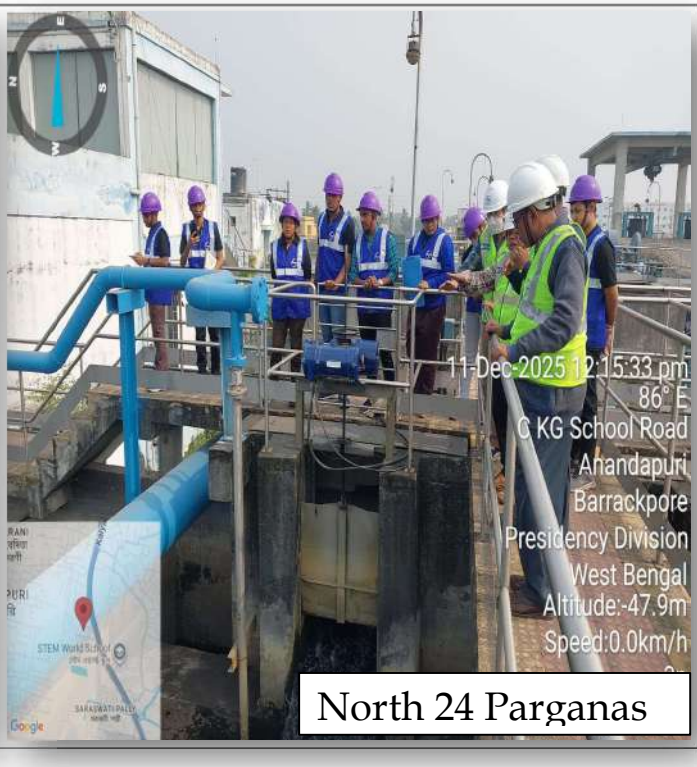

North 24 Parganas

Purba Bardhaman

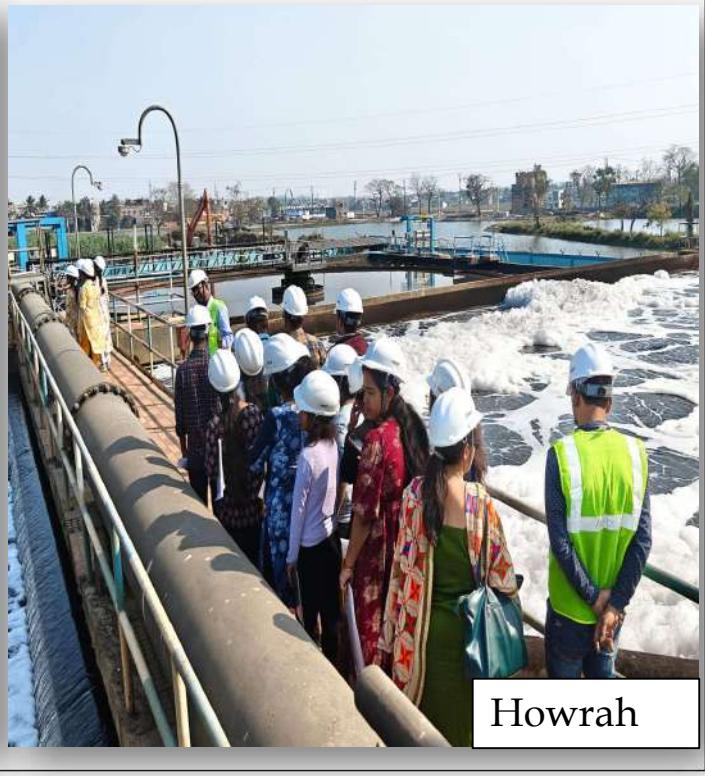

Howrah

Mass Awareness Exhibition (Stall in Fair)

49th International Kolkata Book Fair, 2026, Saltlake

Rabindra Sarobar, Kolkata

Gangasagar Mela, South 24 Parganas

Tribeni Kumbha Mela, Hooghly

Behavioural Change Communication Activities i.e. Street Drama regarding River Pollution Abatement

Rabindra Sarobar, Kolkata

Malda

North 24 Parganas

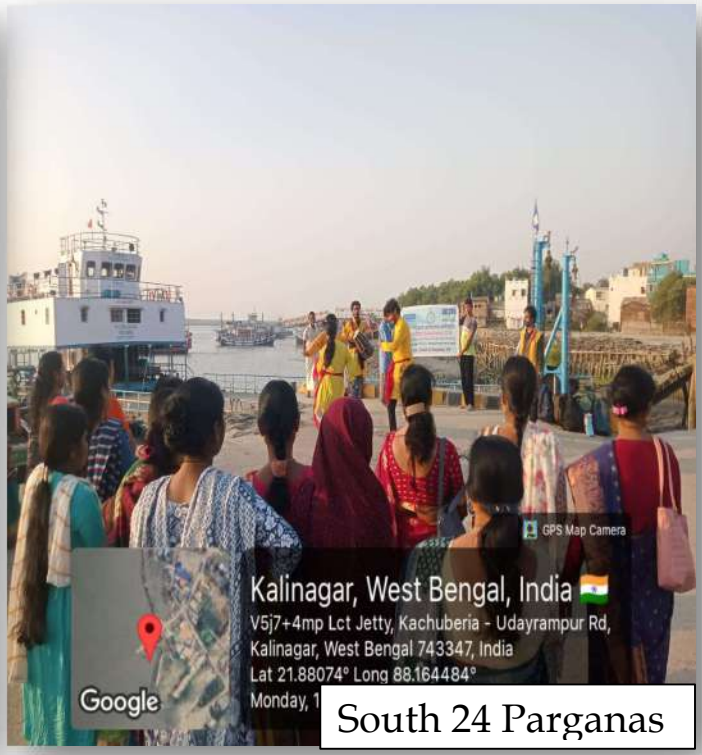

South 24 Parganas

Graffiti (Wall Painting) in Ganga Ghats, STPs and Other strategic locations

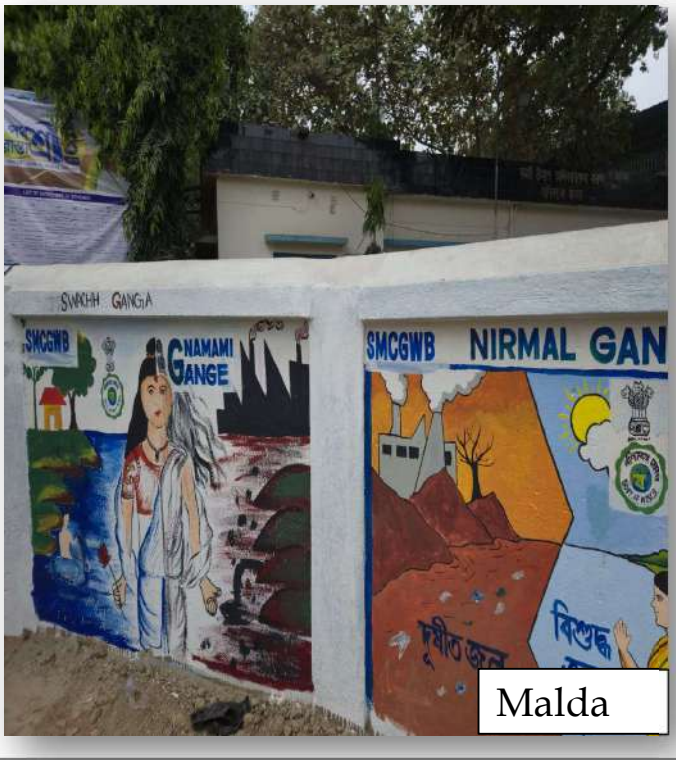

Malda

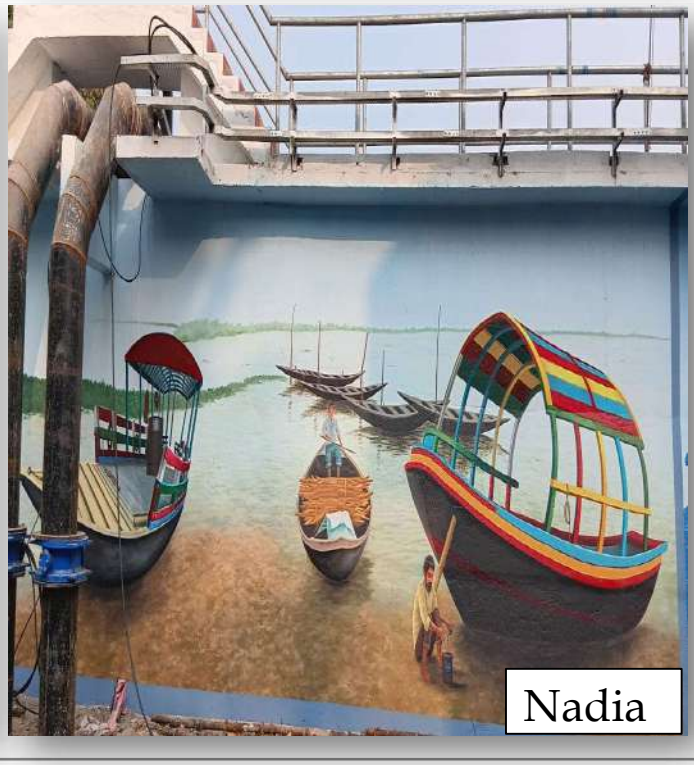

Nadia

South 24 Parganas

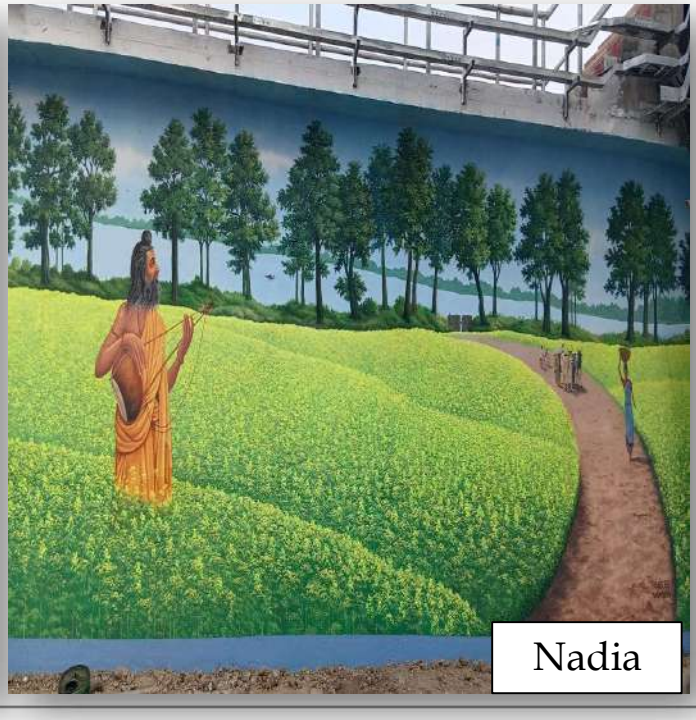

Nadia

List of Annexures

Annexure-A: Water Quality Report for the Month of February 2026, WBPCB
Annexure-B: Site Inspection Report, KMDA

Annexure-I: Report from P&RD
Annexure-II: Report from SUDA
Annexure III: Report from KMC

Status report of SLWM on Polluted River Stretch GPs for the month of Feb, 2026 (O.A. 673/2018)

Sl. No.	Name of the Districts	Total No. of Blocks	Total No. of GPs	Solid Waste Management Units	Grey Water Management	
					No. of Soak pit/ Leach pit	No. of Filter Chamber
1	Alipurduar	3	9	9	1,614	0
2	Bankura	2	10	10	873	10
3	Birbhum	7	25	25	2,822	258
4	Hooghly	1	2	2	7	19
s5	Howrah	9	49	43	4,339	2,971
6	Jalpaiguri	4	21	21	5,698	0
7	Paschim Medinipur	11	28	24	4,685	7
8	Mursidabad	2	2	2	471	14
9	Nadia	12	48	46	8,720	581
10	North 24 PGS	2	7	7	1,658	33
11	Siliguri Mahakuma Parishad	2	7	7	1,453	30
12	South 24 PGS	5	13	13	1,652	276
Total		**60**	**221**	**210**	**33,992**	**4,199**

	Status of per day Collection & Transportation of Fresh Waste of 128 ULBs of West Bengal up to February, 2026													
Sl No	**District**	**ULB**	**No. of ward**	**Population (Census 2011)**	**Per day Generation of fresh waste (TPD)**	**Door to door collection of fresh waste in no. of wards**		**Collection of segregated fresh waste in no. of wards**		**Quantity of fresh waste being collected & transported per day (TPD)**				**Tentative timeline for ensuring 100% segregation**
						Full	**Partial**	**Full**	**Partial**	**Wet Waste**	**Dry Waste**	**Mixed Waste**	**Total**	
1	Bankura	Bankura	24	1,37,386	**40**	24	0	16	8	15.95	5.45	18.60	40	Sept, 26
2	Bankura	Bishnupur	19	67,783	**14**	11	8	8	11	5.00	3.00	4.00	12	July, 26
3	Bankura	Sonamukhi	15	34,228	**9**	15	0	6	9	3.10	1.80	4.10	9	July, 26
4	Paschim Burdwan	Asansol MC	106	11,56,387	**566**	84	22	27	79	200.00	130.00	211.00	541	May, 26
5	Purba Burdwan	Barddhaman	35	3,14,638	**98**	35	0	23	12	44.44	42.00	11.56	98	Sept, 26
6	Purba Burdwan	Dainhat	14	24,397	**7**	14	0	13	1	4.10	2.77	0.13	7	July, 26
7	Paschim Burdwan	Durgapur MC	43	5,66,517	**244**	43	0	20	23	101.94	68.22	73.84	244	Sept, 26
8	Purba Burdwan	Gushkara	16	35,374	**9**	16	0	15	1	4.00	3.50	1.50	9	July, 26
9	Purba Burdwan	Kalna	18	56,722	**15**	18	0	18	0	7.00	5.64	2.30	15	Aug, 26
10	Purba Burdwan	Katwa	20	81,615	**26**	20	0	16	4	12.33	6.77	6.90	26	Sept, 26
11	Purba Burdwan	Memari	16	41,455	**11**	16	0	16	0	7.00	4.00	0.00	11	Achieved
12	Birbhum	Bolpur	22	80,210	**31**	22	0	10	12	14.00	9.00	8.00	31	July, 26
13	Birbhum	Dubrajpur	16	38,041	**10**	16	0	16	0	5.80	3.56	0.64	10	July, 26
14	Birbhum	Nalhati	16	41,244	**9**	14	2	14	2	3.60	1.90	2.50	8	July, 26
15	Birbhum	Rampurhat	18	57,833	**15**	18	0	12	6	5.00	3.00	7.00	15	July, 26
16	Birbhum	Sainthia	16	44608	**12**	16	0	10	6	6.31	3.16	2.53	12	July, 26
17	Birbhum	Suri	21	90,314	**26**	21	0	8	13	10.50	5.00	10.50	26	July, 26
18	Cooch Behar	Cooch Behar	20	77935	**20**	20	0	2	18	6.50	2.00	11.50	20	July, 26
19	Cooch Behar	Dinhata	16	36,124	**9**	16	0	16	0	6.00	2.50	0.50	9	Achieved
20	Cooch Behar	Haldibari	11	14,404	**4**	11	0	11	0	2.30	1.40	0.30	4	Aug, 26
21	Cooch Behar	Mathabhanga	12	23,895	**9**	8	4	8	4	5.00	3.00	1.00	9	July, 26
22	Cooch Behar	Mekhliganj	9	9,123	**5**	9	0	9	0	1.60	1.06	2.34	5	July, 26
23	Cooch Behar	Tufanganj	12	20,998	**7**	12	0	12	0	4.38	1.75	0.88	7	July, 26
24	Dakshin Dinajpur	Balurghat	25	1,51,299	**42**	25	0	25	0	23.20	13.40	5.40	42	July, 26
25	Dakshin Dinajpur	Buniadpur	14	30183	**8**	14	0	10	4	4.00	2.00	2.00	8	July, 26
26	Dakshin Dinajpur	Gangarampore	18	56,217	**14**	13	5	13	5	5.00	2.00	5.00	12	July, 26
27	Darjeeling	Darjeeling	32	1,20,414	**24**	32	0	32	0	16.00	5.00	3.00	24	May, 26
28	Kalimpong	Kalimpong	23	49,403	**13**	16	7	10	4	6.00	2.00	4.00	12	Sept, 26
29	Darjeeling	Kurseong	20	42,346	**7**	20	0	10	10	2.55	1.27	3.18	7	Sept, 26
30	Darjeeling	Mirik	9	11,513	**4**	6	3	6	3	2.00	1.00	1.00	4	July, 26
31	Darjeeling	Siliguri MC	47	5,13,264	**297**	47	0	35	12	142.00	70.00	85.00	297	May, 26
32	Howrah	Uluberia	32	2,32,290	**86**	32	0	25	7	26.00	12.00	48.00	86	July, 26

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
33	Hooghly	Arambagh	19	66,175	16	19	0	14	5	9.00	5.00	2.00	16	July, 26
34	Hooghly	Baidyabati	23	1,21,110	50	23	0	23	0	34.00	14.00	2.00	50	July, 26
35	Hooghly	Bansberia	22	1,03,920	30	20	2	16	6	8.00	4.00	17.00	29	July, 26
36	Hooghly	Bhadreswar	22	1,01,477	26	22	0	22	0	16.25	9.75	0.00	26	Achieved
37	Hooghly	Champdany	22	1,11,251	19	20	2	18	4	9.00	4.00	5.00	18	Aug, 26
38	Hooghly	Chandannagore MC	33	1,66,867	52	33	0	31	2	27.00	17.00	8.00	52	July, 26
39	Hooghly	Dankuni	21	94,966	32	21	0	17	4	15.00	8.00	9.00	32	Sept, 26
40	Hooghly	Hooghly Chinsurah	30	1,77,259	56	30	0	20	10	38.00	16.00	2.00	56	Sept, 26
41	Hooghly	Konnagar	20	76,172	26	20	0	19	1	15.29	7.65	3.06	26	Aug, 26
42	Hooghly	Rishra	23	1,24,585	45	23	0	9	14	13.30	6.70	25.00	45	July, 26
43	Hooghly	Serampore	29	1,83,339	95	29	0	16	13	30.00	21.00	44.00	95	July, 26
44	Hooghly	Tarakeswar	15	30,947	10	15	0	15	0	5.00	3.00	2.00	10	May, 26
45	Hooghly	Uttarpara Kotrung	24	1,62,386	72	24	0	24	0	47.00	25.00	0.00	72	Sept, 26
46	Alipurduar	Alipurduar	20	65,232	21	15	5	15	5	11.50	7.50	1.00	20	July, 26
47	Jalpaiguri	Dhupguri	16	44,719	7	1	15	1	15	2.00	1.00	1.00	4	May, 26
48	Jalpaiguri	Jalpaiguri	25	1,07,341	38	25	0	25	0	22.80	13.24	1.96	38	Aug, 26
49	Jalpaiguri	Mal	15	25,218	6	11	4	11	4	3.00	1.50	1.00	6	July, 26
50	Malda	English Bazar	29	2,05,521	82	29	0	19	10	40.00	18.00	24.00	82	Sept, 26
51	Malda	Old Malda	20	84,012	23	20	0	20	0	11.00	7.50	4.50	23	July, 26
52	Murshidabad	Beldanga	14	29,182	7	14	0	14	0	2.60	1.60	2.80	7	Aug, 26
53	Murshidabad	Berhampore	28	1,95,363	66	28	0	18	10	25.00	14.00	27.00	66	Sept, 26
54	Murshidabad	Dhuliyan	21	95,706	18	21	0	0	21	6.00	4.00	13.00	23	Aug, 26
55	Murshidabad	Domkal	21	1,21,927	24	21	0	6	15	9.00	5.40	9.60	24	July, 26
56	Murshidabad	Jangipur	21	88,165	29	21	0	21	0	14.50	8.70	5.80	29	July, 26
57	Murshidabad	Jiaganj-Azimganj	17	51,790	15	9	8	2	15	6.00	2.00	5.00	13	July, 26
58	Murshidabad	Kandi	18	55,632	12	15	3	15	3	7.00	2.50	1.50	11	July, 26
59	Murshidabad	Murshidabad	16	44,064	16	16	0	10	6	6.00	4.00	6.00	16	Sept, 26
60	Nadia	Birnagar	14	30799	10	14	0	13	1	6.50	3.00	0.50	10	July, 26
61	Nadia	Chakdah	21	95,203	19	6	15	6	3	5.00	3.00	6.00	14	Aug, 26
62	Nadia	Cooper's Camp	12	18,839	5	12	0	8	4	2.50	1.00	1.50	5	May, 26
63	Nadia	Gayeshpur	18	58,998	16	18	0	4	14	8.00	3.20	4.80	16	July, 26
64	Nadia	Haringhata	17	45,953	12	5	12	0	0	0.00	0.00	9.00	9	May, 26
65	Nadia	Kalyani	21	1,00,620	50	21	0	3	18	12.00	4.00	34.00	50	July, 26
66	Nadia	Krishnanagar	25	1,53,062	90	25	0	21	4	50.00	24.00	16.00	90	May, 26
67	Nadia	Nabadwip	24	1,25,528	36	24	0	24	0	18.60	12.00	5.40	36	May, 26
68	Nadia	Ranaghat	20	75,365	20	20	0	12	8	10.00	6.00	4.00	20	July, 26

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
69	Nadia	Santipur	24	1,51,777	40	24	0	16	8	18.00	8.00	14.00	40	July, 26
70	Nadia	Taherpur	13	20,894	5	13	0	11	2	2.70	2.00	0.30	5	Aug, 26
71	North 24 Parganas	Ashokenagar-Kalyangarh	23	1,21,592	35	23	0	23	0	22.00	10.00	3.00	35	July, 26
72	North 24 Parganas	Baduria	17	52,500	6	6	11	6	11	0.50	0.20	3.00	4	Aug, 26
73	North 24 Parganas	Baranagar	34	2,45,213	134	34	0	11	23	50.50	15.00	68.50	134	Sept, 26
74	North 24 Parganas	Barasat	35	2,78,435	163	35	0	30	5	79.00	60.00	24.00	163	May, 26
75	North 24 Parganas	Barrackpore	24	1,52,783	40	24	0	22	2	26.40	12.40	1.20	40	Sept, 26
76	North 24 Parganas	Basirhat	23	1,25,058	53	23	0	23	0	39.50	9.50	4.00	53	Aug, 26
77	North 24 Parganas	Bhatpara	35	3,85,867	164	35	0	35	0	86.57	58.18	19.25	164	May, 26
78	North 24 Parganas	Bidhan Nagar MC	41	6,34,107	287	41	0	0	41	111.00	76.00	100.00	287	Sept, 26
79	North 24 Parganas	Bongaon	22	1,08,864	42	18	4	16	6	20.00	9.00	12.00	41	Sept, 26
80	North 24 Parganas	Dum Dum	22	1,14,786	50	22	0	8	16	22.50	7.50	20.00	50	Sept, 26
81	North 24 Parganas	Garulia	21	85,336	35	21	0	8	13	12.00	5.00	18.00	35	Sept, 26
82	North 24 Parganas	Gobardanga	17	45,392	12	17	0	17	0	10.00	2.00	0.00	12	Achieved
83	North 24 Parganas	Habra	24	1,47,221	44	24	0	20	4	29.00	8.00	7.00	44	May, 26
84	North 24 Parganas	Halisahar	23	1,24,851	38	16	7	16	7	13.00	8.00	15.00	36	July, 26
85	North 24 Parganas	Kamarhati	35	331163	128	35	0	28	7	60.00	41.00	27.00	128	Sept, 26
86	North 24 Parganas	Kanchrapara	24	1,29,576	37	19	5	19	0	15.00	10.00	8.00	33	Aug, 26
87	North 24 Parganas	Khardah	22	1,08,496	38	22	0	20	2	19.00	12.00	7.00	38	May, 26
88	North 24 Parganas	Madhyamgram	28	1,96,127	62	28	0	28	0	36.00	21.00	5.00	62	Aug, 26
89	North 24 Parganas	Naihati	31	2,18,194	72	31	0	20	11	22.00	12.00	38.00	72	July, 26
90	North 24 Parganas	New Barrackpore	20	76,879	22	20	0	20	0	11.60	5.20	5.20	22	Aug, 26
91	North 24 Parganas	North Barrackpore	23	1,32,806	46	23	0	12	11	20.00	8.00	18.00	46	July, 26

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
92	North 24 Parganas	North Dum Dum	34	2,49,142	30	34	0	34	0	20.00	10.00	0.00	30	Sept, 26
93	North 24 Parganas	Panihati	35	3,77,351	127	35	0	0	0	0.00	0.00	127.00	127	May, 26
94	North 24 Parganas	South Dum Dum	35	4,03,316	287	35	0	26	9	135.00	28.00	124.00	287	May, 26
95	North 24 Parganas	Taki	16	38,263	9	16	0	10	6	4.50	2.00	2.50	9	July, 26
96	North 24 Parganas	Titagarh	23	1,16,541	42	23	0	16	7	19.00	13.00	10.00	42	May, 26
97	Paschim Midnapore	Chandrakona	12	23,629	8	12	0	8	4	3.50	2.00	2.50	8	May, 26
98	Paschim Midnapore	Ghatal	17	54,591	17	13	4	4	13	5.00	4.00	7.00	16	July, 26
99	Jhargram	Jhargram	18	61,682	15	16	2	4	14	10.50	1.50	2.00	14	May, 26
100	Paschim Midnapore	Kharagpur	35	2,07,604	40	27	8	1	26	18.00	11.00	9.00	38	May, 26
101	Paschim Midnapore	Kharar	10	12,220	4	10	0	8	2	1.50	0.50	2.00	4	May, 26
102	Paschim Midnapore	Khirpai	10	16,385	5	10	0	3	7	3.00	1.00	1.00	5	May, 26
103	Paschim Midnapore	Midnapore	25	1,69,127	62	25	0	13	12	30.00	18.00	14.00	62	Sept, 26
104	Paschim Midnapore	Ramjibanpur	11	19,611	5	11	0	4	7	2.00	1.50	1.50	5	July, 26
105	Purba Midnapore	Contai	21	92,226	40	15	6	16	5	20.00	8.00	10.00	38	Sept, 26
106	Purba Midnapore	Egra	14	30,148	9	14	0	12	2	5.00	2.00	2.00	9	July, 26
107	Purba Midnapore	Haldia	29	2,00,827	80	29	0	3	26	15.00	5.00	60.00	80	May, 26
108	Purba Midnapore	Panskura	18	57,932	11	18	0	18	0	6.00	5.00	0.00	11	Achieved
109	Purba Midnapore	Tamluk	20	65,312	15	20	0	17	3	8.50	5.00	1.50	15	Aug, 26
110	Jhalda	Jhalda	12	19,540	4	12	0	12	0	1.50	1.00	1.50	4	July, 26
111	Purulia	Purulia	23	1,21,067	16	16	7	0	23	6.00	3.00	6.00	15	July, 26
112	Purulia	Raghunathpur	13	25,621	7	13	0	8	5	1.40	2.66	2.94	7	July, 26
113	South 24 parganas	Baruipur	17	53,128	22	17	0	6	11	12.00	3.00	7.00	22	July, 26
114	South 24 parganas	Budge Budge	20	76,858	24	20	0	18	2	13.60	7.60	2.80	24	Aug, 26
115	South 24 parganas	Diamond Harbour	16	43,169	12	16	0	9	7	5.00	2.50	4.50	12	May, 26

Sl No	District	ULB	No. of ward	Population (Census 2011)	Per day Generation of fresh waste (TPD)	Door to door collection of fresh waste in no. of wards		Collection of segregated fresh waste in no. of wards		Quantity of fresh waste being collected & transported per day (TPD)				Tentative timeline for ensuring 100% segregation
						Full	Partial	Full	Partial	Wet Waste	Dry Waste	Mixed Waste	Total	
116	South 24 parganas	Jainagar-Mazilpur	14	25,922	**6**	14	0	14	0	3.50	1.50	1.00	6	May, 26
117	South 24 parganas	Maheshtala	35	4,49,423	**168**	35	0	10	25	72.00	40.00	56.00	168	May, 26
118	South 24 parganas	Pujali	16	37,040	**11**	2	14	2	2	2.00	0.50	2.00	5	May, 26
119	South 24 parganas	Rajpur-Sonarpur	35	4,23,724	**279**	35	0	28	7	135.00	126.00	18.00	279	Sept, 26
120	Uttar Dinajpur	Dalkhola	16	37,063	**11**	13	3	9	7	5.00	3.50	2.00	11	July, 26
121	Uttar Dinajpur	Islampur	17	54,340	**14**	13	4	13	4	5.00	3.50	4.00	13	July, 26
122	Uttar Dinajpur	Kaliaganj	17	53,530	**22**	17	0	15	2	11.00	7.00	4.00	22	July, 26
123	Uttar Dinajpur	Raiganj	27	1,83,612	**60**	19	8	0	9	16.00	9.00	33.00	58	July, 26
124	Howrah	Howrah MC	50	10,70,645	**568**	45	5	11	0	75.00	40.00	432.00	547	May, 26
125	Howrah	Bally	35	2,91,916	**112**	35	0	0	0	0.00	0.00	112.00	112	May, 26
126	Jalpaiguri	Maynaguri	17	36,263	**8**	2	15	0	17	3.00	1.50	1.00	6	July, 26
127	Alipurduar	Falakata	18	54,039	**14**	2	16	0	0	0.00	0.00	5.77	6	Aug, 26
128	Kolkata	Kolkata MC	144	4594718	**3668**	144	0	27	117	1840.00	360.00	1468.00	3668	Apr '26
		Total =	2997	**21532295**	**10227.00**	**2761**	**236**	**1772**	**1019**	**4488.20**	**1837.13**	**3799.57**	**10124.91**	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to February, 2026

Sl. No.	Name of District	ULB	No. of ward	Population (Census 2011)	Waste Generation (TPD)	Waste being processed per day (TPD)	Gap in processing (TPD)	Type of Wet Waste processing Unit	Type of Dry Waste processing Unit	Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
										Organic material (Wet Waste)	Inert	RDF	Other	Organic material	Inert	RDF	Others	Energy plants (Waste to energy plants)	Bio-Compost units	Used in Cement units	Land Fill Sites	MRF	Budget outlay (Rs. In Cr)	DPR Prepared for Plant Infrastructure works (Yes/ No)	Tender Published for engagement of agency for Plant Infrastructure works (Yes/ No)	Work Order Issued to agency (Yes/ No)	Infrastructure Work Started by agency (Yes/ No)	Time line for starting of 100% processing of Fresh waste	Remarks
1	Bankura	Bankura	24	1,37,386	**40**	0	40	Windraw Composting	Material Recovery Facility (MRF)	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	6.68	Yes	Yes	Yes	Yes	June, 2026	
2	Bankura	Bishnupur	19	67,783	**14**	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.85	Yes	Yes	Yes	Yes	Sept, 2026	
3	Bankura	Sonamukhi	15	34,228	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.42	Yes	Yes	Yes	Yes	April, 2026	
4	Paschim Bardhaman	Asansol MC	106	11,56,387	**566**	0	566	Windraw Composting	MRF	311.3	56.6	33.96	164.14	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	76.65	Yes	Yes	Yes	No	June, 2026	
5	Purba Bardhaman	Barddhaman	35	3,14,638	**98**	0	98	Windraw Composting	MRF	53.9	9.8	5.88	28.42	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	18.40	Yes	No	No	No	Dec, 2026	
6	Purba Bardhaman	Dainhat	14	24,397	**7**	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.16	Yes	No	No	No	Dec, 2027	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Sept, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
7	Paschim Bardhaman	Durgapur MC	43	5,66,517	**244**	0	244	Windraw Composting	MRF	134.2	24.4	14.64	70.76	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	33.29	Yes	Yes	Yes	No	Dec, 2026	Work order issued to an agency for setting up of fresh waste processing unit at the ULB. Due to local agitation the agency could not start infrastrcure work for setting up of fresh waste processing unit at the reclaimed land of the dumpsite. For this, a feasible land is under identification.
8	Purba Bardhaman	Guskhara	16	35,374	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.31	Yes	Yes	Yes	Yes	June, 2026	
9	Purba Bardhaman	Kalna	18	56,722	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.52	Yes	Yes	Yes	Yes	June, 2026	
10	Purba Bardhaman	Katwa	20	81,615	**26**	0	26	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	5.16	Yes	No	No	No	Dec, 2027	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
11	Purba Bardhaman	Memari	16	41,455	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.75	Yes	Yes	Yes	Yes	April, 2026	
12	Birbhum	Bolpur	22	80,210	**31**	0	31	Windraw Composting	MRF	17.05	3.1	1.86	8.99	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	6.02	Yes	No	No	No	Dec, 2026	
13	Birbhum	Dubrajpur	16	38,041	**10**	0	10	Windraw Composting	MRF	5.5	1	0.6	2.9	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.70	Yes	Yes	Yes	Yes	April, 2026	
14	Birbhum	Nalhati	16	41,244	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.64	Yes	Yes	Yes	Yes	April, 2026	
15	Birbhum	Rampurhat	18	57,833	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.07	Yes	Yes	Yes	Yes	March, 2027	
16	Birbhum	Sainthia	16	44608	**12**	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.08	Yes	Yes	Yes	Yes	April, 2026	
17	Birbhum	Suri	21	90,314	**26**	0	26	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.05	Yes	Yes	Yes	Yes	Sept, 2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to February, 2026

										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
18	Cooch Behar	Coochbehar	20	77935	**20**	0	20	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.07	Yes	No	No	No	Dec, 2026	
19	Cooch Behar	Dinhata	16	36,124	**9**	3	6	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	1.65	0.18	0.3	0.87	1.70	Yes	Yes	Yes	Yes	April, 2026	
20	Cooch Behar	Haldibari	11	14,404	**4**	2.5	1.5	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	1.375	0.15	0.25	0.725	0.57	Yes	Yes	Yes	Yes	June, 2026	
21	Cooch Behar	Mathabhanga	12	23,895	**9**	5	4	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.75	0.3	0.5	1.45	1.56	Yes	Yes	Yes	Yes	March, 2027	Construction of Infrsatructre Work for setting up of fresh waste processing unit was started but due to public agiatation it was disrupted.
22	Cooch Behar	Mekhliganj	9	9,123	**5**	4	1	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.2	0.24	0.4	1.16	0.51	Yes	Yes	Yes	Yes	April, 2026	
23	Cooch Behar	Tufanganj	12	20,998	**7**	6	1	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	3.3	0.36	0.6	1.74	0.88	Yes	Yes	Yes	Yes	April, 2026	
24	Dakshin Dinajpur	Balurghat	25	1,51,299	**42**	0	42	Windraw Composting	MRF	23.1	4.2	2.52	12.18	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	8.21	Yes	Yes	Yes	Yes	Dec, 2026	
25	Dakshin Dinajpur	Buniadpur	14	30183	**8**	0	8	Windraw Composting	MRF	4.4	0.8	0.48	2.32	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.31	Yes	Yes	Yes	Yes	Dec, 2026	
26	Dakshin Dinajpur	Gangarampur	18	56,217	**14**	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.07	Yes	Yes	Yes	Yes	Dec, 2026	
27	Darjeeling	Darjeeling	32	1,20,414	**24**	0	24	Windraw Composting	MRF	13.2	2.4	1.44	6.96	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.83	Yes	No	No	No	Sept, 2027	
28	Kalimpong	Kalimpong	23	49,403	**13**	0	13	Windraw Composting	MRF	7.15	1.3	0.78	3.77	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.08	Yes	No	No	No	Sept, 2027	
29	Darjeeling	Kurseong	20	42,346	**7**	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.20	Yes	No	No	No	Dec, 2027	
30	Darjeeling	Mirik	9	11,513	**4**	0	4	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.46	Yes	No	No	No	Dec, 2027	
31	Darjeeling	Siliguri MC	47	5,13,264	**297**	297	0	Windraw Composting	MRF	163.35	29.7	17.82	86.13	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	163.35	17.82	29.7	86.13	39.20	Yes	Yes	Yes	Yes	Started	
32	Howrah	**Uluberia**	32	2,32,290	**86**	0	86	Windraw Composting	MRF	47.3	8.6	5.16	24.94	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	13.14	Yes	Yes	Yes	Yes	June, 2026	
33	Hooghly	Arambagh	19	66,175	**16**	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.15	Yes	No	No	No	Dec, 2027	State Government has provided a land to the ULB for setting up of fresh waste processing unit. But due to public agitation further action could not be taken. Local administration is trying to reslove the matter.Expected that the matter will be resloved within Oct, 2025. After that, tender will be folated for enagagement of agency for setting up of freh waste processing plant.
34	Hooghly	Baidyabati	23	1,21,110	**50**	50	0	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	27.5	3	5	14.5	5.48	Yes	Yes	Yes	Yes	Started	
35	Hooghly	Bansberia	22	1,03,920	**30**	0	30	Windraw Composting	MRF	16.5	3	1.8	8.7	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.38	Yes	No	No	No	Dec, 2026	
36	Hooghly	Bhadreswar	22	1,01,477	**26**	26	0	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	14.3	1.56	2.6	7.54	3.50	Yes	Yes	Yes	Yes	Started	
37	Hooghly	Champdany	22	1,11,251	**19**	19	0	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	10.45	1.14	1.9	5.51	2.08	Yes	Yes	Yes	Yes	Started	
38	Hooghly	Chandernagore municipal corporation	33	1,66,867	**52**	0	52	Bio-CNG	MRF	28.6	5.2	3.12	15.08	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	7.82	Yes	No	No	No	Dec, 2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to February, 2026																														
					Method of treatment in TPD					Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste												
39	Hooghly	Dankuni	21	94,966	32	32	0	Windraw Composting	MRF	17.6	3.2	1.92	9.28	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	17.6	1.92	3.2	9.28	4.60	Yes	Yes	Yes	Yes	Started		
40	Hooghly	Hooghly Chinsurah	30	1,77,259	56	0	56	Bio-CNG	MRF	30.8	5.6	3.36	16.24	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	8.21	Yes	No	No	No	Dec, 2026		
41	Hooghly	Konnagar	20	76,172	26	26	0	Windraw Composting	MRF	14.3	2.6	1.56	7.54	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	14.3	1.56	2.6	7.54	2.79	Yes	Yes	Yes	Yes	Started		
42	Hooghly	Rishra	23	1,24,585	45	45	0	Windraw Composting	MRF	24.75	4.5	2.7	13.05	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	24.75	2.7	4.5	13.05	5.91	Yes	Yes	Yes	Yes	Started		
43	Hooghly	Serampore	29	1,83,339	95	95	0	Windraw Composting	MRF	52.25	9.5	5.7	27.55	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	52.25	5.7	9.5	27.55	10.40	Yes	Yes	Yes	Yes	Started		
44	Hooghly	Tarakeswar	15	30,947	10	0	10	Windraw Composting	MRF	5.5	1	0.6	2.9	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.44	Yes	No	No	No	Dec, 2026		
45	Hooghly	Uttarpara Kotrung	24	1,62,386	72	72	0	Windraw Composting	MRF	39.6	7.2	4.32	20.88	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	39.6	4.32	7.2	20.88	7.88	Yes	Yes	Yes	Yes	Started		
46	Alipurduar	Alipurduar	20	65,232	21	21	0	Windraw Composting	MRF	11.55	2.1	1.26	6.09	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	11.55	1.26	2.1	6.09	2.30	Yes	Yes	Yes	Yes	Started		
47	Jalpaiguri	Dhupguri	16	44,719	7	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.15	Yes	No	No	No	June, 2026		
48	Jalpaiguri	Jalpaiguri	25	1,07,341	38	3	35	Windraw Composting	MRF	20.9	3.8	2.28	11.02	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	1.65	0.18	0.3	0.87	6.79	Yes	Yes	Yes	Yes	March, 2027		
49	Jalpaiguri	Mal	15	25,218	6	0	6	Windraw Composting	MRF	3.3	0.6	0.36	1.74	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.99	Yes	Yes	Yes	Yes	June, 2026		
50	Malda	English Bazar	29	2,05,521	82	0	82	Windraw Composting	MRF	45.1	8.2	4.92	23.78	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	16.97	Yes	Yes	Yes	Yes	Dec, 2026		
51	Malda	Old Malda	20	84,012	23	0	23	Windraw Composting	MRF	12.65	2.3	1.38	6.67	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.05	Yes	No	No	No	Dec, 2026		
52	Murshidabad	Beldanga	14	29,182	7	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.20	Yes	Yes	Yes	Yes	March, 2027		
53	Murshidabad	Berhampore	28	1,95,363	66	0	66	Windraw Composting	MRF	36.3	6.6	3.96	19.14	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	10.95	Yes	Yes	Yes	Yes	Dec, 2026		
54	Murshidabad	Dhuliyan	21	95,706	18	0	18	Windraw Composting	MRF	9.9	1.8	1.08	5.22	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.19	Yes	Yes	Yes	Yes	Dec, 2026		
55	Murshidabad	Domkol	21	1,21,927	24	0	24	Windraw Composting	MRF	13.2	2.4	1.44	6.96	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.38	Yes	No	No	No	Dec, 2027		
56	Murshidabad	Jangipur	21	88,165	29	0	29	Windraw Composting	MRF	15.95	2.9	1.74	8.41	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	5.26	Yes	No	No	No	Dec, 2027		
57	Murshidabad	Jiaganj-Azimganj	17	51,790	15	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.79	Yes	Yes	Yes	Yes	Dec, 2026		
58	Murshidabad	Kandi	18	55,632	12	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.08	Yes	No	No	No	Dec, 2027		
59	Murshidabad	Murshidabad	16	44,064	16	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.19	Yes	Yes	Yes	Yes	Dec, 2026		
60	Nadia	Birnagar	14	30799	10	8	2	Windraw Composting	MRF	5.5	1	0.6	2.9	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	4.4	0.48	0.8	2.32	1.08	Yes	Yes	Yes	Yes	April, 2026		

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to February, 2026

										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
61	Nadia	Chakdaha	21	95,203	**19**	0	19	Windraw Composting	MRF	10.45	1.9	1.14	5.51	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.05	Yes	Yes	Yes	Yes	Dec, 2026	
62	Nadia	Cooper's Camp	12	18,839	**5**	0	5	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.88	Yes	Yes	Yes	Yes	April, 2026	
63	Nadia	Gayeshpur	18	58,998	**16**	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.19	Yes	Yes	Yes	Yes	April, 2026	
64	Nadia	Haringhata	17	45,953	**12**	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.19	Yes	No	No	No	March, 2027	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
65	Nadia	Kalyani	21	1,00,620	**50**	0	50	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	6.57	Yes	No	No	No	Dec, 2026	
66	Nadia	Krishnanagar	25	1,53,062	**90**	120	-30	Windraw Composting	MRF	49.5	9	5.4	26.1	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	66	7.2	12	34.8	13.14	Yes	Yes	Yes	Yes	March, 2027	
67	Nadia	Nabadwip	24	1,25,528	**36**	16	20	Windraw Composting	MRF	19.8	3.6	2.16	10.44	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	8.8	0.96	1.6	4.64	6.57	Yes	Yes	Yes	Yes	Sept, 2026	
68	Nadia	Ranaghat	20	75,365	**20**	0	20	Windraw Composting	MRF	11	2	1.2	5.8	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.74	Yes	Yes	Yes	Yes	Sept, 2026	
69	Nadia	Santipur	24	1,51,777	**40**	0	40	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	9.09	Yes	Yes	Yes	Yes	Sept, 2026	
70	Nadia	Taherpur NAA	13	20,894	**5**	4.1	0.9	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.255	0.246	0.41	1.189	0.55	Yes	Yes	Yes	Yes	April, 2026	
71	North 24 Parganas	Ashoknagar-Kalyangarh	23	1,21,592	**35**	6	29	Windraw Composting	MRF	19.25	3.5	2.1	10.15	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	3.3	0.36	0.6	1.74	5.26	Yes	Yes	Yes	Yes	Sept, 2026	
72	North 24 Parganas	Baduria	17	52,500	**6**	4	2	Windraw Composting	MRF	3.3	0.6	0.36	1.74	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	2.2	0.24	0.4	1.16	0.65	Yes	Yes	Yes	Yes	June, 2026	
73	North 24 Parganas	Baranagar	34	2,45,213	**134**	554	0	Windraw Composting & Bio methanation	MRF	304.7	55.4	33.24	160.66	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	304.7	33.24	55.4	160.66	70.91	Yes	Yes	Yes	Yes	Started	
74	North 24 Parganas	Dum Dum	35	2,78,435	**163**																								
75	North 24 Parganas	South DumDum	24	1,52,783	**40**																								
76	North 24 Parganas	North Dum Dum	23	1,25,058	**53**																								
77	North 24 Parganas	New Barrackpur	35	3,85,867	**164**																								
78	North 24 Parganas	Kamarhati	41	6,34,107	**287**	0	287	Windraw Composting	MRF	157.85	55.4	33.24	160.66	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	17.52	Yes	Yes	Yes	Yes	Sept, 2026	
79	North 24 Parganas	Barasat	22	1,08,864	**42**	0	42	Windraw Composting	MRF	23.1	4.2	2.52	12.18	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	22.23	Yes	Yes	Yes	Yes	April, 2026	
80	North 24 Parganas	Barrackpore	22	1,14,786	**50**	0	50	Windraw Composting	MRF	27.5	5	3	14.5	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.48	Yes	Yes	No	No	March, 2027	
81	North 24 Parganas	Basirhat	21	85,336	**35**	53	-18	Windraw Composting	MRF	19.25	3.5	2.1	10.15	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	29.15	3.18	5.3	15.37	6.13	Yes	Yes	Yes	Yes	April, 2026	
82	North 24 Parganas	Bhatpara	17	45,392	**12**	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	22.45	Yes	No	No	No	March, 2027	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to February, 2026

					Method of treatment in TPD					Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
83	North 24 Parganas	Bidhannagar Municipal Corporation	24	1,47,221	**44**	0	44	Bio-CNG	MRF	24.2	4.4	2.64	12.76	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	38.33	Yes	Yes	No	No	Dec, 2026	
84	North 24 Parganas	Bongaon	23	1,24,851	**38**	31	7	Windraw Composting	MRF	20.9	3.8	2.28	11.02	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	17.05	1.86	3.1	8.99	6.79	Yes	No	No	No	Dec, 2026	
85	North 24 Parganas	Garulia	35	331163	**128**	0	128	Windraw Composting	MRF	70.4	12.8	7.68	37.12	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	3.92	Yes	Yes	No	No	March, 2027	
86	North 24 Parganas	Gobardanga	24	1,29,576	**37**	0	37	Windraw Composting	MRF	20.35	3.7	2.22	10.73	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.04	Yes	Yes	Yes	Yes	Dec, 2026	
87	North 24 Parganas	Habra	22	1,08,496	**38**	0	38	Windraw Composting	MRF	20.9	3.8	2.28	11.02	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	7.67	Yes	Yes	Yes	Yes	Sept, 2026	
88	North 24 Parganas	Halisahar	28	1,96,127	**62**	0	62	Windraw Composting	MRF	34.1	6.2	3.72	17.98	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.69	Yes	No	No	No	March, 2027	State Government identified the land for setting up of fresh waste processing unit. Expected that the land will be under possession of the ULB within Oct, 2025. After that the tender will be floated for enagagement of agency for setting up of fresh waste processing plant.
89	North 24 Parganas	Kanchrapara	31	2,18,194	**72**	0	72	Windraw Composting	MRF	39.6	7.2	4.32	20.88	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	5.90	Yes	Yes	Yes	No	Dec, 2026	
90	North 24 Parganas	Khardah	20	76,879	**22**	0	22	Windraw Composting	MRF	12.1	2.2	1.32	6.38	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.08	Yes	Yes	No	No	March, 2027	
91	North 24 Parganas	Madhyamgram	23	1,32,806	**46**	16	30	Windraw Composting	MRF	25.3	4.6	2.76	13.34	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	8.8	0.96	1.6	4.64	9.86	Yes	Yes	Yes	No	Dec, 2026	
92	North 24 Parganas	Naihati	34	2,49,142	**30**	0	30	Windraw Composting	MRF	16.5	3	1.8	8.7	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	11.72	Yes	Yes	Yes	Yes	Dec, 2026	
93	North 24 Parganas	North Barrackpore	35	3,77,351	**127**	0	127	Windraw Composting	MRF	69.85	12.7	7.62	36.83	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	7.99	Yes	Yes	No	No	March, 2027	
94	North 24 Parganas	Panihati	35	4,03,316	**287**	0	287	Windraw Composting	MRF	157.85	28.7	17.22	83.23	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	19.27	Yes	No	No	No	March, 2027	
95	North 24 Parganas	Taki	16	38,263	**9**	8.4	0.6	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	4.62	0.504	0.84	2.436	1.53	Yes	Yes	Yes	Yes	April, 2026	
96	North 24 Parganas	Titagarh	23	1,16,541	**42**	0	42	Windraw Composting	MRF	23.1	4.2	2.52	12.18	Local Farmers/Hoticulture/ Agricluture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	5.22	Yes	Yes	No	No	March, 2027	
97	Paschim Midnapore	Chandrakona	12	23,629	**8**	0	8	Windraw Composting	MRF	4.4	0.8	0.48	2.32	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.92	Yes	Yes	Yes	Yes	April, 2026	
98	Paschim Midnapore	Ghatal	17	54,591	**17**	0	17	Windraw Composting	MRF	9.35	1.7	1.02	4.93	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.92	Yes	No	No	No	March, 2027	
99	Jhargram	Jhargram	18	61,682	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.12	Yes	Yes	Yes	Yes	June, 2026	
100	Paschim Midnapore	Kharagpur	35	2,07,604	**40**	40	0	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	22	2.4	4	11.6	8.98	Yes	Yes	Yes	Yes	Started	
101	Paschim Midnapore	Kharar	10	12,220	**4**	0	4	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.59	Yes	Yes	Yes	Yes	Dec, 2026	Construction of Infrsatructre Work for setting up of fresh waste processing unit is under process.
102	Paschim Midnapore	Khirpai	10	16,385	**5**	0	5	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.74	Yes	Yes	Yes	Yes	June, 2026	
103	Paschim Midnapore	Midnapore	25	1,69,127	**62**	0	62	Windraw Composting	MRF	34.1	6.2	3.72	17.98	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	10.07	Yes	Yes	Yes	Yes	Dec, 2026	
104	Paschim Midnapore	Ramjibonpur	11	19,611	**5**	0	5	Windraw Composting	MRF	2.75	0.5	0.3	1.45	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.77	Yes	Yes	Yes	Yes	June, 2026	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to February, 2026

										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
105	Purba Midnapore	Contai	21	92,226	**40**	0	40	Windraw Composting	MRF	22	4	2.4	11.6	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	6.57	Yes	Yes	Yes	No	March, 2027	
106	Purba Midnapore	Egra	14	30,148	**9**	0	9	Windraw Composting	MRF	4.95	0.9	0.54	2.61	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.60	Yes	Yes	Yes	No	March, 2027	
107	Purba Midnapore	Haldia	29	2,00,827	**80**	80	0	Windraw Composting	MRF	44	8	4.8	23.2	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	44	4.8	8	23.2	8.76	Yes	Yes	Yes	Yes	Started	
108	Purba Midnapore	Panskura	18	57,932	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.97	Yes	No	No	No	Dec, 2026	
109	Purba Midnapore	**Tamralipta**	20	65,312	**15**	0	15	Windraw Composting	MRF	8.25	1.5	0.9	4.35	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.69	Yes	No	No	No	March, 2027	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Sept, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
110	Jhalda	Jhalda	12	19,540	**4**	0	4	Windraw Composting	MRF	2.2	0.4	0.24	1.16	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	0.71	Yes	Yes	Yes	Yes	March, 2027	
111	Purulia	Purulia	23	1,21,067	**16**	0	16	Windraw Composting	MRF	8.8	1.6	0.96	4.64	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0		2.19	Yes	No	No	No	Dec, 2026	State Government is in the process for identifying the land for setting up of fresh waste processing unit. Expected that the land will be identifed within Sept, 2025. After that the tender will be folated for enagagement of agency for setting up of freh waste processing plant.
112	Purulia	Raghunathpur	13	25,621	**7**	0	7	Windraw Composting	MRF	3.85	0.7	0.42	2.03	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.20	Yes	No	No	No	Sept, 2026	
113	South 24 parganas	Baruipur	17	53,128	**22**	0	22	Windraw Composting	MRF	12.1	2.2	1.32	6.38	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.68	Yes	Yes	Yes	Yes	March, 2027	
114	South 24 parganas	Budge Budge	20	76,858	**24**	0	24	Windraw Composting	MRF	13.2	2.4	1.44	6.96	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	3.29	Yes	Yes	Yes	Yes	March, 2027	
115	South 24 parganas	Diamond Harbour	16	43,169	**12**	0	12	Windraw Composting	MRF	6.6	1.2	0.72	3.48	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.14	Yes	Yes	Yes	Yes	Dec, 2026	
116	South 24 parganas	Jaynagar Majilpur	14	25,922	**6**	4	2	Windraw Composting & Bio Gas	MRF	3.3	0.6	0.36	1.74	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	1	1.2	0.24	0.4	1.16	0.99	Yes	Yes	Yes	Yes	April, 2026	
117	South 24 parganas	Maheshtala	35	4,49,423	**168**	5	163	Vermi Compost	MRF	92.4	16.8	10.08	48.72	Local Farmers/Hoticulture/ Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	2.75	0.3	0.5	1.45	23.00	Yes	Yes	Yes	No	Dec, 2027	
118	South 24 parganas	Pujali	16	37,040	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.38	Yes	Yes	Yes	Yes	June, 2026	
119	South 24 parganas	Rajpur- Sonarpur	35	4,23,724	**279**	0	279	Windraw Composting & Bio Gas	MRF	153.45	27.9	16.74	80.91	Local Farmers/Hoticulture/ Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants		0	0	0	0	38.16	Yes	No	No	No	March, 2027	
120	Uttar Dinajpur	Dalkhola	16	37,063	**11**	0	11	Windraw Composting	MRF	6.05	1.1	0.66	3.19	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.89	Yes	Yes	Yes	Yes	June, 2026	
121	Uttar Dinajpur	Islampur	17	54,340	**14**	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.38	Yes	Yes	No	No	March, 2027	
122	Uttar Dinajpur	Kaliyaganj	17	53,530	**22**	0	22	Windraw Composting	MRF	12.1	2.2	1.32	6.38	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	4.27	Yes	Yes	Yes	Yes	June, 2026	
123	Uttar Dinajpur	Raiganj	27	1,83,612	**60**	0	60	Windraw Composting	MRF	33	6	3.6	17.4	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	10.40	Yes	Yes	Yes	Yes	Dec, 2026	
124	Howrah	Howrah MC	50	10,70,645	**568**	10	558	Windraw Composting	MRF	312.4	56.8	34.08	164.72	Local Farmers/Hoticulture/ Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	5.5	0.6	1	2.9	77.75	Yes	No	No	No	Dec, 2027	
125	Howrah	Bally	35	2,91,916	**112**	0	112	Windraw Composting	MRF	61.6	11.2	6.72	32.48	Local Farmers/Hoticulture/ Agriculture	SLF/Road Making/Low land filling	RDF based Cement Plants/Making of different road items (paver block/tiles etc)	Recycling Plants	0	0	0	0	0	15.32	Yes	No	No	No	March, 2027	

Status and action plan for ensuring 100% processing of fresh waste for 128 ULBs of West Bengal up to February, 2026																													
										Method of treatment in TPD				Final destination of each of the componentsof processed waste				Break up details of waste processing					Action plan to process 100% of waste						
126	Jalpaiguri	Maynaguri	17	36,263	8	0	8	Windraw Composting	MRF	4.4	0.8	0.48	2.32	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	1.39	Yes	Yes	Yes	Yes	April, 2026	
127	Alipurduar	Falakata	18	54,039	14	0	14	Windraw Composting	MRF	7.7	1.4	0.84	4.06	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	0	0	0	0	0	2.41	Yes	Yes	Yes	Yes	April, 2026	
128	Kolkata	Kolkata MC	144	4594718	3668	609	3059	Windrow Compost & Bio-CNG	Material Recovery Facility & Plastic Processing Unit	2017.4	366.8	220.08	1063.72	Local Farmers/ Hoticulture/ Aggricluture	SLF / Road Making / Low land filling	RDF based Cement Plants / Making of different road items (paver block/ tiles etc)	Recycling Plants	5	500	2	0	102	600.00	Yes	Yes	Yes	Yes	Dec,2026	
	Total =		2997	21532295	10227	2275	7952																1554.41						

Status of Bio-mining & Bio-remediation of Legacy Waste of 128 ULBs of West Bengal up to February, 2026

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Composition of the Waste				Process adopted to remidiate at each site	Final Destination of the Components at				Earmarked Budget (Rs. In Crore)	Action plan to remidiate and recover the sites				Remarks
																		Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)		Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)		P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	
1	ALIPURDUAR	Alipurduar	1	Beside Radhamadhab Mandir	26°29'33"N 89°32'29"E	0.33	4274	4274	Completed	0.33	0	0	4274	0	4274	Completed	0.33	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.24	NA	NA	NA	NA	Total area recliamed
2	BANKURA	Bankura	1	Keshra Trenching Ground	23.267285° N 87.035388°E	16.53	172937.6	172938	Completed	6.50	187000	96850	359937.6	90150	269788	Jun-26	10.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	19.80	Yes	Yes	Yes	Yes	
3	BANKURA	Sonamukhi	1	Adrab Bazar	23.300813° N 87.398289°E	1.50	2400	2400	Completed	1.50	0	0	2400	0	2400	Completed	1.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.13	NA	NA	NA	NA	Total area recliamed
4	BIRBHUM	Bolpur	1	Bolpur, Khoskadambatur, P. S. Bolpur, JL No. 95, Plot No. 2590, 2703	23.677955° N, 87.721413°E	3.33	60814	60814	Completed	1.20	108870	65750	169684	43120	126564	Jun-26	2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.33	Yes	Yes	Yes	Yes	
5	BIRBHUM	Dubrajpur	1	Mahaprabhu Gate	23.78196°N 87.36859°E	1.20	6122	6122	Completed	0.75	1,05,914	0	112036	105914	6122	Sep-26	0.75	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.16	Yes	No	No	No	
6	BIRBHUM	Rampurhat	1	Bonat & Kusumba Road	24.18826°N 87.75746°E	3.85	24212	24212	Completed	0.85	49280	37900	73492	11380	62112	Jun-26	1.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.04	Yes	Yes	Yes	Yes	
7	BIRBHUM	Sainthia	1	Ward No. 14	23.5657°N 87.4039°E	1.10	7261	7261	Completed	0.40	80,805	0	88066	80805	7261	July, 2026	0.6	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.84	Yes	No	No	No	
8	BIRBHUM	Suri	1	Dhanyogram (JL No. - 206)	23.95225°N 87.48576°E	2.00	16428	16428	Completed	0.60	48870	37100	65298	11770	53528	Jun-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.59	Yes	Yes	Yes	Yes	
9	BIRBHUM	Nalhati	1	Khanpur	24.30658°N 87.825631°E	5.00	56000	56000	Completed	5	36800	0	92800	36800	56000	Apr-26	3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.10	Yes	No	No	No	
10	COOCH BEHAR	Cooch Behar	1	Guriahati-II	26.299124° N 89.468282°E	6.75	67319.21	67319	Completed	2.20	177600	0	244919.21	177600	67319	Sep-26	3.25	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	13.47	Yes	No	No	No	
11	COOCH BEHAR	Dinhata	1	Buri dharia	26.821°N 89.2652°E	3.20	12432	12432	Completed	1.20	30220	0	42652	30220	12432	May-26	1.2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.35	Yes	No	No	No	
12	COOCH BEHAR	Haldibari	1	DBDH	26°19'27.4" N 88°47'6.5"E	0.73	6491.17	6491	Completed	0.20	41400	0	47891.17	41400	6491	Sep-26	0.2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.63	Yes	No	No	No	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
13	COOCH BEHAR	Mathabhanga	2	Ward No. - 4 (behind Jangli Kalibari and Manasi River) & Ward No. - 2, KhadanGhat (Beside Manasi and Sutunga River)	26.2041°N 89.137°E & 26.2017°N 89.1316°E	2.20	8830.16	8830	Completed	1.00	14800	0	23630.16	14800	8830	Jun-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.30	Yes	No	No	No	
14	COOCH BEHAR	Tufanganj	1	Kamat Phoolbari	26.1846°N 89.4014°E	2.70	8918.15	8918	Completed	1.00	19640	0	28558.15	19640	8918	Dec-25	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.57	Yes	No	No	No	
15	DAKSHIN DINAJPUR	Balurghat	1	5 no. Bhatpara, Dangi Under Bhatpara Gram panchayat	25.2052169° N 88.76702841 °E	9.99	72514.595	72515	Completed	3.00	154530	78365	227044.595	76165	150880	Aug-26	5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	12.49	Yes	Yes	Yes	Yes	
16	DAKSHIN DINAJPUR	Gangarampore	1	Naroi Dump-pit, 6 no. Anchol, Gangarappur	25.402148° N 88.532081°E	2.25	4275	4275	Completed	1.10	29100	12800	33375	16300	17075	Sep-26	1.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.84	Yes	Yes	Yes	Yes	
17	DARJEELING	Siliguri MC	1	Don Bosco colony	26.746839° N 88.452293°E	26.00	379382	379382	Completed	10.50	1150000	168720	1529382	981280	548102	Dec-26	15.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	84.12	Yes	Yes	Yes	Yes	
18	HOOGHLY	Chandannagore MC	1	Kalupukur Vermi-Compost Plant, Kolupukur Bhagar more, Ward No. 8	22°52'13"N, 88°21'32"E	4.94	215916	215916	Completed	1.00	106252	81300	322168	24952	297216	Sep-26	2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	17.72	Yes	Yes	Yes	Yes	
19	HOOGHLY	Hooghly Chinsurah	1	Kedia – I GP, Sukantanagar Rabindranagar	22°53'35"N 88°22'44"E	6.50	126266	126266	Completed	2.50	102159	16900	228425	85259	143166	Sep-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	12.56	Yes	Yes	Yes	Yes	
20	HOOGHLY	Baidyabati																														
21	HOOGHLY	Champdany																														
22	HOOGHLY	Rishra	1	RWMC	22.7888N, 88.31202E	52.00	220794	130254	Dec-25	5.00	0	0	220794	90540	130254	Dec, 2026	5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	12.14	No	No	No	No	
23	HOOGHLY	Serampore																														
24	HOOGHLY	Uttarpara-Kotrung																														
25	HOOGHLY	Konnagar																														
26	HOOGHLY	Bhadreswar	1	Sanjay colony, N S Road,	22.834139°N, 88.349718°E	0.42	320000	0	Jun-26	0	337000	0	657000	657000	0	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	36.14	Yes	No	No	No	
27	HOOGHLY	Dankuni	1	Beside Parbatipur Road, Ramanathpur (Panchayet Area)	22°40'31".N , 88°13'58".E	2.40	48078	48078	Completed	1.3	0	0	48078	0	48078	Completed	1.3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.64	NA	NA	NA	NA	Total area recliamed
28	HOOGHLY	Bansberia	2	Ward no. 8 & 18	22° 57'45.1" N 88° 23'45.3" E	2.79	47000	0	Sep-25	0	108000	0	155000	155000	0	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.53	Yes	No	No	No	
29	HOOGHLY	Arambagh	1	Kalipur (Ward No 6)	22.88525N, 87.77549E	1.20	37750	0	Sep-25	0	37750	28675	75500	46825	28675	Jul-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.15	Yes	Yes	Yes	Yes	
30	HOOGHLY	Tarakeswar	1	Kadamtala, Ward No. 13	22.88326N, 88.02701E	0.44	16610	0	Sep-25	0	16610	31025	33220	2195	31025	Jun-26	0.2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.83	Yes	Yes	Yes	Yes	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
31	HOWRAH	Uluberia	2	Banitala, Ward No. 31 (Beside NH 6) & Ward No. 6, Bauria	22.478330° N 88.078462°E & 22.499437° N 88.169112°E	6.50	28394	28394	Completed	3.00	105000	99400	133394	5600	127794	Jun-26	4.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.34	Yes	Yes	Yes	Yes	
32	HOWRAH	Bally	1	Chandmari	22.635658° N 88.334197°E	3.00	120000	30132.59	Dec-25	0.50	0	72400	120000	17467	102533	Sep-26	2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	6.60	Yes	Yes	Yes	Yes	After completion of 1st Phase, Phase-2 processing will be started after assessment of quantity
33	HOWRAH	Howrah MC	1	Belgachia	22°36'35"N 88°19'34"E	21.99	9,61,567	364026.87	Oct-26	1.80	750000	703200	1711567	644340	1067227	Dec-26	7.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	94.14	Yes	Yes	Yes	Yes	
34	JALPAIGURI	Jalpaiguri	1	Paharpur	26.564305° N 88.736121°E	2.50	25891.6	25892	Completed	2.50	160000	0	185891.6	160000	25892	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	10.22	Yes	No	No	No	
35	JHARGRAM	Jhargram	1	Jhargram (Near Jaralat)	22°26'36"N 86°58'29"E	12.00	3739	3739	Completed	4.00	10000	0	13739	10000	3739	Dec-26	4	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.76	No	NA	NA	NA	
36	KOLKATA	Kolkata MC	2	Garden Reach	Lat 22.530578° N Long 88.291576° E	19.77	1500000	10000	Mar-26	0.80	0	0	1500000	1490000	10000	Mar-27	2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	82.50	Yes	No	No	No	
				DHAPA Under W-58 OF BR-VII/KMC	22°32'32.6" N 88°25'17.6"E	60.00	4000000	1813000	Mar-26	25.00	2000000	0	6000000	4187000	1813000	Mar-27	8	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	330.00	Yes	No	No	No	
37	MALDA	English Bazar	1	English Bazar (muza Bahadurpur)	24°54'59.18" N 88°6'57.87"E	3.52	3250	3250	Completed	0.52	240000	0	243250	240000	3250	Dec-26	0.52	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	13.38	Yes	No	No	No	
38	MURSHIDABAD	Berhampore	1	Banappare ring road	Komolapur Khadamkhandi	2.16	123981	123981	Completed	1.00	190000	55600	313981	134400	179581	Oct-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	17.27	Yes	Yes	Yes	Yes	
39	MURSHIDABAD	Jangipur	1	Azgarpara near Milanpur	24°28'43.79" N 88°3'10.75"E	0.28	3211	3211	Completed	0.10	65180	0	68391	65180	3211	Oct-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.76	Yes	No	No	No	
40	MURSHIDABAD	Jiaganj-Azimganj	1	Ghoramari (Azimganj Side)	24°14'14.8" N 88°15'56.8" E	3.00	19426	19426	Completed	1.00	53000	0	72426	53000	19426	Oct-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.98	Yes	No	No	No	
41	MURSHIDABAD	Murshidabad	1	Kathgola bagan, Ward No. - 15	Kathgola bagan, Ward No. 15	5.38	94059	94059	Completed	1.00	62500	0	156559	62500	94059	Dec-26	2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.61	Yes	No	No	No	
42	MURSHIDABAD	Dhulian	1	Dhuliyan (near Malancha, Ratanpur)	24°39'29.89" N 87°55'50.74" E	2.00	0	0	0	0	60000	0	60000	60000	0	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.30	Yes	NA	NA	NA	
43	MURSHIDABAD	Kandi	1	Kandi (Jafadanga, Ward No. 12)	23°56'51.56" N 88°4'3.47"E	5.82	0	0	0	0	5000	0	5000	5000	0	July, 2026	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.28	Yes	NA	NA	NA	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
44	NADIA	Birnagar	1	Mathurapukur	23.268035° N 88.55683°E	3.00	6799	6799	Completed	3.00	0	0	6799	0	6799	Completed	3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.37	NA	NA	NA	NA	Total area recliamed
45	NADIA	Gayeshpur	2	1) Near VS Club, Ward No.-16 & Near SHG Training Centre, Ward No.- 15	22.955519° N 88.472313°E & 22.953232° N 88.48228°E	5.00	12465	12465	Completed	1.20	34400	0	46865	34400	12465	Sep-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.58	Yes	No	No	No	
46	NADIA	Kalyani	2	Near Kacharipara, Ward No.-6 & Beside highway, Ward No.-10	22.960863° N, 88.439684°E & 22.960863° N 88.439684°E	2.1 & 1.4	60543	60543	Completed	1.20	115000	32300	175543	82700	92843	Sep-26	1.2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.65	Yes	Yes	Yes	Yes	
47	NADIA	Krishnanagar	1	Godadanga, Ward – 5	(23.4052240 °N 88.5116291° E	8.00	51802	51802	Completed	3.00	412000	0	463802	412000	51802	Dec-26	3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	25.51	Yes	No	No	No	
48	NADIA	Nabadwip	1	Near Bishnupriya Halt Station, Ward No. – 1	23.4150386° N 88.3562766° E	12.35	83900	83900	Completed	5.00	111870	55750	195770	56120	139650	Jul-26	6	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	10.77	Yes	Yes	Yes	Yes	
49	NADIA	Ranaghat	1	Anulia GP	23.268035° N 88.55683°E	6.31	65374	65374	Completed	3.30	99750	0	165124	99750	65374	Dec-26	3.3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.08	Yes	No	No	No	
50	NADIA	Santipur	1	Moylar math, Ward no. – 10	23.2501021° N 88.4116394° E	4.55	22097	22097	Completed	2.20	86840	59125	108937	27715	81222	Oct-26	3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.99	Yes	Yes	Yes	Yes	
51	NADIA	Taherpur	1	Cremation Ground Road, Ward No.-1	23.270603° N 88.521961°E	1.26	6119	6119	Completed	0.50	14140	0	20259	14140	6119	Jul-26	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.11	Yes	No	No	No	
52	NADIA	Chakdah	1	Ward No - 19	23.062613N, 88.517296E	5.00	19426	19426	Completed	5.00	0	0	19426	0	19426	Completed	5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.07	NA	NA	NA	NA	Total area recliamed
53	NADIA	Cooper's Camp	1	Ward 2- near burning ghat	23.270603N, 88.521961E	0.50	19620	0	Dec-25	0	22860	0	42480	42480	0	Sep-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.34	Yes	No	No	No	
54	NORTH 24-PARGANAS	Barasat	1	Kadambagachi	22.70483°N 88.51908°E	3.50	67846.935	67847	Completed	3.50	0	0	67847	0	67847	Completed	3.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.73	NA	NA	NA	NA	Total area recliamed
55	NORTH 24-PARGANAS	Barrackpore	1	Kolkata Road	22.748542° N 88.382122°E	5.00	72846	72846	Completed	3.00	57812	14750	130658	43062	87596	Sep-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.19	Yes	Yes	Yes	Yes	
56	NORTH 24-PARGANAS	Basirhat	1	Ward 8	22.65254°N 88.87294°E	4.00	24273.065	24273	Completed	4.00	0	0	24273	0	24273	Completed	4	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.34	NA	NA	NA	NA	Total area recliamed

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
57	NORTH 24-PARGANAS	Bongaon	1	Beside Indira Park, Ward No. – 19 (opposite Truck Parking lot)	23°1'44.13" N 88°50'31.40" E	2.26	7013	7013	Completed	1.20	84832	0	91845	84832	7013	Nov-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.05	Yes	No	No	No	
58	NORTH 24-PARGANAS	Habra	1	Near Banipur Home, Ward No.-3	22.818064° N 88.635827°E	1.20	9458.1	9458	Completed	0.50	91700	0	101158.1	91700	9458	Oct-26	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.56	Yes	No	No	No	
59	NORTH 24-PARGANAS	Kanchrapara	1	Bidhanpally	23.4150386° N 88.3562766° E	3.00	24282	24282	Completed	1.20	136000	0	160282	136000	24282	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.82	Yes	No	No	No	
60	NORTH 24-PARGANAS	Khardah	1	Ruiyaiswaripur	22°44'31"N 88°24'25"E	2.75	46118	46118	Completed	1.00	38140	350	84258	37790	46468	Aug-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.63	Yes	Yes	Yes	Yes	
61	NORTH 24-PARGANAS	Madhyamgram	1	Digberia	22.69264° 88.50134°E	7.17	116068	116068	Completed	1.19	87700	1250	203768	86450	117318	Nov-26	1.19	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	11.21	Yes	Yes	Yes	Yes	
62	NORTH 24-PARGANAS	Panihati	1	Ramchandra Pur	22°41'31"N 88°23'10"E	1.50	51763.391	51763	Completed	0.20	120000	57256	171763.391	62744	109019	Jul-26	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.45	Yes	Yes	Yes	Yes	
63	NORTH 24-PARGANAS	Taki	1	Mansing road	22.57787°N 88.93308°E	0.80	3625	3625	Completed	0.35	13400	0	17025	13400	3625	Dec-26	0.35	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.94	Yes	No	No	No	
64	NORTH 24-PARGANAS	Titagarh	1	Mathpara	22.88326°N 88.02701°E	4.90	120886	120886	Completed	1.00	44716	0	165602	44716	120886	Dec-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.11	Yes	No	No	No	
65	NORTH 24-PARGANAS	Bhatpara	2	Madral & Jilabi Math	22.87426°N 88.41807°E & 22.85932°N 88.39001°E	2.57	58260	58260	Completed	1.00	71905	0	130165	71905	58260	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.16	Yes	No	No	No	
66	NORTH 24-PARGANAS	Garulia	1	Fanching Ground Road	22.817161° N 88.372613°E	1.80	52499	51991.017	Completed	1.00	38218	3050	90717	35676	55041	Oct-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.99	Yes	Yes	Yes	Yes	
67	NORTH 24-PARGANAS	Halisahar	1	Niraljan Trenching Ground	23.2501021° N 88.4116394° E	0.84	6799	6789	Completed	0.25	43905	19800	50704	24115	26589	Aug-26	0.25	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.79	Yes	Yes	Yes	Yes	
68	NORTH 24-PARGANAS	Bidhannagar MC	1	Mollar Bheri	22.35'52" N 88.26'47" E	55.00	300000	300000	Completed	55.00	0	0	300000	0	300000	Completed	55	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	16.50	NA	NA	NA	NA	Total area recliamed
69	NORTH 24-PARGANAS	Baranagar	1	Pramodnagar, Beside Belghoria Expressway	22.648657N, 88.397365E	22.68	845400	845400	Completed	2.00	1100000	710250	1945400	389750	1555650	Mar, 27	6	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	107.00	Yes	Yes	Yes	Yes	
70	NORTH 24-PARGANAS	Dum Dum																														
71	NORTH 24-PARGANAS	New Barrackpore																														
72	NORTH 24-PARGANAS	North Dum Dum																														

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
73	NORTH 24-PARGANAS	South Dum Dum																														
74	NORTH 24-PARGANAS	Kamarhati	1	Matagiri Harna Pally, Kamarhati	22.679309N, 88.379746E	8.00	50000	50000	Completed	0.50	900000	52950	950000	847050	102950	Dec-27	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	52.25	**Yes**	**Yes**	**Yes**	**Yes**	
75	NORTH 24-PARGANAS	Naihati	3	Along Patterson road, Chighat, W.No. 14, Naihati	22.897030N, 88.410584E	23.94	300000	300000	Completed	15.00	144000	94200	444000	49800	394200	Sep-26	15	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	24.42	**Yes**	**Yes**	**Yes**	**Yes**	
76	NORTH 24-PARGANAS	Ashoknagar-Kalyangarh	1	Ward 22 beside Naihati-Habra Road	22.50'21" N, 88.35'44 E	21.49	81585	41275	Dec-25	9.13	0	39050	81585	1260	80325	Jul-26	13	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.49	**NA**	**NA**	**NA**	**NA**	
77	NORTH 24-PARGANAS	Gobardanga	1	Ward 3- near Belluni bridge	22.52'49" N, 88.44'37 E"	4.00	19296	19296	Completed	3.50	0	0	19296	0	19296	Completed	3.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.06	**NA**	**NA**	**NA**	**NA**	Total area recliamed
78	PaSCHIM BARDHAMAN	Asansol MC	5	a.Asansol-Kalipahari, b.Burnpur-Hirapur, c.Raniganj- Ronai, d.Jamuria- 6 No. Bypass, e.Kulti- Aldi	a.23.614345°N;87.133207°E, b.23.661219°N; 86.939790°E, c.23.614345°N;87.133207°E, d.23.707714°N;87.074470°E, e.23.703844°N;86.883500°E	36.95	1100000	496284	Mar-26	11.00	700000	0	1800000	1303716	496284	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	99.00	**Yes**	**No**	**No**	**No**	After completion of 1st Phase, Phase-2 processing will be started
79	PaSCHIM BARDHAMAN	Durgapur MC	1	Sankarpur	23.530679° N 87.356380°E	6.60	300000	300000	Completed	3.00	730000	143280	1030000	586720	443280	Dec-26	3.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	56.65	**Yes**	**Yes**	**Yes**	**Yes**	
80	PASCHIM MEDINIPUR	Ghatal	1	Argora Shyampur	22.6636275° N 87.7241965° E	1.25	16038.41	16038	Completed	0.50	41520	0	57558.41	41520	16038	Dec-26	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.17	**Yes**	**No**	**No**	**No**	
81	PASCHIM MEDINIPUR	Kharagpur	1	Hiradih, Ward No. - 32	22.321856° 87.280617°E	1.50	29995.51	29996	Completed	1.50	50000	0	79995.51	50000	29996	Dec-26	1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	4.40	**No**	**NA**	**NA**	**NA**	
82	PASCHIM MEDINIPUR	Khirpai	1	Bhutdanga	22.706906° N 87.615709°E	2.00	693.34	693	Completed	1.00	9480	0	10173.34	9480	693	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.56	**Yes**	**No**	**No**	**No**	
83	PASCHIM MEDINIPUR	Midnapore	1	Dharma Dumping Ground, Hosnabad Mouuza	22.421732° N 87.340956°E	4.00	168814.31	168814	Completed	1.50	264000	99200	432814.31	164800	268014	Oct-26	2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	23.80	**Yes**	**Yes**	**Yes**	**Yes**	
84	PASCHIM MEDINIPUR	Chandrakona	1	Ransagar, Ward No - 02	22.7191N, 88.3800E	2.00	40902	40902	Completed	1.20	21720	0	62622	21720	40902	Nov-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.44	**Yes**	**No**	**No**	**No**	
85	PASCHIM MEDINIPUR	Kharar	2	Kharar ByPass Road	30.750526N, 76.640536E & 30.750528N, 76.640539E	0.57	2044	2044	Completed	0.30	0	0	2044	0	2044	Completed	0.3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.11	**NA**	**NA**	**NA**	**NA**	Total area recliamed

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
86	PASCHIM MEDINIPUR	Ramjibanpur	1	Bypass Road	22.824006N, 87.62073E	0.20	4611	4611	Completed	0.10	0	0	4611	0	4611	Completed	0.1	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.25	**NA**	**NA**	**NA**	**NA**	Total area recliamed
87	PURBA BARDHAMAN	Barddhaman	1	Kapilbagan	25°14'16.5" N 87°51'7.3"E	6.85	180825	180825	Completed	1.20	390000	105275	570825	284725	286100	Jun-26	3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	31.40	**Yes**	**Yes**	**Yes**	**Yes**	
88	PURBA BARDHAMAN	Gushkara	1	Ratani Kalitala	23.498347° N, 87.744647°E	2.00	7285	7285	Completed	0.50	54235	0	61520	54235	7285	Aug-26	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.38	**Yes**	**No**	**No**	**No**	
89	PURBA BARDHAMAN	Kalna	1	Beside Kalna Rail Station, kalayanpur Gram Payanchat Ambika Kalna	23.213381° N 88.353344°E	3.33	36850	36850	Completed	0.50	71900	0	108750	71900	36850	Mar-27	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	5.98	**Yes**	**No**	**No**	**No**	
90	PURBA BARDHAMAN	Katwa	1	Stadium Para, W-12	22.71923N, 88.38046E	2	3885	3885	Completed	1.00	67720	0	71605	67720	3885	Nov-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.94	**Yes**	**No**	**No**	**No**	
91	PURBA BARDHAMAN	Memari	1	Lock gate, Nudipur Bridge Memari Burdwan	Lock gate, Nudipur Bridge	2.50	38851	38851	Completed	1.25	28425	0	67276	28425	38851	Aug-26	1.25	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.70	**Yes**	**No**	**No**	**No**	
92	PURBA MIDNAPORE	Egra	1	Ramkrishnapur	22°23'58.04" N 87°45'19.13" E	0.32	2122.51	2123	Completed	0.12	41160	0	43282.51	41160	2123	Dec-26	0.12	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.38	**Yes**	**No**	**No**	**No**	
93	PURBA MIDNAPORE	Panskura	1	Panskura Railway Station	22°23'58.04" N 87°45'19.13" E	2.28	667.3	667	Completed	1.20	23840	12420	24507.3	11420	13087	Jul-26	1.3	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.35	**Yes**	**Yes**	**Yes**	**Yes**	
94	PURBA MIDNAPORE	Tamralipta	1	Malia Bari	22°16'6"N 87°55'48"E	0.49	23890.48	23890	Completed	0.20	28720	27750	52610.48	970	51640	Aug-26	0.2	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.89	**Yes**	**Yes**	**Yes**	**Yes**	
95	PURBA MIDNAPORE	Contai	1	Contai Digha Road	21.765423N, 87.730407E	4.59	62385	62385	Completed	2.00	98000	0	160385	98000	62385	Nov-26	1.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	8.82	**Yes**	**No**	**No**	**No**	
96	PURULIA	Purulia	3	a.Chharra, b.Banga Bari Samsan, c.Hutmura	a.23.3753°N 86.42805°E, b.23.34977° N 86.38601°E, c.23.3495°N 86.4992°E	10.83	77325	77325	Completed	4.00	119800	0	197125	119800	77325	Dec-26	4	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	10.84	**Yes**	**No**	**No**	**No**	
97	PURULIA	Raghunathpur	3	a.W–2 (Between Lohar & Mondal Petrol Pump), b.W-7 (beside Gara Kiari Mandir), c.W -11 (Stadium More)	a.23.53709° N 86.6746°E, b.23.52927° N 86.6763°E, c.23.52928° N 86.6763°E	1.00	8201	8201	Completed	0.50	27960	0	36161	27960	8201	Nov-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.99	**Yes**	**No**	**No**	**No**	

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
98	PURULIA	Jhalda	3	a.Beside Panagarh-Moregram SH. bPat Jhalda Road Railway Cabin Side, c.Ward 5	a.23.361579 °N 85.971785°E , b.23.37796N , 85.98471E, c.23.34956N , 85.97531E	2.00	16318.43	16318	Completed	0.50	0	0	16318	0	16318	Completed	0.5	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.90	**NA**	**NA**	**NA**	**NA**	Total area recliamed
99	SOUTH 24-PARGANAS	Baruipur	1	Kritankhola	22°20'14"N 88°26'49"E	2.30	19685	19685	Completed	1.20	113000	0	132685	113000	19685	Oct-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	7.30	**Yes**	**No**	**No**	**No**	
100	SOUTH 24-PARGANAS	Budge Budge	1	Subhas Udyan trenching ground Ward No. - 17	22.47335°N 88.18879°E	3.48	20721	20721	Completed	2.20	41100	0	61821	41100	20721	Oct-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.40	**Yes**	**No**	**No**	**No**	
101	SOUTH 24-PARGANAS	Diamond Harbour	1	Doloanghata, Beside NH 117 (Panchayet Area)	22°10'17"N 88°13'44"E	2.00	9421.092	9421	Completed	0.50	34710	0	44131.092	34710	9421	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	2.43	**Yes**	**No**	**No**	**No**	
102	SOUTH 24-PARGANAS	Jaynagar-Mazilpur	1	Shahajadpur	22°10'85"N 88°26'2"E	4.00	1379	1379	Completed	1.00	21140	0	22519	21140	1379	Apr-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.24	**Yes**	**No**	**No**	**No**	
103	SOUTH 24-PARGANAS	Maheshtala	1	Sarengabad, Ward No. – 35	22.49216°N 88.20567°E	19.61	230517	230517	Completed	4.00	104000	34300	334517	69700	264817	Dec-26	6	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	18.40	**Yes**	**Yes**	**Yes**	**Yes**	
104	SOUTH 24-PARGANAS	Rajpur-Sonarpur	1	Mailapota	22°25'16"N 88°25'37"E	10.00	18511.329	18511	Completed	2.00	4223	0	22734.329	4223	18511	Jun-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.25	**Yes**	**No**	**No**	**No**	
105	UTTAR DINAJPUR	Dalkhola	1	Uttar Dalkhola	25°53'6.6"N 87°50'26.1"E	0.68	7375	7375	Completed	0.68	28550	0	35925	28550	7375	Sep-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.98	**Yes**	**No**	**No**	**No**	
106	UTTAR DINAJPUR	Islampur	1	Sonakhoda Gurujbasti Trenching Ground; Ward No. – 9	26°15'32.5" N 88°12'13.1" E	0.17	1469	1469	Completed	0.10	24570	0	26039	24570	1469	Oct-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	1.43	**Yes**	**No**	**No**	**No**	
107	UTTAR DINAJPUR	Kaliaganj	1	Mahadebpur, Ward No. - 17)	25°38'25.6" N 88°18'26.6"E	2.84	28144	28144	Completed	1.00	33930	0	62074	33930	28144	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.41	**Yes**	**No**	**No**	**No**	
108	UTTAR DINAJPUR	Raiganj	1	Bandar Sashan, Ward No. – 22	25°36'31"N 88°7'0.9"E	3.00	38429.02	38429	Completed	1.00	141665	0	180094.02	141665	38429	Mar-27	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	9.91	**Yes**	**No**	**No**	**No**	
109	DARJEELING	Darjeeling	1	Darjeeling (Near Gorkha Road and Victoria Road)	27° 2'26.60"N 88°15'33.05" E	3.33	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	**NA**	**NA**	**NA**	**NA**	As legacy waste is lying in the slope so no technology could be adopted to process the same
110	DARJEELING	Kurseong	1	Kurseong (Down Hill from Pankhabari Road)	26°51'53.26" N 88°15'56.05" E	5.00	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	**NA**	**NA**	**NA**	**NA**	As legacy waste is lying in the slope so no technology could be adopted to process the same
111	DARJEELING	Mirik	1	Mirik Notified Area (Near DP Rai Road)	26°52'59.28" N 88°10'12.35" E	4.00	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	**NA**	**NA**	**NA**	**NA**	As legacy waste is lying in the slope so no technology could be adopted to process the same

Sl No	District	ULB	No. of Legacy waste sites	Location of site	GPS coordinate (Lat & Long)	Phase-I Area of Dump Site (in acre)	P-I Quantity of Waste in each site (MT)	P-I Quantity of legacy waste processed upto (MT)	P-I Timeline to complete processing at each site	P-I Area Reclaimed (in Acre)	Phase-II Quantity of Waste in each site (MT)	P-II Quantity of legacy waste processed upto (MT)	P-I + P-II Total Quantity of Waste in each site (MT)	Total Quantity of Legacy Waste to be processed (MT)	P-I + P-II Total Quantity of legacy waste processed (MT)	P-I +P-II Timeline to complete processing at each site	Area Reclaimed (in Acre)	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Process adopted to remidiate at each site	Inert (%) (Construction Waste, Wood, Glass etc)	Compost (%) organic.	RDF (%) Plastic	If any Other material (%)	Earmarked Budget (Rs. In Crore)	P-II RfP prepared for engagement of agency for processing (Y/N)	P-II Tender floated (Y/N)	P-II Work order issued to Agency for processing (Y/N)	P-II Processing Work Started (Y/N)	Remarks
112	KALIMPONG	Kalimpong	1	Kalimpong (near BhalulhopKhasmahal)	27° 5'24.23"N 88°28'39.82" E	8.25	0	0		0	0	0	0	0	0	0	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.00	**NA**	**NA**	**NA**	**NA**	As legacy waste is lying in the slope so no technology could be adopted to process the same
113	Malda	Old Malda	1	Near Fata Kesta Club, School para Mongolbari, Ward No-09	23.0172470° "N 88.1457094° E	0.5	0	0	NA		57200	0	57200	57200	0	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.15	**Yes**	**No**	**No**	**No**	
114	Murshidabad	Beldanga	1	Bagdanga math, Mouza-Maniknagar, J.L no.-54, P.S-Beldanga, Dist-Murshidabad	23.93300, 88.30323	2.05					57761	0	57761	57761	0	Dec-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	3.18	**Yes**	**No**	**No**	**No**	
115	Pur Burdwan	Dainhat	1	Ganga Rasta, Ward-02	23.614199°" N 88.17797°E	0.75					17960	0	17960	17960	0	Nov-26	0	35 - 45 %	30 - 40 %	5 - 15 %	10 - 20 %	Biomining and Bio Remediation	Low land filling	Low land filling & used as soil enricher in cultivation	Cement Plants of other states	Moisture Loss and other handling Loss	0.99	**Yes**	**No**	**No**	**No**	
TOTAL			**126**			**694.82**	13930062.71	**8389591.18**		**264.02**	**13960757.00**	**3148291.00**	**27890819.71**	**16352937.52**	**11537882.18**		**248.41**										**1534.00**					

**** No Dumpsite Present at 13 ULBs i.e. Haldia, Pujali, Domkal, Falakata, Bishnupur, Mekhliganj, Buniadpur, Dhupguri, Mal, Maynaguri, Haringhata, Baduria, North Barrackpore,**

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
1	Bankura	Bankura	**5.67**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
2	Bankura	Bishnupur	**2.8**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
3	Bankura	Sonamukhi	**1.41**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
4	Paschim Burdwan	Asansol MC	**47.7**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
5	Purba Burdwan	Barddhaman	**12.98**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
6	Purba Burdwan	Dainhat	**1.01**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
7	Paschim Burdwan	Durgapur MC	**23.37**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
8	Purba Burdwan	Gushkara	**1.46**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
9	Purba Burdwan	Kalna	**2.34**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
10	Purba Burdwan	Katwa	**3.95**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
11	Purba Burdwan	Memari	**1.71**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
12	Birbhum	Bolpur	**3.31**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
13	Birbhum	Dubrajpur	**1.57**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
14	Birbhum	Nalhati	**1.7**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
15	Birbhum	Rampurhat	**2.39**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
16	Birbhum	Sainthia	**1.84**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
17	Birbhum	Suri	**3.73**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
18	Cooch Behar	Cooch Behar	**3.21**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
19	Cooch Behar	Dinhata	**1.49**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
20	Cooch Behar	Haldibari	**0.59**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
21	Cooch Behar	Mathabhanga	**0.99**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
22	Cooch Behar	Mekhliganj	**0.38**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
23	Cooch Behar	Tufanganj	**0.87**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
24	Dakshin Dinajpur	Balurghat	**6.24**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
25	Dakshin Dinajpur	Buniadpur	**1.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
26	Dakshin Dinajpur	Gangarampore	**2.32**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
27	Darjeeling	Darjeeling	**4.97**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
28	Kalimpong	Kalimpong	**2.04**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
29	Darjeeling	Kurseong	**1.75**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
30	Darjeeling	Mirik	**0.47**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
	Darjeeling	Siliguri MC	**21.17**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
32	Howrah	Uluberia	**10.85**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
33	Hooghly	Arambagh	**2.73**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
34	Hooghly	Baidyabati	**7**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
35	Hooghly	Bansberia	**6**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
36	Hooghly	Bhadreswar	**5.58**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
37	Hooghly	Champdany	**6**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
38	Hooghly	Chandannagore MC	**9.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
39	Hooghly	Dankuni	**3.92**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
40	Hooghly	Hooghly Chinsurah	**9.63**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
41	Hooghly	Konnagar	**3.85**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
42	Hooghly	Rishra	**5.89**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
43	Hooghly	Serampore	**7.68**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
44	Hooghly	Tarakeswar	**1.28**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
45	Hooghly	Uttarpara Kotrung	**6.89**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
46	Alipurduar	Alipurduar	**2.69**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
47	Jalpaiguri	Dhupguri	**1.84**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
48	Jalpaiguri	Jalpaiguri	**4.43**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
49	Jalpaiguri	Mal	**1.04**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
50	Malda	English Bazar	**8.48**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
51	Malda	Old Malda	**3.47**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
52	Murshidabad	Beldanga	**1.2**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
53	Murshidabad	Berhampore	**7.9**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
54	Murshidabad	Dhuliyan	**4.36**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
55	Murshidabad	Domkal	**5.03**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
56	Murshidabad	Jangipur	**4.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
57	Murshidabad	Jiaganj-Azimganj	**1.75**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
58	Murshidabad	Kandi	**2.29**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
59	Murshidabad	Murshidabad	**2.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
60	Nadia	Birnagar	**1.27**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
61	Nadia	Chakdah	**4.86**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
62	Nadia	Cooper's Camp	**0.78**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
63	Nadia	Gayeshpur	**3.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
64	Nadia	Haringhata	**1.9**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
65	Nadia	Kalyani	**5.15**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
66	Nadia	Krishnanagar	**8.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
67	Nadia	Nabadwip	**6.75**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
68	Nadia	Ranaghat	**3.11**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
69	Nadia	Santipur	**6.26**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
70	Nadia	Taherpur	**0.86**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
71	North 24 Parganas	Ashokenagar-Kalyangarh	**5.02**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
72	North 24 Parganas	Baduria	**2.17**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
73	North 24 Parganas	Baranagar	**10.12**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
74	North 24 Parganas	Barasat	**11.49**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
75	North 24 Parganas	Barrackpore	**6.3**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
76	North 24 Parganas	Basirhat	**5.16**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
77	North 24 Parganas	Bhatpara	**15.92**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
78	North 24 Parganas	Bidhan Nagar MC	**26.16**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
79	North 24 Parganas	Bongaon	**4.49**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
80	North 24 Parganas	Dum Dum	**4.73**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
81	North 24 Parganas	Garulia	**2.43**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
82	North 24 Parganas	Gobardanga	**1.87**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
83	North 24 Parganas	Habra	**6.07**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
84	North 24 Parganas	Halisahar	**5.15**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
85	North 24 Parganas	Kamarhati	**13.66**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
86	North 24 Parganas	Kanchrapara	**5.35**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
87	North 24 Parganas	Khardah	**4.48**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
88	North 24 Parganas	Madhyamgram	**8.09**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
89	North 24 Parganas	Naihati	**9**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
90	North 24 Parganas	New Barrackpore	**3.17**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
91	North 24 Parganas	North Barrackpore	**5.48**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
92	North 24 Parganas	North Dum Dum	**10.29**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
93	North 24 Parganas	Panihati	**15.57**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
94	North 24 Parganas	South Dum Dum	**16.64**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
95	North 24 Parganas	Taki	**1.58**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
96	North 24 Parganas	Titagarh	**4.81**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
97	Paschim Midnapore	Chandrakona	**0.97**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
98	Paschim Midnapore	Ghatal	**2.25**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
99	Jhargram	Jhargram	**2.54**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
100	Paschim Midnapore	Kharagpur	**8.56**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
101	Paschim Midnapore	Kharar	**0.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
102	Paschim Midnapore	Khirpai	**0.68**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
103	Paschim Midnapore	Midnapore	**6.98**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
104	Paschim Midnapore	Ramjibanpur	**0.81**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
105	Purba Midnapore	Contai	**3.8**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
106	Purba Midnapore	Egra	**1.24**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
107	Purba Midnapore	Haldia	**8.28**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
108	Purba Midnapore	Panskura	**2.39**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
109	Purba Midnapore	Tamluk	**2.69**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
110	Jhalda	Jhalda	**0.81**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
111	Purulia	Purulia	**4.99**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
112	Purulia	Raghunathpur	**1.06**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
113	South 24 parganas	Baruipur	**2.19**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
114	South 24 parganas	Budge Budge	**3.17**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
115	South 24 parganas	Diamond Harbour	**1.78**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
116	South 24 parganas	Jainagar-Mazilpur	**1.07**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
117	South 24 parganas	Maheshtala	**18.54**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
118	South 24 parganas	Pujali	**1.53**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
119	South 24 parganas	Rajpur-Sonarpur	**17.48**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
120	Uttar Dinajpur	Dalkhola	**1.53**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
121	Uttar Dinajpur	Islampur	**2.24**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
122	Uttar Dinajpur	Kaliaganj	**2.21**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
123	Uttar Dinajpur	Raiganj	**7.57**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
124	Howrah	Howrah MC	**44.16**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.

Status of Construction and demolition waste management of 128 ULBs of West Bengal up to February, 2026					
Sl No	**District**	**ULB**	**Total per day generation of C&D waste (TPD)**	**The detail of plant established for the treatment of C&D waste including the existing capacity and capacity utilization**	**Remarks**
125	Howrah	Bally	**12.04**	**0**	Segregated fractions are being sold and reused and the remaining are being disposed at KMC plant for processing.
126	Jalpaiguri	Maynaguri	**1.5**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
127	Alipurduar	Falakata	**2.23**	**0**	Segregated fractions are being sold and reused and it is planned that remaining to be processed in Cluster mode. Identification of land for the plant is under process.
128	Kolkata	Kolkata MC	**245.65**	**500**	
		Total =	965.79	500	

National Mission for Clean Ganga
Monthly Progress Report in the NGT Matter OA No. 673 of 2018
(In compliance to NGT order dated 24.09.2020)
The Kolkata Municipal Corporation
Reporting Month: February 2026 Version: 20260318R0(Draft)

1. Details of each existing STP

No.	Location	Existing STP Capacity	Capacity Being Utilized	Operational Status of STP	Compliance Status of STP
A	B	C	D	E	F
1	Bangur (22.60561, 88.41498)	52	26	Operational	Complied
2	Garden Reach (22.52186, 88.28669)	57	53.68	Operational (Under Rejuvenation)	Complied
3	Keorapukur (22.46849, 88.33192)	45	36	Operational (Under Rejuvenation)	Complied
4	Baghajatin (22.48072, 88.39004)	15	14.25	Operational	Complied
5	Hatisur (22.51866, 88.39340)	10	8	Operational	Complied

2. Details of under construction STPs

No.	Location	Capacity of the plant in MLD	Physical Progress in % a. Overall % b. Components completed in the current month.	Status of I&D or House sewer connections	Completion Timeline
A	B	C	D	E	F
1	Near WBSETCL, Joka (22.4496,88.2982)	45	a. 70.04 % b. Piling work for all units completed. Construction of super structure under progress.	The sewage network at the 03 nos. STPs under KEIIP are being developed under respective works. Trunk sewers are being laid. S&D network to be completed by 2025. Approximately Rs. 1800cr. For S&D works. Out of this, about 1500 cr. linked for development of the trunk S&D system within the catchment areas of the 3 STPs and remaining indirectly linked for the abatement of pollution to the River Ganga in other areas. Out of 1500 cr. about **1342** cr. has been disbursed.	August, 2026
2	At Bank Plot, M.G Road(22.4583,88.3130)	40	a. 77.6% b. Piling work for all units completed. Construction of super structure under progress.		August, 2026

No.	Location	Capacity of the plant in MLD	Physical Progress in % a. Overall % b. Components completed in the current month.	Status of I&D or House sewer connections	Completion Timeline
3	Rajpur-Sonarpur, Rania (22.4492,88.3504)	23	a. 99 % b. Trial run in process	Laying of S&D lines including construction of pumping stations in ward 127, part of ward 142 and part of ward 143 are considered in new project under KMC-SHARP which will be funded by ADB. Considering the contribution of the aforesaid areas STPs are being constructed under ongoing KEIIP. LOA for development of trunk S&D network for few packages has been issued and work commence soon. Time line for balance work not within the present scope under KEIIP & KMC - SHARP will be considered in KMC-SHARP Phase 2. (Part of ward 127, 142, 125,126, 143 &144). The Preliminary Project Report (PPR) for KMC-SHARP Phase 2 is submitted to the Government of West Bengal (GoWB) for approval. Upon receiving approval, the report will be forwarded to the Department of Economic Affairs (DEA), GoI for consideration of external financing assistance.	March, 2026
4	Bansdroni STP	11.6	a. 2.18% b. Survey work and soil testing completed for STP and allied SPSs, BEP and Hydraulic design is in Progress.	Letter of Acceptance (LoA) has been issued by KMC to the L1 bidder viz. M/s EMS Limited– M/s Neercare India Private Limited (JV) at a total cost of Rs. 781.98 Crore on 23.06.2025. The agency has submitted the Performance Bank Guarantees and ESHS Bank Guarantees which have been vetted by the respective Banks. The Agreement has been executed on 30.07.2025. Mobilization Advance amounting to Rs. 29.67 Crore has	August 2028 +15years O&M
5	STP Near Golf Garden, Sukhapukur (22.49851, 88.35096)	3.5	a. 0% b. Survey work in progress.		

No.	Location	Capacity of the plant in MLD	Physical Progress in % a. Overall % b. Components completed in the current month.	Status of I&D or House sewer connections	Completion Timeline
6	Birji Road STP near SahidKhudiram Metro (22.46576, 88.38884)	10	a. 2.18% b. Survey work and soil testing completed for STP and allied SPSs, BEP and Hydraulic design is in Progress.	been paid to M/s GR Sewage Treatment Plant Pvt. Ltd.	
7	New STP at Garden Reach	65	a. 62.85% b. 100% completion of Earthwork, PCC, pile work, pile cap & Tie beam. Decanter and Diffuser has been supplied at site.	Effective Date for the instant Project: 21.10.2024. Mobilization Advance amounting to Rs. 15.93 Crore has been paid to M/s GR Sewage Treatment Plant Pvt. Ltd.	October 2026 +15years O&M
8	Additional capacity at existing Keorapukur STP	5	a. 2.2% b. Survey work in progress.	Rehabilitation of Existing 50MLD STP along with associated infrastructure at Keorapukur, Kolkata, WB. LoA issued to M/s TEPL-GSJ (JV) on 24/09/2025. I&D or House Service Connection not considered under this rehabilitation project.	12months + 03months trial run + 15years O&M

3. Details of proposed STPs

No.	Location	Capacity of the STP proposed in MLD	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
A	B	C	D	E
1	STP Near Badartala	15	The Preliminary Project Report (PPR) for KMC-SHARP Phase 2 is submitted to the Government of West Bengal (GoWB) for approval. Upon receiving approval, the report will be forwarded to the Department of Economic Affairs (DEA), GoI for consideration of external financing assistance.	Time line to be finalized based on the approval of the project from GOI.
2	STP Near BhangaKhal, Gardenreach area (22.54118, 88.25155)	45		
3	New Baghajatin STP	26		
4	Hossianpur STP	41	It has been taken up under KMC-SHARP. Tender document for the said STP has been prepared.	Tender to be floated by March, 2026
5	New Keorapukur STP	25	Sent to 15th Finance Commission, Tripartite MOU already signed.	NA
6	Strand Road STP	23	Sent to 15th Finance Commission, Tripartite MOU already signed. The land area is under KOPT. The requisition for land allotment for STP has been send to KOPT (Kolkata Port Trust). Land allotment is pending.	NA

4. Drain details:

River name	No. of drains falling in the river	No. of drains having floating racks/screens installed to prevent solid waste from falling into the river
A	B	C
Ganga	Dhankheti Khal	1*
	Tolly's Nullah	1#
	Nimtala Burning Ghat Drain	0
	Cossipore Ghat Drain	0
	Chitpur Ghat Khal/ Circular Canal	0

*****Dhankheti Khal is guarded with 3bar screens at different locations to arrest the floating materials for the ease of removing the same from reaching to the River.

Tolly's Nullah is guarded with 8 floating garbage arrester nets at different locations to arrest the floating materials for the ease of removing the same from reaching to the River.

5. Alternate treatment details:

Bio/ Phyto remediation is not feasible as the drains are under tidal effect.

River name	Polluting drain	In-situ treatment details	MLD treated	Details of parameters before treatment	Details of parameters after treatment
				DO: BOD: TC: FC:	DO: BOD: TC: FC:

6. Reuse of treated water

Total sewage generation in Kolkata is 1400 MLD. Approx. out of which major portion (910 MLD. approx i.e.65% of total sewage generation) is being naturally treated and used at EKW for pisciculture, mixed farming and animal husbandry etc.
Now, KMC has 5 STP which are in operation, having capacity of 179 MLD i.e. 12.8% of the total generated sewage for which provision for reuse of treated water is being considered and is expected to be completed by next financial year.
For upcoming and ongoing projects of STP having capacity upto 146 MLD (108 MLD from 3 STPs under construction by KEIIP, 25 MLD from upcoming project under TollysNullah is sanctioned and 8 MLD +5MLD additional capacity at Garden Reach STP& Keorapukur STP) i.e., 10% of the total generated sewage, provision will be made for reuse of treated water.

Location of STP/Alternate Treatment	MLD of treated water generated	Details of the reused water
Treatment through East Kolkata Wetland	NA 910MLD of raw sewage is reused	The majority of the sewage from the core inner city area - about 910 MLD in magnitude receives natural treatment as it passes through the East Kolkata Wetlands - an extensive fishery to the East of the city before discharging the same to Kulti River.

Treatment through East Kolkata Wetland (EKW)
The City of Kolkata is surrounded by a huge low-lying marshy land & fisheries called East Kolkata Wetland (EKW) on the East which is fed by a number of water channels carrying and discharging City waste water (dry weather flow & storm water flow) in the Kulti-Vidyadhari river after natural treatment-sedimentation, oxidation.
EKW has been recognized as Ramsar site. Excerpts from Information Sheet on Ramsar Wetlands can be quoted as below:

"The wetlands to the east of Calcutta are well known over the world for their multiple uses. The resource recovery systems developed by the local people through ages using wastewater from the city is the largest in the world. In the process it treats the wastewater and has saved the city of Calcutta from constructing and maintaining a wastewater treatment plant."
"The East Calcutta wetland is an urban facility for treating the Calcutta city's waste water and for utilizing the treated water for pisciculture and agriculture, through recovery of waste water nutrients in an efficient manner. In the wetland to the east of Calcutta, wastewater is used in fisheries and agriculture covering an area of about 12,500 hectares which has been designated as conservation area by an order of the Calcutta High Court.
In the fish ponds covering about 4000 hectares, city's wastewater is made to flow through. The wastewater ponds act basically as solar reactors and complete most of their bio-chemical reactions with the help of solar energy. The wetland ecosystem of the east Calcutta is thus one of the rare examples of environmental protection and development management where a complex ecological process has been adopted by the local farmers by mastering the resource recovery activities."
Ref: https://rsis.ramsar.org/RISapp/files/RISrep/IN1208RIS.pdf

7. Ground Water Regulation

River	Ground water regulation details
A	B
Ganga Vidyadhari	Ground Water Regulation is already in practice and is dealt by State Water & Investigation Directorate (SWID) for the entire state under Water Resources Investigation & Development Department (WRI&DD). Assessment of ground water resource at KMC area is checked periodically by State Water & Investigation Directorate (SWID). For extraction of ground water, case to case basis application is obtained by SWID and merit of such application is judged by an expert committee as per The West Bengal Ground Water Resources (Management, Control and Regulation) Act, 2005 which is called Corporation Level Authority (CLA) comprising of the following members: i) The Municipal Commissioner of the Corporation : Chairman ii) The Chief Executive Officer, Kolkata Metropolitan Development Authority : Member iii) Superintendent Geologist, State Water & Investigation Directorate, Government of West Bengal: Member Secretary. iv) Two elected representatives of the Kolkata Municipal Corporation, to be nominated by the Mayor, Kolkata Municipal Corporation : Members v) One expert from the Central Ground Water Board as may be nominated by the Regional Director, Central Ground Water Board : Member vi) Two experts in the field of conservation, protection or development of ground water resources as the State Government may, by notification appoint. : Members vii) Two eminent persons of the locality as the State Government may, by notification appoint. : Member viii) One representative of the Public Health Engineering Directorate, Government of West Bengal : Member ix) One representative of the State Pollution Control Board : Member Only on recommendation of such committee and subsequent permission from State Water & Investigation Directorate (SWID) ground water extraction is allowed. After completion of these formalities KMC issues license for tube well boring. The above procedure is being maintained as a continuous process.

8. Good irrigation practices

River	Details of adopting good irrigation practices
NA	NA

9. Rain water harvesting

River	Details of rain water harvesting
A	B
Ganga Vidyadhari	Rain Water Harvesting in already incorporated in Building Rule 2009 which is as follows: Rule-144 Rain Water Harvesting and Tree Cover Rain Water Harvesting (RWH), RWH shall form a part the building and shall have to be included in the plan, either for direct use of the rain water or for ground water recharging or both, in case of (i) New building or buildings or any housing complex as per Environment Impact Assessment Guideline issued by State Government/ Government of India. (ii) Expansion of any existing building or buildings or housing complex, as per Environment Impact Assessment Guideline issued by State Government/ Government of India. This system shall comply with Central & State statutory requirements laid down in the relevant Acts & by-laws. It is implemented for the buildings on area exceeding 20,000Sqm

10. Demarcation of Floodplain and removal of illegal encroachments

River	Details of demarcation of floodplain and removal of illegal encroachments
NA	NA

11. Maintaining minimum e-flow of river

River	Maintaining minimum flow of the river
NA	NA

12. Plantation activities

River	Details of plantation activities along the river
A	B
Ganga Vidyadhari	Total Plantation made during: 2020-21, 2021-22 = 28,000nos. **February 2026** Road side plantation - 0 Plantation of Shrubs - 126262 Cumulative Figure Road side plantation- 105238 Plantation of Shrubs- 389897

13. Development of biodiversity park

Details of setting up biodiversity parks on flood plains by removing encroachment along the river

1. Dr. Anupama Mitra, Expert Member of the Committee of the West Bengal Bio-Diversity Board has been engaged vide letter dated 07/11/2022 and same has been communicated through Affidavit to HNGT in the matter of OA-20/2022/EZ.
2. For availability of land KMC has approached to Army Authority, Eastern Railway and SMP-Kolkata for identification of land for setting up of Bio-diversity park.
3. SMP-Kolkata has informed that there is no availability of land and the same has been communicated through Affidavit in the matter of OA-20/2022/EZ of HNGT. Army Authority had informed that NoC will be issued for the purpose as and when land is identified.
4. A Model DPR regarding setting up of Bio-Diversity Park has been obtained by KMC from West Bengal Bio-Diversity Board.

WEST BENGAL POLLUTION CONTROL BOARD

Water Quality of Polluted River stretches of 11 rivers in West Bengal during February, 2026

Priority	River	Stations	pH (Unit)	(DO) (mg/l)	BOD (mg/l)	Total Coliform (MPN/100ml)	Fecal Coliform (MPN/ 100ml)	Fecal Streptococci (MPN/100ml)
I	Mahananda	Siliguri (Upstream)	7.1	7.3	2.1	11000	2300	39
		Ramghat(Downstream)	6.96	5.2	3.8	220000	170000	2700
III	Vidyadhari	Haroa bridge (upstream)	7.53	NIL	16.67	110000	49000	1300
		Malancha (downstream)	7.63	NIL	12.5	23000	17000	940
III	Churni/Matha Bhanga	Downstream of Ranaghat town	7.3	3.9	3.71	24000	13000	700
		Majhdia	7.29	Nil	4.21	7000	3300	210
		Gobindapur	7.14	Nil	4.67	13000	4900	790
IV	Karola	Downstream of Jalpaiguri	7.2	8.5	1.9	7900	2700	33
IV	Dwarka	Upstream of Tarapith at Sadhak Bamdeb ghat	7.85	7.1	3.65	79000	34000	46
		Downstream of Tarapith Satighat	7.8	7.9	3.45	130000	79000	40
V	Ganga	Farakka	7.17	8.5	2.7	1300	330	130
		Farakka	7.14	8	2.4	1100	330	78
		Khagra	7.04	8.8	2.6	4900	2300	170
		Khagra	7.29	8.2	1.95	4600	1100	230
		Baharampore	7.14	8.9	2.65	14000	4600	310
		Baharampore	7.07	8.2	1.9	13000	4900	490
		Gorabazar	7.29	8.7	2.5	9400	3300	330
		Gorabazar	7.14	8.3	2.1	14000	4600	460
		Nabadip	7.3	8.3	2.6	4600	1700	330
		Nabadip	7.21	8.3	2.8	4900	2200	330
		Tribeni	7.14	8	2.75	4900	1700	230
		Tribeni	7.36	8.5	2.7	3300	1300	130
		Palta Shitalatala	7.29	8.5	2.9	7000	3300	310
		Palta Shitalatala	7.14	7.8	2.4	7900	2300	230
		Palta,	7.11	8.6	2.7	9400	2300	330
		Palta	7.2	8.2	2	13000	3300	310
		Serampore	7.07	8.7	2.8	49000	13000	1100
		Serampore	7.03	8	2.1	70000	24000	1300
		Dakshmineswar	7.88	8	2.6	79000	33000	1400
		Dakshmineswar	7.69	6.2	2.8	70000	13000	330
		Garden reach	7.93	8.4	2.9	110000	79000	2200
		Garden reach	7.61	5.6	2.95	94000	33000	700
		Howrah-shivpur	7.96	8.1	2.85	49000	23000	1100
		Howrah-shivpur	7.69	7.3	2.65	79000	27000	460
		Uluberia,	7.61	8.3	2.8	24000	13000	78
		Uluberia,	7.38	5.5	2.9	17000	9400	130
		Durgachak near Pathikhali,	7.88	5.8	1.8	28000	17000	330
		Durgachak near Pathikhali,	7.78	7.3	1.85	13000	7000	490
		Diamond harbour,	7.54	6.2	2.75	790	490	20
		Diamond harbour,	7.64	5.8	2.85	3300	1100	78

Water Quality of Polluted River stretches of 11 rivers in West Bengal during February, 2026

Priority	River	Stations	pH (Unit)	(DO) (mg/l)	BOD (mg/l)	Total Coliform (MPN/100ml)	Fecal Coliform (MPN/ 100ml)	Fecal Streptococci (MPN/100ml)
V	JALANGI.	Downstream of Krishnanagar	7.1	8.4	2.9	7000	3300	490
V	Damodar	Dishergarh	7.7	8.7	2.1	7900	3300	34
		IISCO near Dhenna Village	7.85	8.9	2.2	3300	1700	26
		Narainpur	8.01	8.5	1.8	2300	1100	21
		Near Mujher Mana Village	7.4	8	3.5	26000	13000	46
		Andal D/s	7.95	8.4	2.7	1300	1100	11
		Andal U/s	7.98	8.3	2.4	1100	780	11
		Asansol U/s	7.78	8.4	2.8	2700	1700	22
		Durgapur U/s	7.9	8.7	2.6	1400	680	13
		Raniganj D/s	7.75	8.5	2.4	1300	780	14
		Water intake point for Burdwan Town	7.8	8.5	2.8	780	450	13
V	Dwarakeshwar	Bankura town	7.73	8.5	2.5	22000	13000	32
V	Silabati	Ghatal (Downstream)	7.71	7.2	2.15	14000	4900	220
V	Jaldhaka	At Dhupguri	7.05	8.5	1.4	7000	2100	27

WEST BENGAL POLLUTION CONTROL BOARD

The following four rivers have been removed from this list of polluted River stretches based on improvement in water quality in 2025.

Priority	River	Stations	pH (Unit)	(DO) (mg/l)	BOD (mg/l)	Total Coliform (MPN/ 100ml)	Fecal Coliform (MPN/100ml)	Fecal streptococci (MPN/100ml)
Delisted	KANSI	Downstream at Midnapore	7.67	8	1.6	14000	7000	240
	Barakar	Asansol	7.53	8.2	2.55	4000	2600	14
	Rupnarayan	Geonkhali	7.58	7.5	2.85	11000	7900	240
		Kolaghat (Down Stream)	7.86	5.9	2.9	7000	3300	210
	Teesta	At Jalpesh	7.65	7.5	1	4700	1700	17
		At Sevoke	7.2	8.6	2	4700	1400	14
	Mayurakshi	Suri Town	*7.93*	*9.1*	*1.55*	*2600*	*1700*	*14*
	Kaljani	Downstream of Alipurduar	*7.48*	*7.5*	*1.5*	*17000*	*8000*	*94*
			6.5-8.5	≥5	≤3		<2500	500

Note: Implementation of Polluted River Stretches Action Plan, presently the above six Rivers i.e., Kansi, Barakar, Rupnarayan, Teesta, Mayurakshi, Kaljani have been improved and is removed from the list. Therefore, Polluted River Stretches in West Bengal stands with 11 rivers.

O.A. 673/2018 for the month of FEB 2026

1. Details of each existing STP

No.	Location	Existing STP Capacity	Design Flow come as on 2026	Capacity Being Utilized	Percentage Utilization	Operational Status of STP	Compliance Status of STP
1.	Jagaddal Bhatpara New(FBAS)	31.00		13.47	=	Operation and Maintenance started since Sept.'2017, Sept.'2017, July'2018, July' 2018, July' 2018, July' 2018 and Sept.'2017 respectively. Operational status of all STPs are appraised to NMCG under O.A. 200/2014, which is sent quarterly and last report in this regard has been sent in September 2020 (Detail attached in **Annexure-II**).	O&M started with STP.
2	Jagaddal Bhatpara old (ASP)_	9.50		1.56			
3	Shyamnagar(WSP)	10.00		1.56			
4	Kankinara STP, Madrail, (FBAS)Bhatpara	10.00		4.08			
5	STP Kalyani-I	11.00		10.41 & 9.46			
6	STP Kalyani-II	10.00					
7	Gayeshpur	8.33		3.95			
8	Budge Budge	9.33		5.63		Operation and Maintenance started since	O&M started with STP.
9	Barrackpore	6 MLD & 18 MLD		3.02& 9.16		Overall physical progress achieved as on 31.03.24 is 99.99%. (O&M of STPs Started)	O&M started with STP.

						STP-100%, Network – 99.98%, Pumping Stations-100% Details of the work completed- STP-18 MLD - 100% STP-6 MLD- 100%	
10	Halisahar	16.0		8.28		Operation and Maintenance running.	STP Commisioned (09.03.2021)
11	Baidyabati	6.00		3.86		Operation and Maintenance running.	O & M will start from 01.08.2022
12	Bhadreswar	7.60		5.31		Operation and Maintenance running.	O & M will start from 01.08.2022
13	Chandannagar, Khalisani,	18.16		4.19 & 2.9		Operation and Maintenance running.	O & M started from 15.08.2022
14	Chandannagar, Khalisani,	4.50					
15	Bansberia	0.30	0.3	0.29		Operation and Maintenance running.	O & M going on since 01.06.2022.
16	Kanaipur	22.00		14.95		Operation and Maintenance running.	O&M started from 27/07/2022 Chlorination unit work was in progress. Required to operate MPS in controlled manner.
17	Nabadwip	9.50		3.69		Operation and Maintenance running.	O&M started from 01/07/2022
18	Naihati	11.56		9.32		Operation and Maintenance running.	(STP COMMISSIONED FROM 01.04.2022)

19	Titagarh	4.54		4.17		Operation and Maintenance running.	(STP COMMISSIONED FROM 01.06.2022)
20	Titagarh	4.54		4.17			(STP COMMISSIONED FROM 01.06.2022)
21	Bandipur (Khardaha)	14		11.42		Operation and Maintenance running.	(STP COMMISSIONED FROM 01.08.2022)
22	Champadani	1.00		0.00		DPR for Augmentation and up gradation of the STP is under process	Augmentation/upgradation
23	Garulia	4.10		3.2		Operation and Maintenance running.	(STP COMMISSIONED FROM 01.07.2022)
24	Naihati	6.50		5.24		Operation and Maintenance running.	(STP COMMISSIONED FROM 01.07.2022)
25	Panihati	12.00		9.86		Operation and Maintenance running.	(STP COMMISSIONED FROM 01.07.2022)
26	Serampore	18.60		0.00		DPR for Augmentation and up gradation of the STP is under process	Augmentation/upgradation
27	Sreenathpur, Ranaghat	4.0		1.61		Operation and Maintenance running.	
28	Silver Jubliee Road, Ranaghat	2.6		1.21		Operation and Maintenance running	
29	Chinsurah-Hooghly	26.50		4.45			
30	Maheshtala	35.00	35.0	25.47		Operation and Maintenance running	

						from 14.11.25	
30	Kanchrapara	18.00		6.88		Operation and Maintenance running from 06/03/2023	September 2022
31	Bangur (22.60561, 88.41498)	52		26		Operational	Complied
32	Garden Reach (22.52186, 88.28669)	57		53.68		Operational (Under Rejuvenation)	Complied
33	Keorapukur (22.46849, 88.33192)	45		36		Operational (Under Rejuvenation)	Complied
34	Baghajatin (22.48072, 88.39004)	15		14.25		Operational	Complied
35	Hatisur (22.51866, 88.39340)	10		8		Operational	Complied

2. <u>Details of under construction STPs</u>

No.	Location	Capacity of the plant in MLD	Physical Progress in %	Status of I&D or House sewer connections	Completion Timeline
1	Hooghly-Chinsurah	26.50	progress as on 27.02.2026 For Civil parts =90.80% , E&M Part= 97.00%		31.12.2025(applied)

			Overall progress =92.900% (Including E&M) 1) Sewrage network design as well as structral design completed and work going on. 2) Admin building Finishing work Completed. 3) 500 dia D.I pipe laying almost ompleted &Laying of 600 mm dia D.I pipe going on& gravity line going on. 4) MPS work Completed. 5) LS-3 work Completed 6) HDPE pipe line work in progress.		
2	Baharampore	3.50	Physical Progress of STP upto 31.12.2025 : 90%(Considering SBR Basin: Civil Work- 97.5.0% Completed. ii) MPS- 70% Completed iii) Centrifuse House- 92% Completed iv) Inlet Chamber- 98% Completed v) MCC Blower Room-95% Completed. vi) Chlorination Building: 85% Completed. vii) CCT - 90% Completed. vii) Boundary Wall- Civil work- 120m of 240m Completed		SEPTEMBER2025(applied)
3	Raghunathganj	5.00	AAs per proposed revised BOQ Construction of STP Physical progress- Civil Work 97% completed i) SBR Basin: Civil Work- 99% Completed. ii) Inlet Chamber: Civil Work- 99%Completed. iii)MCC- Blower Room: Civil Work-97% Completed. iv) Centrifuge House of STP: Civil Work-98% Completed.		SEPTEMBER 2025(applied)

			v) Chlorination Building : Civil Work-98% Completed. vi) CCT room: Civil Work-98% Completed. vii) MPS- 1no. Civil Work-98% viii) Boundary wall- 70%		
4	Jangipur	8.00	Jangipur: Construction of STP Physical progress- Civil Work 98.1%. Completed i) SBR Basin: SBR wall is under progress.-Civil-99.25% Completed. ii) Inlet Chamber: Civil- 98.6% Completed. iii)MCC- Blower Room: Civil Work-99% Completed. iv) Centrifuge House of STP: Civil work-99% Completed. v) Chlorination Building : Civil work-98% Completed. vi) CCT : Civil Work-98.1% Completed. vii) Boundary Wall- Civil work-70%		SEPTEMBER2025(applied)

5	Sreenathpur, Ranaghat	4	Commisioned and under Trial and Run w.e f. 19/07/2024		NA
6	Jiyanagar, Ranaghat	5.2	The construction of the proposed 5.20 MLD STP can be done only after the process of purchase of land is completed		NA
7	Silver Jubliee Road, Ranaghat	2.6	Commisioned and under Trial and Run w.e f. 19/07/2024 except 02(two) nos of UGLS Physical Progress100%		NA
8	Howrah-Arupara	65.00	Overall progress: 95.07% STP :99.86% Network: Manhole Rising 99% LS MPS Repair 98% Desilting 94% Pipe Laying 92%		JUNE 2026
9	Bally (Kona)-Kona, Chakpara (Anandanagar gram Panchayet)	62.00	Overall progress: 97.54% STP: 99.83% Network: Manhole Rising 98% LS MPS Repair 90% Desilting 97% Pipe Laying 97%Pipe Laying 98%		JUNE2026
10	Kamarhati - Baranagar - Kamarhati,	60.00	Overall progress: 96.10% STP : 99.91% Network: Manhole Rising 96%		JUNE 2026

	Mathkol, near Belgachia Metro Car Shed		LS MPS Repair 95% Desilting 98% Pipe Laying 94%		
11	South Dum Dum STP	27.0	Progress as on 31.12.2025 For Civil parts =1.60% , E&M Part=0.00% Overall progress =1.60% (Including E&M) 1)Soil Investigation of STP & MPS completed. 2)Structral design & drawing of STP completed . 3)Pile Foundation of SBR Basin is in progess(110nos pile out of 484nos pile of SBR basin conpleted)		Oct-27(Including completion of Trial Run)
12	Khardah House connection and STP	8.15	Overall progress: 10%		12.03.27
13	Sanragachi STP	1.5	Overall progress:%		11.09.25
14	Maheshtala	35.00	Total: -100% completed till 31-12-25 consisting of:- 1. 100% of STP Civil Process unit. 2. 100% of Office Building & Staff Quarter. 3. 100% of Supply of Electromechanical Items. 4. 100% of Associate Infra Civil Structure & pipe Laying works. SBR Basin:-Platform & wall 100% completed. Hydrotesting of Basin-1 ,2,3,4 completed.		

			CCT:- 100% completeed SHU:- 100% completed. PTU:- 100 % completed. Admin Building:- 100% completed Staff Quarter:- 100% Completed Pipelaying:- Pipe Laying , Hydrotesting & Road Restiration WIP. LS2- Some miscellaneous works are in progress like Boundary wall, plaster, paintings, cabling, Security room etc. LS-2A:- 100% Civil completed. LS-3:- 100% completed. Boundary Wall WIP.		
15	Bansberia	15.0KLD	Over all progress-60%		23.07.26
16	North Barrackpore (Babanpur STP)	30.0	Total:-99.92% completed till 28-02-2026 consisting of :- SBR Basin:- 100% completed. Primary Unit:- 100% completed. SHU:- 100% completed. STP Mechanical Procurements - 100% Completed. STP Electrical Procurements - 100% Completed. STP Mechanical Erection - 100% completed. STP Electrical Erection - 100% completed. ADMIN BUILDING: 100% completed. HT SUBSTATION : 100% completed. 700mm Dia having length of 110 metres (Trenchless /Open Cut Method) - 100% Completed.		15.03.26 (Including completion of Trial Run)

			Construction of New 11 MLD LS at D-Drain (Civil Part) - Roof Slab 100% complete. Gravity Sewarage & RCC Channel - Work In Progress.		
17	Chakdaha STP	15.0	Total:-91.90% completed till 28-02-2026 consisting of :- SBR Basin:- Basin wall and walkway 100% completed. Other miscellaneous works 100% Completed. E&M work Completed. Primary Unit:- Miscellaneous Work Completed. E&M work Completed. SHU:- Miscellaneous Work 100% Completed CCT:- Miscellaneous Work has been going on. Boundary Wall -: i) PCC Work - 95% Completed. ii)RCC Work - 93% Completed. iii) Brick Work & Plaster - 90%Completed Mechanical Procurements - 100% Completed. Electrical Procurements - 100% Completed. Mechanical Erecation - 99% Completed. Electrical Erecation -99% Completed. MPS-:Miscellaneous Work has been going on. LS-2 Wall 5th Lift Casting Completed & Sinking Work in Progress. . LS-3: MCC Panel Room Brick work, Plaster work , Painting work has been going on. Miscellaneous Work has been going on. LS-4: Miscellaneous works has been going on ADMIN BUILDING-: Miscellaneous works 100% Completed. Gravity Sewerage-		31.03.26(Including completion of Trial Run)

			89% Completed(6715M/5995M). Rising Main 98 % Completed(4900M/4310M).		
18	Near WBSETCL, Joka (22.4496,88.2982)	45	a. 68.6% b.Piling work for all units completed. Construction of super structure under progress.	The sewage network at the 03nos. STPs under KEIIP is being developed under respective works. Trunk sewers are being laid. S&D network to be completed by 2023. Approximately Rs. 1700cr. For S&D works. Out of this, about 1300 cr. linked for development of the trunk S&D system within the catchment areas of the 3 STPs and remaining indirectly linked for the abatement of pollution to the River Ganga in other areas. Out of 1300 cr. about **1113** cr. has been disbursed. Time line for balance work not within the present scope	DEC. 2024
19	At Bank Plot, M.G Road(22.4583, 88.3130)	40	a. 76.5 % b. Piling work for all units completed. Construction of super structure under progress.		DEC. 2024
20	Rajpur-Sonarpur, Rania (22.4492,88.3504)	23	a. 98.8% b. Piling work for all units completed. Super Structure of SBR completed. Installation of electro-mechanical is in progress		DEC, 2024

				including uncovered areas to be finalized based on the time frame of implementation of future loan or from own resources of KMC. (ward 127, 142, part of 125,126,143 &144) [Laying of trunk S&D lines including construction of pumping stations in ward 127, 142, part of 125,126,143 &144 are considered in new project under KURIP which will be funded by ADB. Considering the contribution of the aforesaid areas and areas under KEIIP, STPs are being constructed under ongoing KEIIP. Preparation of the DPRs & bid documents are in progress for the	

				same. Time frame for implementation of the said works can be finalized after signing of the loan with ADB. However, the said loan is expected to be signed with ADB by middle of 2024.]	

[FOR Sl No. 13-15(Annexure V _KMC)

3. Details of Proposed STPs

No.	Location	Capacity of the STP proposed in MLD	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
1	Bardhaman	50. 00	Revised estimate is under process	-
2	STP at North DumDum	33.00	AA&FS from Ring fenced account is under process of state fund.	-
3	**Jiaganj-Azimganj STP**		Setting up of Package STP at Azimganj. Municipality informs that the said land may be under Indian Railway. Proposal send to Land cell of KMDA for identification of the said land	-

No.	Location	Capacity of the STP proposed in MLD	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
4	STP at Baranagar	8.70	DPR shall be revised depending on the availabilty of solid land. for AA&FS from Ring fenced account is under process of state fund.	-
5	Katwa STP	11.0	DPR is submitted to NMCG. Compliance of Third party observation completed. Awaiting from AA&ES from NMCG.	
6	Katwa STP	2.5	DPR is submitted to NMCG. Compliance of Third party observation completed. Awaiting from AA&ES from NMCG.	
7	Santipur STP	18.1	DPR has been submitted to WBSPMG/NMCG on 04.04.25.Initial observation of WBSPMG is being complited.	
8	**Diamond Harbour STP**		DPR under preparation.	
9	Mursidabad STP	4.0	DPR is submitted to NMCG. Third party visit had also been done and they had given some observation. Awaiting from AA&ES from NMCG.	
10	**Dhuliyan STP**		DPR preparation on hold due to non-availability of land from ULB. A proposal for providing 0.78 acres land has been send to Dhulian Municipality. The land handing over is awaited	

No.	Location	Capacity of the STP proposed in MLD	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
11	**Uluberia (STP &FSTP)**		Tender 2nd Call under process	
12	**Asansol Durgapur (STP &FSTP)**		Due to unavailable of Land AA&ES has been withdrawn by NMCG. However on the basis of available land KMDA will submit revised DPR within February,2025	
13	**Kalyani STP**		DPR has been sent to PCC (Finance) for vetting.	
14	**Bansberia FSTP**		Tender is under process.	
15	**Uttarpara_ Kotrung FSTP**		Approval awaited from NMCG.	
16	Bansdroni STP	11.6	Revised AA&ES approved in the 46th EC Meeting held on 23/12/2022, Agenda Item No. 46.01. Estimated amount of Rs 653.72 Crores (including cost of O & M for 15 years -Rs 211.53 Crores) under DBOT mode. Tendering done on 29.08.2023. Tender opening date extended upto 10.01.2024.	30 Months from the date of issuance of Work Order
17	STP Near Golf Garden, Sukhapukur (22.49851, 88.35096)	3.5		

No.	Location	Capacity of the STP proposed in MLD	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
18	Birji Road STP near SahidKhudiram Metro (22.46576, 88.38884)	10	Tender opened. Tech. bid under evaluation process.	30 Months from the date of issuance of Work Order
19	New STP at Garden Reach	65	AA&ES approved in the 44th EC Meeting held on 17/08/2022, Agenda Item No. 44.18. Estimated amount of Rs 289.02 Crores (including cost of O & M for 15 years -Rs 149.11 Crores) under HAM mode. Tendering Completed. Letter of Award (LoA) issued. Formal WO to be issued in due course.	24 months + 15years
20	Additional capacity at existing Keorapukur STP	5	AA&ES approved in the 45th EC Meeting held on 30/09/2022, Agenda Item No. 45.3. "DPR for Rehabilitation of existing 50 MLD STP at Keorapukur and other allied works at Kolkata, West Bengal" EC approved the proposal at an estimated amount of Rs 67.06 Cr. (including cost of O & M for 15 years – Rs 38.99 Cr.) under DBOT mode. Tendering under progress Tender Publish date: 28/03/2023, Bid opening extended up to date: 14/09/2023. Since, after opening of technical bid, it has been found that, Single Bidder has participated in the said tender, NMCG has directed to go for 2nd time e-tender.	24 months + 15years

No.	Location	Capacity of the STP proposed in MLD	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
			After incorporating the observation points as obtained during 2nd time pre-tender meeting, the revised DPR of Keorapukur STP has been submitted to WBSPMG via. Official mail dated-30.05.24 & the same has been forwarded to Director General of NMCG by Program Director of WBSPMG vide memo no.- 5792-NGRBA/SPMG/DPR-178/2015(P-I)/2019 Dt.-03.06.24. for necessary approval and getting revised AE&FS for the same.	
21	STP Near SurinaamGhat, DhankhetiNikashi (22.55041, 88.29222)	25	Sent to 15th Finance Commission , Tripartite MOU signed.	52months from the date of issuance of work order.
22	STP Near BhangaKhal, Gardenreach area (22.54118, 88.25155)	35	Sent to 15th Finance Commission , Tripartite MOU already signed. Formal Approval of authority has been obtained for tendering.Under process of tendering	
23	New Baghajatin STP	26	Sent to 15th Finance Commission,, Tripartite MOU already signed. Preparation of NIT etc. under process.	NA
24	New Keorapukur STP	25	Sent to 15th Finance Commission , Tripartite MOU signed.	NA

No.	Location	Capacity of the STP proposed in MLD	Status of Project (at DPR Stage/ Under Tendering/ Work to be Awarded)	Likely Date of Completion
25	Strand Road STP	23	Sent to 15th Finance Commission , Tripartite MOU already signed. The land area is under KOPT. The requision for land allotment for STP has been send to KOPT(Kolkata Port Trust). Land allotment is pending.	NA

[FOR Sl No. 7-17(Annexure V _KMC)]

4. <u>Drain details:</u>

River name	No. of drains falling in the river	No. of drains having floating racks/screens installed to prevent solid waste from falling into the river
GANGA	56 nos.	There are 35 drains which are already under I&D proposals for treatment in STPS **(Detail enclosed as Annexure-III)** The detail of action for 21 nos of drain are enclosed as **Annexure-IV**
Ganga	DhankhetiKhal	1*
	Tolly'sNullah	1#
	Nimtala Burning Ghat Drain	0

River name	No. of drains falling in the river	No. of drains having floating racks/screens installed to prevent solid waste from falling into the river
	Cossipore Ghat Drain	0
	Chitpur Ghat Khal/ Circular Canal	0

*****DhankhetiKhal is guarded with 3bar screens at different locations to arrest the floating materials for the ease of removing the same from reaching to the River.

Tolly'sNullah is guarded with 8 floating garbage arrester nets at different locations to arrest the floating materials for the ease of removing the same from reaching to the River.

(**Annexure V _KMC)**

5. <u>Alternate treatment details:</u>

River name	Polluting drain	In-situ treatment details	MLD treated	Details of parameters before treatment	Details of parameters after treatment
Ganga	Jangipur	Bio/Phyto remediation treatment process as interim measure has been taken up for Jangipur drain. Chemical dosing, desilting work etc. has been taken up periodically and as per the test result data it is expected, the desired test result for waste water may be achieved with the present treatment process.	0.2	**1st Test (Dated – 08.09.2020)** DO: NA BOD: 158mg/L TC:NA FC:260 MPN/100 ml TSS : 240 mg/L	**1st Test (Dated – 08.09.2020)** DO: NA BOD:99 mg/L TC:NA FC:220 MPN/100 ml TSS : 177 mg/L

River name	Polluting drain	In-situ treatment details	MLD treated	Details of parameters before treatment	Details of parameters after treatment
				2ndTest (Dated – 28.09.2020) DO: NA BOD: 27 mg/L TC: NA FC:5800 MPN/100 ml TSS : 105 mg/L	**2nd Test (Dated – 28.09.2020)** DO: NA BOD: 16 mg/L TC: NA FC:3900 MPN/100 ml TSS : 54 mg/L
Churni	Basko Canal	Bio/Phyto remediation treatment process as interim measure was taken up for Basko Canal but due disposal of sewage by some other drains and local habitants at down most point of the drain the required effluent quality did not achieve.	4.28	NA	
	Sreenathpur Drain	Bio/Phyto remediation treatment process as interim measure taken up for Sreenathpur Drain. Chemical dosing, desilting etc. has been taken up periodically and as per the test result data it is apprehended the desired test result for waste water may be achieved with the present treatment process.	2.79	**1st Test on (Dated 28.09.20)** DO: NA BOD: 12 mg/L TC: NA FC:2400 MPN/100 ml COD: 46 mg/L **2nd Test on Dated 18.02.2021** Total Coliform: $68x10^2$	**1st Test (Dated 28.09.20)** DO: NA BOD: 2 mg/L TC: NA FC:1100 MPN/100 ml COD: 10 mg/L **2nd Test on Dated 18.02.2021** Total Coliform: $16x10^2$ Fecal Coliform: $9x10^2$ COD : 23 mg/l BOD: 11 mg/l

River name	Polluting drain	In-situ treatment details	MLD treated	Details of parameters before treatment	Details of parameters after treatment
				Fecal Coliform: $35x10^2$ COD : 67 mg/l BOD: 32 mg/l	

6. Reuse of treated water

Location of STP/Alternate Treatment	MLD of treated water generated	Details of the reused water
Kalyani Municipal area	Trickling Filter- 11.00 MLD WSP- 10.00 MLD	About 2 MLD water coming from Storage pond 1 and it will use in various block of Bidhan Chandra Krishi Vidyalaya (BCKV) and Picnic Garden. Total consumption of BCKV and Picnic Garden is 1.6 MLD. Municipality has been requested to explore measures such that the treated water can be collected through tanker and used for gardening, car washing etc. for which tentative cost is to be submitted by the ULB.
Treatment through East Kolkata Wetland	NA 910MLD of raw sewage is reused	The majority of the sewage from the core inner city area - about 910 MLD in magnitude receives natural treatment as it passes through the East Kolkata Wetlands - an extensive fishery to the East of the city before discharging the same to Kulti River.

7. Ground water regulation

River	Ground water regulation details
GANGA	**Groundwater Regulation** Ground Water Regulation is already in practice and is dealt by State Water & Investigation Directorate (SWID) for the entire state under Water Resources Investigation & Development Department (WRI&DD). Assessment of ground water resource at KMC area is checked periodically by State Water & Investigation Directorate (SWID). For extraction of ground water, case to case basis application is obtained by SWID and merit of such application is judged by an expert committee as per The West Bengal Ground Water Resources (Management, Control and Regulation) Act, 2005 which is called Corporation Level Authority (CLA) comprising of the following members: i) The Municipal Commissioner of the Corporation : Chairman ii) The Chief Executive Officer, Kolkata Metropolitan Development Authority : Member iii) Superintendent Geologist, State Water & Investigation Directorate, Government of West Bengal: Member Secretary. iv) Two elected representatives of the Kolkata Municipal Corporation, to be nominated by the Mayor, Kolkata Municipal Corporation : Members v) One expert from the Central Ground Water Board as may be nominated by the Regional Director, Central Ground Water Board : Member vi) Two experts in the field of conservation, protection or development of ground water resources as the State Government may, by notification appoint. : Members vii) Two eminent persons of the locality as the State Government may, by notification appoint. : Member viii) One representative of the Public Health Engineering Directorate, Government of West Bengal : Member ix) One representative of the State Pollution Control Board : Member Only on recommendation of such committee and subsequent permission from State Water & Investigation Directorate (SWID) ground water extraction is allowed. After completion of these formalities KMC issues license for tube well boring. The above procedure is being maintained as a continuous process.

	(Annexure _ V_KMC) The West Bengal Groundwater Resources (Management Control and Regulation), Act, 2005 was enacted in the state since 15th September 2005 and Rules thereof was finalized and came into force with effect from 1st August 2006, for proper utilization of ground water resources through effective management, control and regulation in the state. The State Water Investigation Directorate (SWID) under WRIDD acts as the functional organ. The act stipulates obtaining mandatory permit for installation of ground water extraction structures operated by engine or motor driven pump is present against payment of prescribed fees. 3(three) different tiers of Authorities as provided in the Act are established by the Government in the Water Resources Investigation & Development Department. These authorities are 1. District Level Ground Water Resources Development Authority (DLA), 1 (one) for each of the 22 (twenty two) districts of the State, 2. Corporation Level Ground Water Resources Development Authority (CLA) at Kolkata for the Kolkata Municipal Corporation Area, 3. State Level Ground Water Resources Development Authority (SLA) at Kolkata which acts as the apex body of all the District Level Authorities and the Corporation Level Authority and For the industrial purpose of groundwater use, the High Level Ground Water Resources Development Authority (HLA) for those applications for sinking of well for extraction or use of ground water at the rate exceeding 100 cubic metre per hour. G**roundwater Monitoring** • GW Level database for Jan'22, April'22, Aug'22, Nov`22 & Jan`23 against 136 GW monitoring stations under the blocks along polluted stretch of River Ganga has been validated & GWL data for the month of April`23 has been generated.

	GW Monitoring Stations (136) = 92 (Manual) + 44 (Real-Time) • 2. Physio- Chemical test of GW samples for the month of April'23 are generated.
CHURNI	**Groundwater Regulation** Groundwater extraction is regulated according to West Bengal Ground Water Resources (Management, Control and Regulation) Act, 2005. 1. Installation of Water Meter without telemetry system at industrial Tube Wells for monitoring of real-time GW withdrawal is in progress. 2. Groundwater Resources Estimation and Assessment is done as per GEC'2015 guidelines. 3. Implementation of Real-Time GW Level monitoring system is in progress. **Groundwater Monitoring** 1. GW Level database for Jan'22, April'22, Aug'22, Nov`22 & Jan`23 against 52 GW monitoring stations under the blocks along polluted stretch of River Churni has been validated & GWL data for the month of April`23 has been generated. GW Monitoring Stations (52) = 42 (Manual) + 10 (Real-Time) • 2. Physio- Chemical tests of GW samples for the month of April'23 are generated.

8. Good irrigation practices

River	Details of adopting good irrigation practices						
Ganga	District	Block	Total Beneficiary Regd.	Coverage Area (Ha.)	Budgetary Estimate (Rs.)	Expenditure (Rs.)	Works Completed (Rs.)
	Hooghly	Chinsurah-Magra	64	4.46	1717526.15	0	0
	Howrah	Bagnan-I	74	3.24	1547657.2	84329.1	843633.24
		Bagnan-II	43	4.00	925014.6	71874	261360
		Uluberia-I	5	0.43	75963.25	0	73945.3
	South 24-Parganas	Budge Budge-I	17	0.76	354610.55	0	101640
		Budge Budge-II	9	1.33	146367.4	0	0
	North 24-Parganas	Barrackpur-II	47	2.17	839290.7	0	0
Total			259	16.39	5606429.9	156203.1	1280578.5
Churni	Nadia	Ranaghat-I	60	6.33	2162716.45	0	0
		Hanskhali	90	28.22	2596709.9	0	1503350
		Shantipur	36	25.27	1173899	0	491763
Total			186	59.82	5933325.4	0	1995113

9. Rain water harvesting

River	Details of rain water harvesting
GANGA	Rain Water Harvesting in already incorporated in Building Rule 2009 which is as follows: Rule-144 Rain Water Harvesting and Tree Cover Rain Water Harvesting (RWH), RWH shall

	form a part the building and shall have to be included in the plan, either for direct use of the rain water or for ground water recharging or both, in case of (i) New building or buildings or any housing complex as per Environment Impact Assessment Guideline issued by State Government/ Government of India. (ii) Expansion of any existing building or buildings or housing complex, as per Environment Impact Assessment Guideline issued by State Government/ Government of India. This system shall comply with Central & State statutory requirements laid down in the relevant Acts & by-laws. It is implemented for the buildings on area exceeding 20,000Sqm **(Annexure_V_KMC)** The nos. of Roof Top Rain Water Harvesting and artificial recharge to ground water and / or re-use schemes implemented by the State Water Investigation Directorate (SWID) in the Districts of Malda is 18, Murshidabad is 3, Purba Burdwan is 11, Nadia is 25, Hooghly is 13, North 24 Parganas District is 11, Howrah is 6, Kolkata is 13, South 24 Parganas is 8 and Purba Medinipur is 15.
CHURNI	1. Hanskhali- 5 nos.

10. **Demarcation of Floodplain and removal of illegal encroachments**

River	**Details of demarcation of floodplain and removal of illegal encroachments**
CHURNI	
GANGA	

11. Maintaining minimum e-flow of river

River	**Maintaining minimum e-flow of the river**
CHURNI	
GANGA	

12. Plantation activities

River	Details of plantation activities along the river
GANGA Vidyadhari	Total Plantation made during: 2020-21, 2021-22 = 28,000nos. February 2024 Road side plantation - NIL Shrubs inside green verge- 4255 Cumulative Figure Road side plantation- 70618 Shrubs inside green verge- 163235 **(Anneuxure_V_KMC)** **24 Pargana North :** Advance (Nursury work) 100% completed in March 2021. 1st year maintenance work done over 6 Ha. Institutional plants and 3 km Avenue plantation. **Nadia / Mursidabad** 1st year maintenance work over 2 Ha is going on under Namami Gange Project. **(Anneuxure_VI_WBSFDA)**
CHURNI	Advance (Nursury work) 100% completed Creation work 100% completed during 2021-22 2ND year maintenance work is going on for 7.265 Ha(One side) **(Anneuxure_V_WBSFDA)**

13. <u>Development of biodiversity park</u>

River	Details of setting up biodiversity parks on flood plains by removing encroachment along the river
Ganga & Churni	Details of setting up biodiversity parks on flood plains by removing encroachment along the river 1. Dr. AnupamaMitra, Expert Member of the Committee of the West Bengal Bio-Diversity Board has been engaged vide letter dated 07/11/2022 and same has been communicated through Affidavit to HNGT in the matter of OA-20/2022/EZ. 2. For availability of land KMC has approached to Army Authority, Eastern Railway and SMP-Kolkata for identification of land for setting up of Bio-diversity park. 3. SMP-Kolkata has informed that there is no availability of land and the same has been communicated through Affidavit in the matter of OA-20/2022/EZ of HNGT. Army Authority had informed that NoC will be issued for the purpose as and when land is identified. 4. A Model DPR regarding setting up of Bio-Diversity Park has been obtained by KMC from West Bengal Bio-Diversity Board. **(Anneuxure_V_KMC)**
